



City of Chico

Salem Street Bridge Replacement Project

Volume 3

September 3, 2025

Salem Street Bridge Replacement Project

Monthly Update

Introduction

The following is the latest in a series of monthly electronic updates that City staff provides to property owners, businesses, interested organizations, and other stakeholders adjacent to the project. These updates will continue throughout the 2025 construction season to share detailed information regarding the progress of the Salem Street Bridge Replacement Project. If you do not wish to receive these updates, you may opt-out by sending a quick email with that instruction. Alternatively, if you know of others interested in being added to the list, please have them visit the project webpage to sign up to receive regular project updates. [City of Chico – Salem Street Bridge Replacement Project.](#)


Project Status



During the month of August, construction on the north and south bridge abutments was completed, opening the door for the contractor to begin construction of the temporary false work required to pour the concrete bridge deck. Prior to construction of false work, however, the contractor removed the temporary stream diversion and re-graded the stream channel and installed Rock Slope Protection (RSP) along both stream banks.

Planned Work

Planned activities for the month of September include construction of the temporary false work and placement of concrete for the new bridge deck. Once the bridge deck has been poured and allowed time to cure, the false work will be removed and final grading of the creek channel will be performed so that all construction activity within the stream channel is complete by the permit deadline of October 31, 2025.

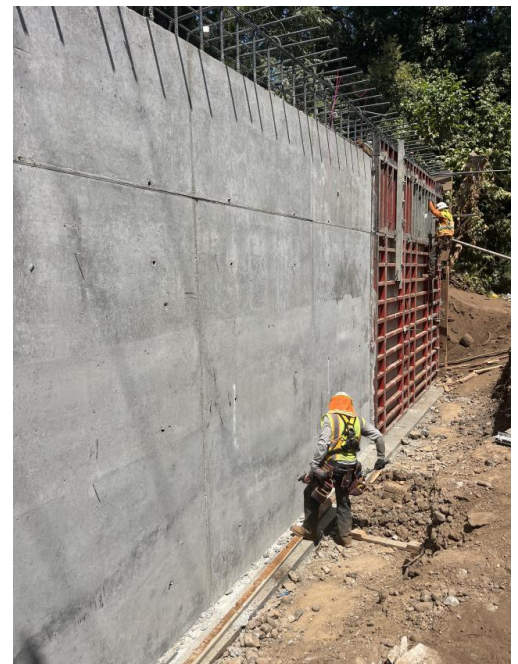



Contact Information

For any questions or concerns, please contact the Capital Project Services Department at 879-6900 or Police Dispatch for immediate assistance from 5 PM to 8 AM at 895-4911. For design questions, you can reach Ryan Morris or Felicia McDowell, Senior Civil Engineer, at 879-6930. For construction issues, contact Justin Seufert, Resident Engineer, at 863-2545. The contractor, Franklin Construction, Inc., can be reached 24-hours a day at 343.9600.

We appreciate your patience and cooperation as we work diligently to complete these critical infrastructure improvements.

- ✓ Remain alert for changing conditions, construction workers and large equipment moving into and out of the construction site.
- ✓ Obey all construction signs and avoid entering the construction site, this includes on weekends.
- ✓ With school back in session, be aware of increased pedestrian traffic and congestion around the construction site.

CONTACT PHONE NUMBERS (Area Code – 530)

Capital Project Services Department	879-6900
Police Dispatch (use this number for immediate assistance from 5PM - 8AM)	895-4911

Design Questions

Felicia McDowell, Senior Civil Engineer	879-6930
Ryan Morris, Project Manager	

Construction Issues

Justin Seufert, Resident Engineer	863-2545
-----------------------------------	----------

Franklin Construction, Inc. (Contractor)

Myles MacColl (Project Manager)	343.9600
---------------------------------	----------

The City appreciates your patience and understanding during the project. Please feel free to contact City staff or the contractor should you need additional information. The Contractor will notify businesses at least 2 weeks prior to the commencement of any construction activities that occur directly in front of their property. For more information, please refer to the City Capital Project webpage at [City of Chico – Salem Street Bridge Replacement Project](#).
