

SIX-MONTH SURVEILLANCE AHERA REPORT

**SIERRAMONT MIDDLE SCHOOL
3155 KIMLEE DRIVE
SAN JOSE, CA 95132**

**PREPARED FOR:
BERRYESSA UNION ELEMENTARY SCHOOL DISTRICT
981 RIDDER PARK DRIVE
SAN JOSE, CA 95131**

**INSPECTED ON:
SEPTEMBER 17, 2025**

HAZMAT DOC PROJECT #25-101

**PREPARED BY:
HAZMAT DOC
3080 OLCOTT STREET • SUITE D135
SANTA CLARA, CA 95054
Tel: 408.748.0055**

BERRYESSA UNION ELEMENTARY SCHOOL DISTRICT
SIERRAMONT MIDDLE SCHOOL

INSPECTED ON:
SEPTEMBER 17, 2025

INSPECTED BY:



Leland Kafeyan
Cal/OSHA Certified Site Surveillance Technician
Certification Number 06-4110

REPORTED BY:



Maheen B. Doctor
Cal/OSHA Certified Asbestos Consultant
Certification Number 95-1798

CONTENTS

PART - I

LEGEND AND GLOSSARY OF TERMS

PART – II

AHERA REPORT A – LIST OF BUILDINGS

PART – III

AHERA REPORT B – SURVEY REPORT

PART – IV

HOMOGENEOUS MATERIALS REPORT

PART – V

FRIABLE LOCATIONS REPORT

PART – VI

NON-FRIABLE LOCATIONS REPORT

PART – VII

RECOMMENDATIONS REPORT

PART – VIII

SAMPLES REPORT

PART – IX

DAMAGE REPORT

PART - X

SITE MAPS

LEGEND

THE FOLLOWING IS A LIST OF ABBREVIATIONS USED IN THIS REPORT:

Asbestos Sample Types

AC	=	ACTINOLITE
AM	=	AMOSITE
AN	=	ANTHOPHYLLITE
CH	=	CHRYBOTILE
CR	=	CROCIDOLITE
TR	=	TREMOLITE
ND	=	NONE DETECTED
NS	=	NO SAMPLE

Measurements

APPROX.	=	APPROXIMATELY
EA	=	EACH
I	=	INCHES
LF	=	LINEAR FEET
N	=	NUMBER
O.D.	=	OUTSIDE DIAMETER
SF	=	SQUARE FEET
TBD	=	TO BE DETERMINED

LIST OF BUILDINGS AT

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME	BUILDING USED AS (#FLOORS) CONSTRUCTION	BUILDING AREA (APPROXIMATE)
BOILER ROOM		
Boiler Room		1,530 SF
(1)	Concrete Slab and Plaster Walls	
CLASSROOM 40 PORTABLE BUILDING		
Classroom		960 SF
(1)	Wood, Metal, and Pre-formed Walls	
CLASSROOM 41 PORTABLE BUILDING		
Classroom		960 SF
(1)	Wood and Metal Portable	
CLASSROOM 42 PORTABLE BUILDING		
Classroom		960 SF
(1)	Wood and Metal Portable	
CLASSROOM 45 PORTABLE BUILDING		
Classroom		960 SF
(1)	Wood and Metal	
CLASSROOM 46 PORTABLE BUILDING		
Classroom		960 SF
(1)	Wood and Metal	
MAIN BUILDING		
Offices, Classrooms, Library, Storage Rooms, Restrooms, Utility Rooms		36,600 SF
(1)	Wood, Metal, Plaster, Gypsum Wallboard System, Concrete	
METAL STORAGE CONTAINERS (4 EA)		
Storage		1,420 SF
(1)	Metal	
MULTI-PURPOSE BUILDING		
Gym, Classrooms, Locker Rooms		25,600 SF
(1)	Wood, Metal, Plaster, Gypsum Wallboard System, Concrete	
Total Number Of Buildings : 9		(Approximate) Total Sq Ft. : 69,950
End Of Report, Total Of 1 Pages		

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

COMMENTS

QTY (APPROXIMATE)

SAMPLE NO.

ASBESTOS CONTENT

ASBESTOS NAME

ASBESTOS CODE

BOILER ROOM

BOILER ROOM

BOILER ROOM

ROUGH WALL

1,800 SF

09/12/2005 Stucco Exterior Walls. This Material is in GOOD condition as of this date.

02/03/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-21AAA

ASSUMED

NO SAMPLE

(NS)

BOILER ROOM

BOILER ROOM

ROUGH WALL SURFACING

1,800 SF

09/12/2005 Skim Coat for Stucco Exterior Walls. This Material is in GOOD condition as of this date.

02/03/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

SF= Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		
05-212AAA	ASSUMED	NO SAMPLE	(NS)

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

COMMENTS

QTY (APPROXIMATE)

SAMPLE NO.

ASBESTOS CONTENT

ASBESTOS NAME

ASBESTOS CODE

CLASSROOM 40 PORTABLE BUILDING

CLASSROOM 40 PORTABLE BUILDING

03/06/2007 BUILDING NOTES:

03/06/2007 Manufacturer's Tag Info:
By: American Modular Systems; Date 10-06; Serial #s 06-222-011A & B.
This entry for informational and tracking purposes.

10/16/2008 Building Name changed from CLASSROOM 42 PORTABLE BUILDING to CLASSROOM 40 PORTABLE BUILDING.

CLASSROOM 40 PORTABLE BUILDING

PORTABLE 40

PORTABLE BUILDING

960 SF

03/06/2007 New 2006 Construction Relocatable Building per Manufacturer's Tag information.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212.NS

NEW

NO SAMPLE

(NS)

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

CLASSROOM 41 PORTABLE BUILDING

CLASSROOM 41 PORTABLE BUILDING

09/12/2005 BUILDING NOTES:

09/12/2005 Manufacturer's Tag Info:
BY DESIGNED MOBILE SYSTEM; DATE: 03/91; OSA# 55824; SERIAL# 2632-1, 2632-2.
This entry for informational and tracking purposes.

10/16/2008 Building Name changed from CLASSROOM 40 PORTABLE BUILDING to CLASSROOM 41 PORTABLE BUILDING.

CLASSROOM 41 PORTABLE BUILDING

PORTABLE 41

PORTABLE BUILDING

960 SF

09/12/2005 New 1991 Construction Relocatable Building per Manufacturer's Tag information.

02/03/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212.NS	NEW	NO SAMPLE	(NS)
-----------	-----	-----------	--------

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

CLASSROOM 42 PORTABLE BUILDING

CLASSROOM 42 PORTABLE BUILDING

09/12/2005 BUILDING NOTES:

09/12/2005 Manufacturer's Tag Info:
BY AMERICAN MODULAR SYS; DATE: 05/99; SERIAL# 99-R320-657A, 99-R320-657B.
This entry for informational and tracking purposes.

10/16/2008 Building Name changed from CLASSROOM 41 PORTABLE BUILDING to CLASSROOM 42 PORTABLE BUILDING.

CLASSROOM 42 PORTABLE BUILDING

PORTABLE 42

PORTABLE BUILDING

960 SF

09/12/2005 New 1999 Construction Relocatable building per Manufacturer's Tag information.

02/03/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212.NS	NEW	NO SAMPLE	(NS)
-----------	-----	-----------	--------

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

CLASSROOM 45 PORTABLE BUILDING

CLASSROOM 45 PORTABLE BUILDING

03/07/2017 BUILDING INFORMATION:

03/07/2017 Manufacturer's Tag Info:
By American Modular Systems; Date 06-12; DSA # 01-112697; Serial #'s 12-825-002A, 12-825-002B.
This entry for informational and tracking purposes.

CLASSROOM 45 PORTABLE BUILDING

PORTABLE 45

PORTABLE BUILDING

960 SF

10/11/2012 New 2012 Construction Relocatable Building per Manufacturer's Tag information.

02/03/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

12-185.NS	NEW	NO SAMPLE	(NS)
-----------	-----	-----------	--------

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

CLASSROOM 46 PORTABLE BUILDING

CLASSROOM 46 PORTABLE BUILDING

03/07/2017 BUILDING INFORMATION:

03/07/2017 Manufacturer's Tag Info:
By American Modular Systems; Date 03-99; Serial #'s 99-R-320-655A, 94-R-320-655B.
This entry for informational and tracking purposes.

CLASSROOM 46 PORTABLE BUILDING

CLASSROOM 46

PORTABLE BUILDING

960 SF

10/11/2012 New 1999 Construction Relocatable Building per Manufacturer's Tag information.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

12-185.NS	NEW	NO SAMPLE	(NS)
-----------	-----	-----------	--------

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

MAIN BUILDING

MAIN BUILDING

09/12/2005	BUILDING NOTES:
09/12/2005	Existing Gypsum Wallboard Systems Removed and Replaced with new in-kind in Path-of-Construction. Existing Plaster Systems Removed and Replaced with new in-kind in Path-of-Construction. New Flooring Finishes per information received from the BUESD. New Suspended Ceiling Tiles installed.
10/16/2008	New Ceramic Wall and Floor Tiles installed in all Student and Staff Restrooms, and Nurse's Restroom per information received from BUESD.
08/31/2010	New Sinks with Thermal Undercoating installed in Staff Lounge Room, Staff Work Room, 1 EA in each Pod Entry (6 Pods), Classrooms 21, 26, 27, 29, and Storage.
09/13/2016	New Flooring Finishes installed Summer 2016 per information received from the BUESD. New Suspended Ceiling Tiles installed. Existing Gypsum Wallboard Systems Removed and Replaced with new in-kind in Path-of-Construction.

MAIN BUILDING

ALL ADMIN OFFICES, UTILITY ROOMS, STORAGE ROOMS, CUSTODIAL ROOM, CLASSROOMS 24, 26, 28, 29, DARK ROOM, COMPUTER CLERK ROOM, AND PREP ROOMS

FIRE DOOR CORE INSULATION

693 SF

09/12/2005	Fire Door Core Insulation. (33 EA Doors). This Material is in GOOD condition as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MAIN BUILDING

ALL CLASSROOMS, LOUNGE, AND PREP AREAS

PRESSED WOOD WALL PANEL

14,630 SF

03/06/2007 4'x10' Pressed Wood Wall Panel with Vinyl Wall Cover, (over Gypsum Wallboard System). This Material is in GOOD condition as of this date.

02/03/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 Additional Damage Observed. 1 SF of Missing Vinyl Wall Cover at Entry into Pod 2 by Baseboard. No other changes as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MAIN BUILDING

ALL CLASSROOMS, LOUNGE, AND PREP AREAS

PRESSED WOOD WALL PANEL MASTIC

14,630 SF

03/06/2007 Mastic/Adhesive for 4'x10' Pressed Wood Wall Panel with Vinyl Wall Cover, (over Gypsum Wallboard System). This Material is in GOOD condition as of this date.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
02/03/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	Additional Damage Observed. 1 SF of Missing Vinyl Wall Cover at Entry into Pod 2 by Baseboard. No other changes as of this date.		
09/17/2025	This Material is unchanged as of this date.		
05-212AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

ALL CLASSROOMS, LOUNGE, AND PREP AREAS

VINYL WALL COVER MASTIC

14,630 SF

09/12/2005	Mastiv/Adhesive for Vinyl Covering on 4'x10' Vinyl Covered Pressed Wood Walls. This Material is in GOOD condition as of this date.		
02/03/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 Additional Damage Observed. 1 SF of Missing Vinyl Wall Cover at Entry into Pod 2 by Baseboard. No other changes as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MAIN BUILDING

ATTIC / PLENUM

DUCT WRAP TAPE

1,000 LF

09/12/2005 Duct Wrap Tape. This Material is in GOOD condition as of this date.

02/03/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

MAIN BUILDING

CLASSROOM 27 STORAGE ROOM

KILN BRICK

60 SF

03/22/2016 Kiln Brick Insulation. (1 EA Unit). This Material is in GOOD condition as of this date.

02/03/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

16-074AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MAIN BUILDING

ENTIRE BUILDING

SMOOTH WALL MISCELLANEOUS

76,000 SF

09/12/2005 Gypsum Wallboard System, (under 4'x10' Pressed Wood Wall Panel with Vinyl Wall Cover in some areas). Existing Gypsum Wallboard Systems Removed and Replaced with new in-kind in Path-of-Construction. This Material is in GOOD condition as of this date.

01/29/2016 Sample 16-031-019 collected from Corridor 18C, Gypsum Board. Sample 16-031-020 collected from Corridor 18C, Joint Compound for Drywall Board. Sample 16-031-023 collected from Custodian #7, Gypsum Board. Sample 16-031-024 collected from Custodian #7, Joint Compound for Drywall Board. Sample 16-031-026 collected from Corridor 6, Drywall Board. Sample 16-031-027 Corridor 6, Joint Compound for Drywall.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
02/08/2016	Sample 16-031-053 collected from Main Lobby by Drinking Fountain, Wallboard. Sample 16-031-055 collected from Main Lobby by Drinking Fountain, Joint Compound on Wallboard.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	Damage Observed. <5% Physical Damage - in the form of 1 SF of Missing Scratch-Skim Coat around Whiteboards in Room 3A. Material condition changed from GOOD to FAIR overall. Friability changed from Non-Friable to Friable. No other changes as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

16-031-019	ND	NONE DETECTED	(ND)
16-031-020	ND	NONE DETECTED	(ND)
16-031-023	ND	NONE DETECTED	(ND)
16-031-024	ND	NONE DETECTED	(ND)
16-031-026	ND	NONE DETECTED	(ND)
16-031-027	2%	CHRYSTILE	(CH)
16-031-053	ND	NONE DETECTED	(ND)
16-031-055	ND	NONE DETECTED	(ND)
05-212AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

ENTIRE BUILDING

SMOOTH WALL SURFACING

76,000 SF

08/24/2006 Skim Coat for Gypsum Wallboard System, (under 4'x10' Pressed Wood Wall Panel with Vinyl Wall Cover in some areas). Existing Gypsum Wallboard Systems Removed and Replaced with new in-kind in Path-of-Construction. This Material is in GOOD condition as of this date.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
01/29/2016	Sample 16-031-021 collected from Corridor 18C, Skim Coat and Paint for Gypsum Board. Sample 16-031-025 collected from Custodian #7, Skim Coat and Paint for Gypsum Board. Sample 16-031-028 collected from Corridor 6, Skim Coat and Paint for Drywall Board.		
02/08/2016	Sample 16-031-054 collected from Main Lobby by Drinking Fountain, Skim Coat on Wallboard.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	Damage Observed. <5% Physical Damage - in the form of 1 SF of Missing and Scratch-Skim Coat around Whiteboards in Room 3A. Material condition changed from GOOD to FAIR overall. Friability changed from Non-Friable to Friable. No other changes as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

16-031-021	ND	NONE DETECTED	(ND)
16-031-021	<1	CHRYSTILE	(CH)
16-031-025	ND	NONE DETECTED	(ND)
16-031-028	ND	NONE DETECTED	(ND)
16-031-028	2%	CHRYSTILE	(CH)
16-031-054	ND	NONE DETECTED	(ND)
06-223AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

ENTRY FOYERS AND CLASSROOM WINDOWS

CEMENTITIOUS WINDOW PANEL

286 SF

09/12/2005 Cementitious Window Panels. This Material is in GOOD condition as of this date.

02/03/2020 This Material is unchanged as of this date.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		
05-212AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

HALLWAY, MEDIA CENTER, NORTH OFFICE, AND MAIN OFFICE

CEILING TILE

6,000 SF

09/12/2005	1'x1' Ceiling Tile. This Material is in GOOD condition as of this date.		
03/06/2007	Damage: <5% Physical Damage - in Entry Area (next to RSP Room) in the form of approximately 80 SF of gouging and holes. This Material is in FAIR condition overall. No other changes as of this date.		
12/01/2011	Additional damage, now <5% Physical Damage and <10% Water Damage- in the form of Media Center has 1 Tile broken and 2 Tiles are water stained. No other changes as of this date.		
01/29/2016	Sample 16-031-001 collected from Lobby Area, 1'x1' Glue on Ceiling Tile.		
03/30/2017	Additional Damage Observed. Approximately 80 SF of gouging and holes in Entry Area (next to RSP Room), and 4 Tiles with Cracks in RSP Room. No other changes as of this date.		
02/14/2018	Additional Damage Observed. 25 Tiles have Physical Damage gouging and holes in them in RSP Room. No other changes as of this date.		
02/03/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

16-031-001	ND	NONE DETECTED	(ND)
05-212AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

HALLWAY, MEDIA CENTER, NORTH OFFICE, AND MAIN OFFICE

CEILING TILE MASTIC

6,000 SF

09/12/2005	Mastic/Adhesive for 1'x1' Ceiling Tile. This Material is in GOOD condition as of this date.		
03/06/2007	Damage: <5% Physical Damage - in Entry Area (next to RSP Room) in the form of approximately 80 SF of gouging and holes. This Material is in FAIR condition overall. No other changes as of this date.		
12/01/2011	Additional damage, now <5% Physical Damage and <10% Water Damage- in the form of Media Center has 1 Tile broken and 2 Tiles are water stained. No other changes as of this date.		
01/29/2016	Sample 16-031-002 collected from Lobby Area, Brown Mastic/Adhesive for 1'x1' Ceiling Tile.		
03/30/2017	Additional Damage Observed. Approximately 80 SF of gouging and holes in Entry Area (next to RSP Room), and 4 Tiles with Cracks in RSP Room. No other changes as of this date.		
02/14/2018	Additional Damage Observed. 25 Tiles have Physical Damage gouging and holes in them in RSP Room. No other changes as of this date.		
02/03/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		

SF= Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		
16-031-002	ND	NONE DETECTED	(ND)
05-212AAA	ASSUMED	NO SAMPLE	(NS)

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

COMMENTS

QTY (APPROXIMATE)

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

METAL STORAGE CONTAINERS (4 EA)

METAL STORAGE CONTAINERS (4 EA)

09/12/2005	BUILDING NOTES:		
05/14/2009	Metal Storage Containers. 2 EA.		
09/04/2009	1 additional Container. Now 3 EA. 920 SF. (2 are located in the Shop's Storage Yard next to Classrooms 22-25. 1 is located on West side of the Locker Rooms Building next to Multipurpose Room).		
08/31/2010	1 additional Container. Now 4 EA. 1,420 SF.		

METAL STORAGE CONTAINERS (4 EA)

METAL STORAGE CONTAINERS

STORAGE CONTAINER

1,420 SF

09/12/2005	Metal Storage Structures.		
02/03/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

05-212.NS	NEW	NO SAMPLE	(NS)
-----------	-----	-----------	--------

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

MULTI-PURPOSE BUILDING

MULTI-PURPOSE BUILDING

09/12/2005	BUILDING NOTES:
09/12/2005	Existing Gypsum Wallboard Systems Removed and Replaced with new in-kind in Path-of-Construction. New Flooring Finishes per information received from the BUESD. New Suspended Ceiling Tiles installed.
03/06/2007	Building Name changed from GYM, LOCKER ROOMS, AND MUSIC ROOMS to MULTI-PURPOSE BUILDING. No other changes as of this date.
03/11/2010	New Ceramic Wall and Floor Tiles installed in Student Restrooms (2), and Boys and Girls Locker Room Restrooms per information received from BUESD.
09/13/2016	New Flooring Finishes installed Summer 2016 per information received from the BUESD.

MULTI-PURPOSE BUILDING

ASSEMBLY ROOM OF MULTI-PURPOSE ROOM

VINYL WALL COVER

500 SF

03/11/2010	Vinyl Cover on Accordion Wall Partition. (No Adhesive). This Material is in GOOD condition as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

10-052AAA

ASSUMED

NO SAMPLE

(NS)

SF= Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

MULTI-PURPOSE BUILDING

BOILER ROOM NEXT TO GIRLS LOCKER ROOM

DUCT WRAP TAPE

20 SF

09/12/2005 Duct Wrap Tape. This Material is in GOOD condition as of this date.

09/01/2017 This Material is unchanged as of this date.

02/03/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MULTI-PURPOSE BUILDING

BOYS AND GIRLS RESTROOMS, KITCHEN RESTROOM, LOCKER ROOMS, AND BOYS' AND GIRLS' COACHES' RESTROOM

MORTAR MISCELLANEOUS

2,050 SF

10/16/2008 Grout for 4"x4" and 6"x6" Multi-Colored Ceramic Wall Tiles (Original Entry Updated 8/17/22). This Material is in GOOD condition as of this date.

09/01/2017 Damage Observed. <5% Physical Damage - in the form of 2 Cracked Tiles in the Girls Locker Room. Material Condition changed from GOOD to FAIR. Friability changed from Non-Friable to Friable. No other changes as of this date.

02/03/2020 This Material is unchanged as of this date.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

08/28/2020	Additional Damage Observed. <5% Physical Damage in the form of 7 Tiles with Holes in Boys Restroom near Boys Locker Room Entry. Material remains in FAIR condition overall. No other changes as of this date.		
02/10/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

08-241AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MULTI-PURPOSE BUILDING

ENTIRE BUILDING

SMOOTH WALL MISCELLANEOUS

18,000 SF

09/12/2005	Gypsum Wallboard System, (under 4'x10' Pressed Wood Wall Panel with Vinyl Wall Cover in some areas. This Material is in GOOD condition as of this date.		
02/08/2016	Sample 16-031-075 collected from Multi-Use 92, Drywall.		
02/03/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		

SF=Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

16-031-075 ND NONE DETECTED (ND)

05-212AAA ASSUMED NO SAMPLE (NS)

MULTI-PURPOSE BUILDING

ENTIRE BUILDING

SMOOTH WALL SURFACING

18,000 SF

08/24/2006 Skim Coat for Gypsum Wallboard System, (under 4'x10' Pressed Wood Wall Panel with Vinyl Wall Cover in some areas. This Material is in GOOD condition as of this date.

02/03/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

06-223AAA ASSUMED NO SAMPLE (NS)

MULTI-PURPOSE BUILDING

EXTERIOR WALLS AND OVERHANG

ROUGH WALL

14,360 SF

09/12/2005 Stucco Walls and Overhang. This Material is in GOOD condition as of this date.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
02/03/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	Damage Observed. <5% Physical Damage - in the form of 2 LF of Cracks in Food Serving Area. Material condition changed from GOOD to FAIR overall. Friability changed from Non-Friable to Friable. No other changes as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		
05-212AAA	ASSUMED	NO SAMPLE	(NS)

MULTI-PURPOSE BUILDING

EXTERIOR WALLS AND OVERHANG

ROUGH WALL SURFACING

14,360 SF

09/12/2005	Skim Coat for Stucco Walls and Overhang. This Material is in GOOD condition as of this date.		
02/03/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	Damage Observed. <5% Physical Damage - in the form of 2 LF of Cracks in Food Serving Area. Material condition changed from GOOD to FAIR overall. Friability changed from Non-Friable to Friable. No other changes as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MULTI-PURPOSE BUILDING

KITCHEN EXTERIOR STORAGE (CAGED AREA) AND CONCEALED LOCATIONS

PIPE FITTING INSULATION

6 LF

09/12/2005 Pipe Fitting Insulation visible in Kitchen Exterior Storage (Caged Area) 2 Fittings/4 Mudded Joints, (additional Material may also exist in Attic, Plenums, Wall/Ceiling cavities and other inaccessible locations). This Material is in GOOD condition as of this date.

02/03/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MULTI-PURPOSE BUILDING

KITCHEN FREEZER

SEALANT

1,200 LF

05/14/2009 Sealant/Caulking for Freezer Walls and Ceiling. This Material is in GOOD condition as of this date.

SF=Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
02/03/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		
09-098AAA	ASSUMED	NO SAMPLE	(NS)

MULTI-PURPOSE BUILDING

KITCHEN, STORAGE, ELECTRICAL ROOM, RESTROOM, TABLE STORAGE ROOM, LOCKERS AREA, AND LANDING TO STAGE MULTI-PURPOSE ROOM

FIRE DOOR CORE INSULATION

360 SF

09/12/2005	Fire Door Core Insulation (8 EA DOORS). This Material is in GOOD condition as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.

SF=Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MULTI-PURPOSE BUILDING

MUSIC ROOM, PRACTICE ROOMS (2), AND STAGE

WALL TILE

1,410 SF

10/16/2008 1'x 1' Wall Tile. This Material is in GOOD condition as of this date.

12/01/2011 Quantity changed from 890 SF to 1,410 SF. No other changes as of this date.

03/30/2017 Damage Observed. <5% Physical Damage in the form of 2 Tiles Missing with Mastic Exposed on Stage. Material is in FAIR condition overall. No other changes as of this date.

02/03/2020 This Material is unchanged as of this date.

08/28/2020 Additional Damage Observed. 6 Tiles with Holes in Music Room. 3 Tiles with Holes in Practice Room 1. 2 Tiles with Scuffs in Practice Room 2. Material remains in FAIR condition overall. No other changes as of this date.

02/10/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 Additional Damage Observed. 1 Missing Tile with Brown Mastic Exposed on North Wall of Stage. No other changes as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

08-241AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

MULTI-PURPOSE BUILDING

MUSIC ROOM, PRACTICE ROOMS (2), AND STAGE

WALL TILE MASTIC

1,410 SF

10/16/2008	Mastic/Adhesive for 1'x 1' Wall Tile. This Material is in GOOD condition as of this date.
12/01/2011	Quantity changed from 890 SF to 1,410 SF. No other changes as of this date.
03/30/2017	Damage Observed. <5% Physical Damage in the form of 2 Tiles Missing with Mastic Exposed on Stage. Material is in FAIR condition overall. No other changes as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	Additional Damage Observed. 6 Tiles with Holes in Music Room. 3 Tiles with Holes in Practice Room 1. 2 Tiles with Scuffs in Practice Room 2. Material remains in FAIR condition overall. No other changes as of this date.
02/10/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	Additional Damage Observed. 1 Missing Tile with Brown Mastic Exposed on North Wall of Stage. No other changes as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

08-241AAA

ASSUMED

NO SAMPLE

(NS)

MULTI-PURPOSE BUILDING

OLD RESTROOM NEXT TO PE STORAGE ROOM, AND RESTROOM LOCATED BEHIND CLASSROOM 33

TERRAZZO FLOOR

600 SF

05/14/2009	Gray Epoxy Floor (Original Entry Updated 8/17/22). This Material is in GOOD condition as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
02/10/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	Material Re-Assessed. Material not observed, Material may exist under current Gray Epoxy Floor. No other changes as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

09-098AAA

ASSUMED

NO SAMPLE

(NS)

MULTI-PURPOSE BUILDING

PRACTICE ROOM, AND BAND ROOM OFFICE

PRESSED WOOD WALL PANEL

2,960 SF

03/06/2007	4'x8' Pressed Wood Wall Panel with Vinyl Wall Cover, (over Gypsum Wallboard System). This Material is in GOOD condition as of this date.		
02/03/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

09/17/2025 This Material is unchanged as of this date.

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MULTI-PURPOSE BUILDING

PRACTICE ROOM, AND BAND ROOM OFFICE

PRESSED WOOD WALL PANEL MASTIC

2,960 SF

03/06/2007 Mastic/Adhesive for 4'x8' Pressed Wood Wall Panel with Vinyl Wall Cover, (over Gypsum Wallboard System). This Material is in GOOD condition as of this date.

02/03/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MULTI-PURPOSE BUILDING

PRACTICE ROOM, AND BAND ROOM OFFICE

VINYL WALL COVER MASTIC

2,960 SF

03/06/2007 Mastic/Adhesive for Vinyl Wall Cover, (on 4'x8' Pressed Wood Wall Panel over Gypsum Wallboard System). This Material is in GOOD condition as of this date.

02/03/2020 This Material is unchanged as of this date.

08/28/2020 Damage Observed. <5% Physical Damage in the form of 1 SF of Torn and Missing Wall Cover around wall Outlet, on the West Wall in the Band Room. Material condition changed from GOOD to FAIR overall. Friability updated from Non-Friable to Friable. No other changes as of this date.

02/10/2021 This Material is unchanged as of this date.

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		
05-212AAA	ASSUMED	NO SAMPLE	(NS)

MULTI-PURPOSE BUILDING

STAGE, BAND ROOM, MULTI-PURPOSE ROOM, AND PRACTICE ROOM

CEILING TILE

8,500 SF

09/12/2005	1'x1' Ceiling Tile. This Material is in GOOD condition as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	Damage Observed. <5% Physical Damage in the form of 5 EA Tiles with Water Stains, 1.5 EA Tiles missing with Brown Mastic Exposed, 1 EA Tile is Loose and 1 SF of Black Mold in Multi-purpose Room. Material changed from Non-Friable to Friable. Material condition changed from GOOD to FAIR overall. No other changes as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

16-031-068

ND

NONE DETECTED

(ND)

SF=Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

30

HazMat Doc

AHERA Report B - Survey

SURVEY REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
05-212AAA	ASSUMED	NO SAMPLE	(NS)

MULTI-PURPOSE BUILDING

STAGE, BAND ROOM, MULTI-PURPOSE ROOM, AND PRACTICE ROOM

CEILING TILE MASTIC

8,500 SF

09/12/2005	Mastic/Adhesive for 1'x1' Ceiling Tile. This Material is in GOOD condition as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	Damage Observed. <5% Physical Damage in the form of 5 EA Tiles with Water Stains, 1.5 EA Tiles missing with Brown Mastic Exposed, 1 EA Tile is Loose and 1 SF of Black Mold in Multi-purpose Room. Material changed from Non-Friable to Friable. Material condition changed from GOOD to FAIR overall. No other changes as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

End Of Report, Total Of 31 Pages

HOMOGENEOUS MATERIALS IN SIERRAMONT MIDDLE SCHOOL

BUILDING NAME		
MATERIAL CATEGORY		
LOCATION		MATERIAL TYPE
BOILER ROOM		
SURFACING MATERIAL		
BOILER ROOM		ROUGH WALL
BOILER ROOM		ROUGH WALL SURFACING
CLASSROOM 40 PORTABLE BUILDING		
MISCELLANEOUS MATERIAL		
PORTABLE 40		PORTABLE BUILDING
CLASSROOM 41 PORTABLE BUILDING		
MISCELLANEOUS MATERIAL		
PORTABLE 41		PORTABLE BUILDING
CLASSROOM 42 PORTABLE BUILDING		
MISCELLANEOUS MATERIAL		
PORTABLE 42		PORTABLE BUILDING
CLASSROOM 45 PORTABLE BUILDING		
MISCELLANEOUS MATERIAL		
PORTABLE 45		PORTABLE BUILDING
CLASSROOM 46 PORTABLE BUILDING		
MISCELLANEOUS MATERIAL		
CLASSROOM 46		PORTABLE BUILDING
MAIN BUILDING		
MISCELLANEOUS MATERIAL		
ALL ADMIN OFFICES, UTILITY ROOMS, STORAGE ROOMS, CUSTODIAL ROOM, CLASSROOMS 24, 26, 28, 29, DARK ROOM, COMPUTER CLERK ROOM, AND PREP ROOMS		FIRE DOOR CORE INSULATION
ALL CLASSROOMS, LOUNGE, AND PREP AREAS		PRESSED WOOD WALL PANEL
ALL CLASSROOMS, LOUNGE, AND PREP AREAS		PRESSED WOOD WALL PANEL MASTIC
ALL CLASSROOMS, LOUNGE, AND PREP AREAS		VINYL WALL COVER MASTIC
CLASSROOM 27 STORAGE ROOM		KILN BRICK
ENTIRE BUILDING		SMOOTH WALL MISCELLANEOUS
ENTRY FOYERS AND CLASSROOM WINDOWS		CEMENTITIOUS WINDOW PANEL
HALLWAY, MEDIA CENTER, NORTH OFFICE, AND MAIN OFFICE		CEILING TILE
HALLWAY MEDIA CENTER NORTH OFFICE AND MAIN OFFICE		CEILING TILE MASTIC

HOMOGENEOUS MATERIALS IN SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

MATERIAL CATEGORY

LOCATION

MATERIAL TYPE

SURFACING MATERIAL

ENTIRE BUILDING

SMOOTH WALL SURFACING

THERMAL SYSTEM INSULATION

ATTIC / PLENUM

DUCT WRAP TAPE

METAL STORAGE CONTAINERS (4 EA)

MISCELLANEOUS MATERIAL

METAL STORAGE CONTAINERS

STORAGE CONTAINER

MULTI-PURPOSE BUILDING

MISCELLANEOUS MATERIAL

ASSEMBLY ROOM OF MULTI-PURPOSE ROOM

VINYL WALL COVER

BOYS AND GIRLS RESTROOMS, KITCHEN RESTROOM, LOCKER ROOMS, AND
BOYS' AND GIRLS' COACHES' RESTROOM

MORTAR MISCELLANEOUS

ENTIRE BUILDING

SMOOTH WALL
MISCELLANEOUS

KITCHEN FREEZER

SEALANT

KITCHEN, STORAGE, ELECTRICAL ROOM, RESTROOM, TABLE STORAGE ROOM,
LOCKERS AREA, AND LANDING TO STAGE MULTI-PURPOSE ROOM

FIRE DOOR CORE INSULATION

MUSIC ROOM, PRACTICE ROOMS (2), AND STAGE

WALL TILE

MUSIC ROOM, PRACTICE ROOMS (2), AND STAGE

WALL TILE MASTIC

OLD RESTROOM NEXT TO PE STORAGE ROOM, AND RESTROOM LOCATED
BEHIND CLASSROOM 33

TERRAZZO FLOOR

PRACTICE ROOM, AND BAND ROOM OFFICE

PRESSED WOOD WALL PANEL

PRACTICE ROOM, AND BAND ROOM OFFICE

PRESSED WOOD WALL PANEL
MASTIC

PRACTICE ROOM, AND BAND ROOM OFFICE

VINYL WALL COVER MASTIC

STAGE, BAND ROOM, MULTI-PURPOSE ROOM, AND PRACTICE ROOM

CEILING TILE

STAGE, BAND ROOM, MULTI-PURPOSE ROOM, AND PRACTICE ROOM

CEILING TILE MASTIC

SURFACING MATERIAL

ENTIRE BUILDING

SMOOTH WALL SURFACING

EXTERIOR WALLS AND OVERHANG

ROUGH WALL

EXTERIOR WALLS AND OVERHANG

ROUGH WALL SURFACING

THERMAL SYSTEM INSULATION

BOILER ROOM NEXT TO GIRLS LOCKER ROOM

DUCT WRAP TAPE

KITCHEN EXTERIOR STORAGE (CAGED AREA) AND CONCEALED LOCATIONS

PIPE FITTING INSULATION

End Of Report, Total Of 2 Pages

FRIABLE LOCATIONS IN SIERRAMONT MIDDLE SCHOOL

BUILDING NAME	LOCATION	QTY (APPROXIMATE)	ASBESTOS CONTENT
MATERIAL TYPE			
MAIN BUILDING			
ALL ADMIN OFFICES, UTILITY ROOMS, STORAGE ROOMS, CUSTODIAL ROOM, CLASSROOMS 24, 26, 28, 29, DARK ROOM, COMPUTER CLERK ROOM, AND PREP ROOMS			
	FIRE DOOR CORE INSULATION	693 SF	Assumed
ALL CLASSROOMS, LOUNGE, AND PREP AREAS			
	PRESSED WOOD WALL PANEL	14,630 SF	Assumed
ALL CLASSROOMS, LOUNGE, AND PREP AREAS			
	PRESSED WOOD WALL PANEL MASTIC	14,630 SF	Assumed
ALL CLASSROOMS, LOUNGE, AND PREP AREAS			
	VINYL WALL COVER MASTIC	14,630 SF	Assumed
ATTIC / PLENUM			
	DUCT WRAP TAPE	1,000 LF	Assumed
CLASSROOM 27 STORAGE ROOM			
	KILN BRICK	60 SF	Assumed
ENTIRE BUILDING			
	SMOOTH WALL MISCELLANEOUS	76,000 SF	Assumed
ENTIRE BUILDING			
	SMOOTH WALL SURFACING	76,000 SF	Assumed
HALLWAY, MEDIA CENTER, NORTH OFFICE, AND MAIN OFFICE			
	CEILING TILE	6,000 SF	Assumed
HALLWAY, MEDIA CENTER, NORTH OFFICE, AND MAIN OFFICE			
	CEILING TILE MASTIC	6,000 SF	Assumed
MULTI-PURPOSE BUILDING			
BOILER ROOM NEXT TO GIRLS LOCKER ROOM			
	DUCT WRAP TAPE	20 SF	Assumed
BOYS AND GIRLS RESTROOMS, KITCHEN RESTROOM, LOCKER ROOMS, AND BOYS' AND GIRLS' COACHES' RESTROOM			
	MORTAR MISCELLANEOUS	2,050 SF	Assumed
ENTIRE BUILDING			
	SMOOTH WALL MISCELLANEOUS	18,000 SF	Assumed
ENTIRE BUILDING			
	SMOOTH WALL SURFACING	18,000 SF	Assumed
EXTERIOR WALLS AND OVERHANG			
	ROUGH WALL	14,360 SF	Assumed
EXTERIOR WALLS AND OVERHANG			
	ROUGH WALL SURFACING	14,360 SF	Assumed

FRIABLE LOCATIONS IN SIERRAMONT MIDDLE SCHOOL

BUILDING NAME			
LOCATION		QTY	ASBESTOS
MATERIAL TYPE		(APPROXIMATE)	CONTENT
KITCHEN EXTERIOR STORAGE (CAGED AREA) AND CONCEALED LOCATIONS			
PIPE FITTING INSULATION		6 LF	Assumed
KITCHEN, STORAGE, ELECTRICAL ROOM, RESTROOM, TABLE STORAGE ROOM, LOCKERS AREA, AND LANDING TO STAGE MULTI-PURPOSE ROOM			
FIRE DOOR CORE INSULATION		360 SF	Assumed
MUSIC ROOM, PRACTICE ROOMS (2), AND STAGE			
WALL TILE		1,410 SF	Assumed
MUSIC ROOM, PRACTICE ROOMS (2), AND STAGE			
WALL TILE MASTIC		1,410 SF	Assumed
PRACTICE ROOM, AND BAND ROOM OFFICE			
PRESSED WOOD WALL PANEL		2,960 SF	Assumed
PRACTICE ROOM, AND BAND ROOM OFFICE			
VINYL WALL COVER MASTIC		2,960 SF	Assumed
STAGE, BAND ROOM, MULTI-PURPOSE ROOM, AND PRACTICE ROOM			
CEILING TILE		8,500 SF	Assumed
STAGE, BAND ROOM, MULTI-PURPOSE ROOM, AND PRACTICE ROOM			
CEILING TILE MASTIC		8,500 SF	Assumed
End Of Report, Total Of 2 Pages			

Non- Friable Locations In SIERRAMONT MIDDLE SCHOOL

BUILDING NAME			
LOCATION		QTY	ASBESTOS
MATERIAL TYPE		(APPROXIMATE)	CONTENT
BOILER ROOM			
BOILER ROOM			
ROUGH WALL		1,800 SF	Assumed
BOILER ROOM			
ROUGH WALL SURFACING		1,800 SF	Assumed
MAIN BUILDING			
ENTRY FOYERS AND CLASSROOM WINDOWS			
CEMENTITIOUS WINDOW PANEL		286 SF	Assumed
METAL STORAGE CONTAINERS (4 EA)			
MULTI-PURPOSE BUILDING			
ASSEMBLY ROOM OF MULTI-PURPOSE ROOM			
VINYL WALL COVER		500 SF	Assumed
KITCHEN FREEZER			
SEALANT		1,200 LF	Assumed
OLD RESTROOM NEXT TO PE STORAGE ROOM, AND RESTROOM LOCATED BEHIND CLASSROOM 33			
TERRAZZO FLOOR		600 SF	Assumed
PRACTICE ROOM, AND BAND ROOM OFFICE			
PRESSED WOOD WALL PANEL MASTIC		2,960 SF	Assumed
End Of Report, Total Of 1 Pages			

RECOMMENDATIONS FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

BOILER ROOM

BOILER ROOM

ROUGH WALL

1,800 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

BOILER ROOM

ROUGH WALL SURFACING

1,800 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

CLASSROOM 40 PORTABLE BUILDING

PORTABLE 40

PORTABLE BUILDING

960 SF

- (a) This is a replacement/new material.
- (b) The District should obtain documentation from the manufacturer/installer that no asbestos has been used in the manufacture or installation of this building material.
- (c) This documentation is to be maintained with the District's AHERA records.

RECOMMENDATIONS FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

CLASSROOM 41 PORTABLE BUILDING

PORTABLE 41

PORTABLE BUILDING

960 SF

- (a) This is a replacement/new material.
- (b) The district should obtain documentation from the manufacturer/installer that no asbestos has been used in the manufacture or installation of this building material.
- (c) This documentation is to be maintained with the district's AHERA records.

CLASSROOM 42 PORTABLE BUILDING

PORTABLE 42

PORTABLE BUILDING

960 SF

- (a) This is a replacement/new material.
- (b) The district should obtain documentation from the manufacturer/installer that no asbestos has been used in the manufacture or installation of this building material.
- (c) This documentation is to be maintained with the district's AHERA records.

CLASSROOM 45 PORTABLE BUILDING

PORTABLE 45

PORTABLE BUILDING

960 SF

- (a) This is a replacement/new material.
- (b) The District should obtain documentation from the manufacturer/installer that no asbestos has been used in the manufacture or installation of this building material.
- (c) This documentation is to be maintained with the District's AHERA records.

RECOMMENDATIONS FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME**LOCATION****MATERIAL TYPE****RECOMMENDATION****QTY****(APPROXIMATE)**

CLASSROOM 46 PORTABLE BUILDING

CLASSROOM 46**PORTABLE BUILDING****960 SF**

- (a) This is a replacement/new material.
 - (b) The District should obtain documentation from the manufacturer/installer that no asbestos has been used in the manufacture or installation of this building material.
 - (c) This documentation is to be maintained with the District's AHERA records.
-

MAIN BUILDING

ALL ADMIN OFFICES, UTILITY ROOMS, STORAGE ROOMS, CUSTODIAL ROOM, CLASSROOMS 24, 26, 28, 29,
DARK ROOM, COMPUTER CLERK ROOM, AND PREP ROOMS

FIRE DOOR CORE INSULATION**693 SF**

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.
-

ALL CLASSROOMS, LOUNGE, AND PREP AREAS**PRESSED WOOD WALL PANEL****14,630 SF**

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.
-

RECOMMENDATIONS FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME**LOCATION****MATERIAL TYPE****RECOMMENDATION****QTY****(APPROXIMATE)**

ALL CLASSROOMS, LOUNGE, AND PREP AREAS**PRESSED WOOD WALL PANEL MASTIC****14,630 SF**

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

ALL CLASSROOMS, LOUNGE, AND PREP AREAS**VINYL WALL COVER MASTIC****14,630 SF**

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

ATTIC / PLENUM**DUCT WRAP TAPE****1,000 LF**

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

CLASSROOM 27 STORAGE ROOM**KILN BRICK****60 SF**

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

ENTIRE BUILDING

SMOOTH WALL MISCELLANEOUS 76,000 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

ENTIRE BUILDING

SMOOTH WALL SURFACING 76,000 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

ENTRY FOYERS AND CLASSROOM WINDOWS

CEMENTITIOUS WINDOW PANEL 286 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

HALLWAY, MEDIA CENTER, NORTH OFFICE, AND MAIN OFFICE

CEILING TILE 6,000 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME**LOCATION****MATERIAL TYPE****RECOMMENDATION****QTY****(APPROXIMATE)**

HALLWAY, MEDIA CENTER, NORTH OFFICE, AND MAIN OFFICE

CEILING TILE MASTIC

6,000 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

METAL STORAGE CONTAINERS (4 EA)

METAL STORAGE CONTAINERS

STORAGE CONTAINER

1,420 SF

- (a) This is a replacement/new material.
- (b) The District should obtain documentation from the manufacturer/installer that no asbestos has been used in the manufacture or installation of this building material.
- (c) This documentation is to be maintained with the District's AHERA records.

MULTI-PURPOSE BUILDING

ASSEMBLY ROOM OF MULTI-PURPOSE ROOM

VINYL WALL COVER

500 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

BOILER ROOM NEXT TO GIRLS LOCKER ROOM

DUCT WRAP TAPE

20 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

BOYS AND GIRLS RESTROOMS, KITCHEN RESTROOM, LOCKER ROOMS, AND BOYS' AND GIRLS' COACHES' RESTROOM

MORTAR MISCELLANEOUS

2,050 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

ENTIRE BUILDING

SMOOTH WALL MISCELLANEOUS

18,000 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

ENTIRE BUILDING

SMOOTH WALL SURFACING

18,000 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

EXTERIOR WALLS AND OVERHANG

ROUGH WALL

14,360 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

EXTERIOR WALLS AND OVERHANG

ROUGH WALL SURFACING

14,360 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

KITCHEN EXTERIOR STORAGE (CAGED AREA) AND CONCEALED LOCATIONS

PIPE FITTING INSULATION

6 LF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

KITCHEN FREEZER

SEALANT

1,200 LF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

KITCHEN, STORAGE, ELECTRICAL ROOM, RESTROOM, TABLE STORAGE ROOM, LOCKERS AREA, AND LANDING TO STAGE MULTI-PURPOSE ROOM

FIRE DOOR CORE INSULATION

360 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

MUSIC ROOM, PRACTICE ROOMS (2), AND STAGE

WALL TILE

1,410 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

MUSIC ROOM, PRACTICE ROOMS (2), AND STAGE

WALL TILE MASTIC

1,410 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

OLD RESTROOM NEXT TO PE STORAGE ROOM, AND RESTROOM LOCATED BEHIND CLASSROOM 33

TERRAZZO FLOOR

600 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

PRACTICE ROOM, AND BAND ROOM OFFICE

PRESSED WOOD WALL PANEL

2,960 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

PRACTICE ROOM, AND BAND ROOM OFFICE

PRESSED WOOD WALL PANEL MASTIC

2,960 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

PRACTICE ROOM, AND BAND ROOM OFFICE

VINYL WALL COVER MASTIC

2,960 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

STAGE, BAND ROOM, MULTI-PURPOSE ROOM, AND PRACTICE ROOM

CEILING TILE

8,500 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

STAGE, BAND ROOM, MULTI-PURPOSE ROOM, AND PRACTICE ROOM

CEILING TILE MASTIC

8,500 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.
-

End Of Report, Total Of 11 Pages

SAMPLES REPORT FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

BOILER ROOM

BOILER ROOM

BOILER ROOM

ROUGH WALL

05-212AAA

9/12/2005

Positive

ASSUMED

NO SAMPLE

NS

BOILER ROOM

BOILER ROOM

ROUGH WALL SURFACING

05-212AAA

9/12/2005

Positive

ASSUMED

NO SAMPLE

NS

SAMPLES REPORT FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO.	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
COMMENTS					

CLASSROOM 40 PORTABLE BUILDING

CLASSROOM 40 PORTABLE BUILDING

PORTABLE 40

PORTABLE BUILDING

05-212.NS

3/6/2007

Negative

NEW MATERIAL

NO SAMPLE

NS

New 2006 Construction Relocatable Building per Manufacturer's Tag information.

SAMPLES REPORT FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO.	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
COMMENTS					

CLASSROOM 41 PORTABLE BUILDING

CLASSROOM 41 PORTABLE BUILDING

PORTABLE 41

PORTABLE BUILDING

05-212.NS

9/12/2005

Negative

NEW MATERIAL

NO SAMPLE

NS

New 1991 Construction Relocatable Building per Manufacturer's Tag information.

SAMPLES REPORT FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO.	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
COMMENTS					

CLASSROOM 42 PORTABLE BUILDING

CLASSROOM 42 PORTABLE BUILDING

PORTABLE 42

PORTABLE BUILDING

05-212.NS

9/12/2005

Negative

NEW MATERIAL

NO SAMPLE

NS

New 1999 Construction Relocatable Building per Manufacturer's Tag information.

SAMPLES REPORT FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO.	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
COMMENTS					

CLASSROOM 45 PORTABLE BUILDING

CLASSROOM 45 PORTABLE BUILDING

PORTABLE 45

PORTABLE BUILDING

12-185.NS

10/11/2012 Negative

NEW MATERIAL

NO SAMPLE

NS

New 2012 Construction Relocatable Building per Manufacturer's Tag information.

SAMPLES REPORT FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO.	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
COMMENTS					

CLASSROOM 46 PORTABLE BUILDING

CLASSROOM 46 PORTABLE BUILDING

CLASSROOM 46

PORTABLE BUILDING

12-185.NS

10/11/2012 Negative

NEW MATERIAL

NO SAMPLE

NS

New 1999 Construction Relocatable Building per Manufacturer's Tag information.

SAMPLES REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME
LOCATION
MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

MAIN BUILDING

MAIN BUILDING

ALL ADMIN OFFICES, UTILITY ROOMS, STORAGE ROOMS, CUSTODIAL ROOM, CLASSROOMS 24, 26, 28, 29, DARK ROOM,
 COMPUTER CLERK ROOM, AND PREP ROOMS
 FIRE DOOR CORE INSULATION

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MAIN BUILDING

ALL CLASSROOMS, LOUNGE, AND PREP AREAS
 PRESSED WOOD WALL PANEL

<u>05-212AAA</u>	3/6/2007	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

MAIN BUILDING

ALL CLASSROOMS, LOUNGE, AND PREP AREAS
 PRESSED WOOD WALL PANEL MASTIC

<u>05-212AAA</u>	3/6/2007	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

MAIN BUILDING

ALL CLASSROOMS, LOUNGE, AND PREP AREAS
 VINYL WALL COVER MASTIC

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MAIN BUILDING

ATTIC / PLENUM
 DUCT WRAP TAPE

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MAIN BUILDING

CLASSROOM 27 STORAGE ROOM
 KILN BRICK

<u>16-074AAA</u>	3/22/2016	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MAIN BUILDING

ENTIRE BUILDING
 SMOOTH WALL MISCELLANEOUS

	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
--	-----------	----------	---------	-----------	----

SAMPLES REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

<u>16-031-019</u> Corridor 18C, Drywall Board.	1/29/2016	Negative	ND	NONE DETECTED	ND
--	-----------	----------	----	---------------	----

<u>16-031-020</u> Corridor 18C, Joint Compound for Drywall Board.	1/29/2016	Negative	ND	NONE DETECTED	ND
---	-----------	----------	----	---------------	----

<u>16-031-023</u> Custodian #7, Drywall Board.	1/29/2016	Negative	ND	NONE DETECTED	ND
--	-----------	----------	----	---------------	----

<u>16-031-024</u> Custodian #7, Joint Compound for Drywall Board.	1/29/2016	Negative	ND	NONE DETECTED	ND
---	-----------	----------	----	---------------	----

<u>16-031-026</u> Corridor 6, Drywall Board.	1/29/2016	Negative	ND	NONE DETECTED	ND
--	-----------	----------	----	---------------	----

<u>16-031-027</u> Corridor 6, Joint Compound for Drywall Board.	1/29/2016	Positive	2%	CHRYSTILE	CH
---	-----------	----------	----	-----------	----

<u>16-031-053</u> Main Lobby by Drinking Fountain, Wallboard.	2/8/2016	Negative	ND	NONE DETECTED	ND
---	----------	----------	----	---------------	----

<u>16-031-055</u> Main Lobby by Drinking Fountain, Joint Compound on Wallboard.	2/8/2016	Negative	ND	NONE DETECTED	ND
---	----------	----------	----	---------------	----

MAIN BUILDING

ENTIRE BUILDING

SMOOTH WALL SURFACING

<u>06-223AAA</u>	8/24/2006	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

<u>16-031-021</u> Corridor 18C, Paint.	1/29/2016	Negative	ND	NONE DETECTED	ND
--	-----------	----------	----	---------------	----

<u>16-031-021</u> Corridor 18C, Skim Coat.	1/29/2016	Positive	<1	CHRYSTILE	CH
--	-----------	----------	----	-----------	----

<u>16-031-025</u> Custodian #7, Skim Coat.	1/29/2016	Negative	ND	NONE DETECTED	ND
--	-----------	----------	----	---------------	----

<u>16-031-028</u> Corridor 6, Paint.	1/29/2016	Negative	ND	NONE DETECTED	ND
--	-----------	----------	----	---------------	----

SAMPLES REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

<u>16-031-028</u> Corridor 6, Skim Coat.	1/29/2016	Positive	2%	CHRYSTOTILE	CH
--	-----------	----------	----	-------------	----

<u>16-031-054</u> Main Lobby by Drinking Fountain, Skim Coat on Wallboard.	2/8/2016	Negative	ND	NONE DETECTED	ND
--	----------	----------	----	---------------	----

MAIN BUILDING

ENTRY FOYERS AND CLASSROOM WINDOWS
CEMENTITIOUS WINDOW PANEL

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MAIN BUILDING

HALLWAY, MEDIA CENTER, NORTH OFFICE, AND MAIN OFFICE
CEILING TILE

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

<u>16-031-001</u> Lobby Area.	1/29/2016	Negative	ND	NONE DETECTED	ND
---	-----------	----------	----	---------------	----

MAIN BUILDING

HALLWAY, MEDIA CENTER, NORTH OFFICE, AND MAIN OFFICE
CEILING TILE MASTIC

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

<u>16-031-002</u> Lobby Area, Brown Mastic.	1/29/2016	Negative	ND	NONE DETECTED	ND
---	-----------	----------	----	---------------	----

SAMPLES REPORT FOR
SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO.	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
COMMENTS					

METAL STORAGE CONTAINERS (4 EA)

METAL STORAGE CONTAINERS (4 EA)

METAL STORAGE CONTAINERS

STORAGE CONTAINER

05-212.NS

9/12/2005

Negative

NEW MATERIAL

NO SAMPLE

NS

Metal Storage Structure.

SAMPLES REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

MULTI-PURPOSE BUILDING

MULTI-PURPOSE BUILDING

ASSEMBLY ROOM OF MULTI-PURPOSE ROOM
VINYL WALL COVER

<u>10-052AAA</u>	3/10/2010	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

BOILER ROOM NEXT TO GIRLS LOCKER ROOM
DUCT WRAP TAPE

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

BOYS AND GIRLS RESTROOMS, KITCHEN RESTROOM, LOCKER ROOMS, AND BOYS' AND GIRLS' COACHES' RESTROOM
MORTAR MISCELLANEOUS

<u>08-241AAA</u>	10/16/2008	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	------------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

ENTIRE BUILDING
SMOOTH WALL MISCELLANEOUS

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

<u>16-031-075</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
--------------------------	----------	----------	----	---------------	----

Multi-use 92, Drywall.

MULTI-PURPOSE BUILDING

ENTIRE BUILDING
SMOOTH WALL SURFACING

<u>06-223AAA</u>	8/24/2006	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

EXTERIOR WALLS AND OVERHANG
ROUGH WALL

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

SAMPLES REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

MULTI-PURPOSE BUILDING

EXTERIOR WALLS AND OVERHANG

ROUGH WALL SURFACING

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

KITCHEN EXTERIOR STORAGE (CAGED AREA) AND CONCEALED LOCATIONS

PIPE FITTING INSULATION

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

KITCHEN FREEZER

SEALANT

<u>09-098AAA</u>	5/14/2009	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

KITCHEN, STORAGE, ELECTRICAL ROOM, RESTROOM, TABLE STORAGE ROOM, LOCKERS AREA, AND LANDING TO STAGE MULTI-PURPOSE ROOM

FIRE DOOR CORE INSULATION

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

MUSIC ROOM, PRACTICE ROOMS (2), AND STAGE

WALL TILE

<u>08-241AAA</u>	10/16/2008	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	------------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

MUSIC ROOM, PRACTICE ROOMS (2), AND STAGE

WALL TILE MASTIC

<u>08-241AAA</u>	10/16/2008	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	------------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

OLD RESTROOM NEXT TO PE STORAGE ROOM, AND RESTROOM LOCATED BEHIND CLASSROOM 33

TERRAZZO FLOOR

<u>09-098AAA</u>	5/14/2009	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

SAMPLES REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

MULTI-PURPOSE BUILDING

PRACTICE ROOM, AND BAND ROOM OFFICE

PRESSED WOOD WALL PANEL

<u>05-212AAA</u>	3/6/2007	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

PRACTICE ROOM, AND BAND ROOM OFFICE

PRESSED WOOD WALL PANEL MASTIC

<u>05-212AAA</u>	3/6/2007	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

PRACTICE ROOM, AND BAND ROOM OFFICE

VINYL WALL COVER MASTIC

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MULTI-PURPOSE BUILDING

STAGE, BAND ROOM, MULTI-PURPOSE ROOM, AND PRACTICE ROOM

CEILING TILE

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

<u>16-031-068</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
--------------------------	----------	----------	----	---------------	----

Vestibule 91, 1'x1' Ceiling Tile.

MULTI-PURPOSE BUILDING

STAGE, BAND ROOM, MULTI-PURPOSE ROOM, AND PRACTICE ROOM

CEILING TILE MASTIC

<u>05-212AAA</u>	9/12/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

End Of Report, Total Of 13 Pages

DAMAGE REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
RISK ASSESSMENT CATEGORY	COMMENTS			

MAIN BUILDING

MAIN BUILDING

ALL CLASSROOMS, LOUNGE, AND PREP AREAS

PRESSED WOOD WALL PANEL

14,630 SF

P: Less Than 5%

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

03/06/2007	4'x10' Pressed Wood Wall Panel with Vinyl Wall Cover, (over Gypsum Wallboard System). This Material is in GOOD condition as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	Additional Damage Observed. 1 SF of Missing Vinyl Wall Cover at Entry into Pod 2 by Baseboard. No other changes as of this date.
09/17/2025	This Material is unchanged as of this date.

MAIN BUILDING

ALL CLASSROOMS, LOUNGE, AND PREP AREAS

PRESSED WOOD WALL PANEL MASTIC

14,630 SF

P: Less Than 5%

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

03/06/2007	Mastic/Adhesive for 4'x10' Pressed Wood Wall Panel with Vinyl Wall Cover, (over Gypsum Wallboard System). This Material is in GOOD condition as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RISK ASSESMENT CATEGORY

COMMENTS

QTY
(APPROXIMATE)

PHYSICAL DAMAGE (P:)
WATER DAMAGE (W:)

02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	Additional Damage Observed. 1 SF of Missing Vinyl Wall Cover at Entry into Pod 2 by Baseboard. No other changes as of this date.
09/17/2025	This Material is unchanged as of this date.

MAIN BUILDING

ALL CLASSROOMS, LOUNGE, AND PREP AREAS

VINYL WALL COVER MASTIC

14,630 SF

P: Less Than 5%

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

09/12/2005	Mastiv/Adhesive for Vinyl Covering on 4'x10' Vinyl Covered Pressed Wood Walls. This Material is in GOOD condition as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	Additional Damage Observed. 1 SF of Missing Vinyl Wall Cover at Entry into Pod 2 by Baseboard. No other changes as of this date.
09/17/2025	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESSMENT CATEGORY	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
COMMENTS					

MAIN BUILDING

ENTIRE BUILDING

SMOOTH WALL MISCELLANEOUS	76,000 SF	P: Less Than 5% W: No Evidence
---------------------------	-----------	---

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

09/12/2005	Gypsum Wallboard System, (under 4'x10' Pressed Wood Wall Panel with Vinyl Wall Cover in some areas). Existing Gypsum Wallboard Systems Removed and Replaced with new in-kind in Path-of-Construction. This Material is in GOOD condition as of this date.
01/29/2016	Sample 16-031-019 collected from Corridor 18C, Gypsum Board. Sample 16-031-020 collected from Corridor 18C, Joint Compound for Drywall Board. Sample 16-031-023 collected from Custodian #7, Gypsum Board. Sample 16-031-024 collected from Custodian #7, Joint Compound for Drywall Board. Sample 16-031-026 collected from Corridor 6, Drywall Board. Sample 16-031-027 Corridor 6, Joint Compound for Drywall.
02/08/2016	Sample 16-031-053 collected from Main Lobby by Drinking Fountain, Wallboard. Sample 16-031-055 collected from Main Lobby by Drinking Fountain, Joint Compound on Wallboard.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	Damage Observed. <5% Physical Damage - in the form of 1 SF of Missing Scratch-Skim Coat around Whiteboards in Room 3A. Material condition changed from GOOD to FAIR overall. Friability changed from Non-Friable to Friable. No other changes as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

MAIN BUILDING

ENTIRE BUILDING

SMOOTH WALL SURFACING	76,000 SF	P: Less Than 5% W: No Evidence
-----------------------	-----------	---

DAMAGED FRIABLE SURFACING ACM

08/24/2006	Skim Coat for Gypsum Wallboard System, (under 4'x10' Pressed Wood Wall Panel with Vinyl Wall Cover in some areas). Existing Gypsum Wallboard Systems Removed and Replaced with new in-kind in Path-of-Construction. This Material is in GOOD condition as of this date.
------------	---

DAMAGE REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESMENT CATEGORY	COMMENTS	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
---------------	----------	---------------	-------------------------	----------	----------------------	---

01/29/2016	Sample 16-031-021 collected from Corridor 18C, Skim Coat and Paint for Gypsum Board. Sample 16-031-025 collected from Custodian #7, Skim Coat and Paint for Gypsum Board. Sample 16-031-028 collected from Corridor 6, Skim Coat and Paint for Drywall Board.					
02/08/2016	Sample 16-031-054 collected from Main Lobby by Drinking Fountain, Skim Coat on Wallboard.					
08/28/2020	This Material is unchanged as of this date.					
02/10/2021	This Material is unchanged as of this date.					
08/11/2021	This Material is unchanged as of this date.					
02/18/2022	This Material is unchanged as of this date.					
08/17/2022	This Material is unchanged as of this date.					
02/15/2023	This Material is unchanged as of this date.					
08/16/2023	This Material is unchanged as of this date.					
02/14/2024	This Material is unchanged as of this date.					
08/14/2024	Damage Observed. <5% Physical Damage - in the form of 1 SF of Missing and Scratch-Skim Coat around Whiteboards in Room 3A. Material condition changed from GOOD to FAIR overall. Friability changed from Non-Friable to Friable. No other changes as of this date.					
02/27/2025	This Material is unchanged as of this date.					
09/17/2025	This Material is unchanged as of this date.					

MAIN BUILDING

HALLWAY, MEDIA CENTER, NORTH OFFICE, AND MAIN OFFICE

CEILING TILE

6,000 SF

P: Less Than 5%

W: <10% Stains or Flaking

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

09/12/2005	1'x1' Ceiling Tile. This Material is in GOOD condition as of this date.					
03/06/2007	Damage: <5% Physical Damage - in Entry Area (next to RSP Room) in the form of approximately 80 SF of gouging and holes. This Material is in FAIR condition overall. No other changes as of this date.					
12/01/2011	Additional damage, now <5% Physical Damage and <10% Water Damage- in the form of Media Center has 1 Tile broken and 2 Tiles are water stained. No other changes as of this date.					
01/29/2016	Sample 16-031-001 collected from Lobby Area, 1'x1' Glue on Ceiling Tile.					
03/30/2017	Additional Damage Observed. Approximately 80 SF of gouging and holes in Entry Area (next to RSP Room), and 4 Tiles with Cracks in RSP Room. No other changes as of this date.					
02/14/2018	Additional Damage Observed. 25 Tiles have Physical Damage gouging and holes in them in RSP Room. No other changes as of this date.					
02/03/2020	This Material is unchanged as of this date.					
08/28/2020	This Material is unchanged as of this date.					

DAMAGE REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESMENT CATEGORY	COMMENTS	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
---------------	----------	---------------	-------------------------	----------	----------------------	---

02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

MAIN BUILDING

HALLWAY, MEDIA CENTER, NORTH OFFICE, AND MAIN OFFICE

CEILING TILE MASTIC

6,000 SF

P: Less Than 5%

W: <10% Stains or Flaking

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

09/12/2005	Mastic/Adhesive for 1'x1' Ceiling Tile. This Material is in GOOD condition as of this date.
03/06/2007	Damage: <5% Physical Damage - in Entry Area (next to RSP Room) in the form of approximately 80 SF of gouging and holes. This Material is in FAIR condition overall. No other changes as of this date.
12/01/2011	Additional damage, now <5% Physical Damage and <10% Water Damage- in the form of Media Center has 1 Tile broken and 2 Tiles are water stained. No other changes as of this date.
01/29/2016	Sample 16-031-002 collected from Lobby Area, Brown Mastic/Adhesive for 1'x1' Ceiling Tile.
03/30/2017	Additional Damage Observed. Approximately 80 SF of gouging and holes in Entry Area (next to RSP Room), and 4 Tiles with Cracks in RSP Room. No other changes as of this date.
02/14/2018	Additional Damage Observed. 25 Tiles have Physical Damage gouging and holes in them in RSP Room. No other changes as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RISK ASSESMENT CATEGORY

COMMENTS

QTY
(APPROXIMATE)

PHYSICAL DAMAGE (P:)
WATER DAMAGE (W:)

08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESSMENT CATEGORY	COMMENTS	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
---------------	----------	---------------	--------------------------	----------	----------------------	---

MULTI-PURPOSE BUILDING

MULTI-PURPOSE BUILDING

BOYS AND GIRLS RESTROOMS, KITCHEN RESTROOM, LOCKER ROOMS, AND BOYS' AND GIRLS' COACHES' RESTROOM

MORTAR MISCELLANEOUS	2,050 SF	P: Less Than 5% W: No Evidence
----------------------	----------	---

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

10/16/2008	Grout for 4"x4" and 6"x6" Multi-Colored Ceramic Wall Tiles (Original Entry Updated 8/17/22). This Material is in GOOD condition as of this date.
09/01/2017	Damage Observed. <5% Physical Damage - in the form of 2 Cracked Tiles in the Girls Locker Room. Material Condition changed from GOOD to FAIR. Friability changed from Non-Friable to Friable. No other changes as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	Additional Damage Observed. <5% Physical Damage in the form of 7 Tiles with Holes in Boys Restroom near Boys Locker Room Entry. Material remains in FAIR condition overall. No other changes as of this date.
02/10/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

MULTI-PURPOSE BUILDING

ENTIRE BUILDING

SMOOTH WALL MISCELLANEOUS	18,000 SF	P: No Visible Damage W: No Evidence
---------------------------	-----------	--

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

09/12/2005	Gypsum Wallboard System, (under 4'x10' Pressed Wood Wall Panel with Vinyl Wall Cover in some areas. This Material is in GOOD condition as of this date.
02/08/2016	Sample 16-031-075 collected from Multi-Use 92, Drywall.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RISK ASSESSMENT CATEGORY

COMMENTS

QTY
(APPROXIMATE)

PHYSICAL DAMAGE (P:)
WATER DAMAGE (W:)

02/10/2021 This Material is unchanged as of this date.
02/18/2022 This Material is unchanged as of this date.
08/17/2022 This Material is unchanged as of this date.
02/15/2023 This Material is unchanged as of this date.
08/16/2023 This Material is unchanged as of this date.
02/14/2024 This Material is unchanged as of this date.
08/14/2024 This Material is unchanged as of this date.
02/27/2025 This Material is unchanged as of this date.
09/17/2025 This Material is unchanged as of this date.

MULTI-PURPOSE BUILDING

EXTERIOR WALLS AND OVERHANG

ROUGH WALL

14,360 SF

P: Less Than 5%

W: No Evidence

DAMAGED FRIABLE SURFACING ACM

09/12/2005 Stucco Walls and Overhang. This Material is in GOOD condition as of this date.
02/03/2020 This Material is unchanged as of this date.
08/28/2020 This Material is unchanged as of this date.
02/10/2021 Damage Observed. <5% Physical Damage - in the form of 2 LF of Cracks in Food Serving Area. Material condition changed from GOOD to FAIR overall. Friability changed from Non-Friable to Friable. No other changes as of this date.
02/18/2022 This Material is unchanged as of this date.
08/17/2022 This Material is unchanged as of this date.
02/15/2023 This Material is unchanged as of this date.
08/16/2023 This Material is unchanged as of this date.
02/14/2024 This Material is unchanged as of this date.
08/14/2024 This Material is unchanged as of this date.
02/27/2025 This Material is unchanged as of this date.
09/17/2025 This Material is unchanged as of this date.

DAMAGE REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESSMENT CATEGORY	COMMENTS	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
---------------	----------	---------------	--------------------------	----------	----------------------	---

MULTI-PURPOSE BUILDING

EXTERIOR WALLS AND OVERHANG

ROUGH WALL SURFACING	14,360 SF	P: Less Than 5% W: No Evidence
----------------------	-----------	-----------------------------------

DAMAGED FRIABLE SURFACING ACM

09/12/2005	Skim Coat for Stucco Walls and Overhang. This Material is in GOOD condition as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	Damage Observed. <5% Physical Damage - in the form of 2 LF of Cracks in Food Serving Area. Material condition changed from GOOD to FAIR overall. Friability changed from Non-Friable to Friable. No other changes as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

MULTI-PURPOSE BUILDING

MUSIC ROOM, PRACTICE ROOMS (2), AND STAGE

WALL TILE	1,410 SF	P: Less Than 5% W: No Evidence
-----------	----------	-----------------------------------

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

10/16/2008	1'x 1' Wall Tile. This Material is in GOOD condition as of this date.
12/01/2011	Quantity changed from 890 SF to 1,410 SF. No other changes as of this date.
03/30/2017	Damage Observed. <5% Physical Damage in the form of 2 Tiles Missing with Mastic Exposed on Stage. Material is in FAIR condition overall. No other changes as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	Additional Damage Observed. 6 Tiles with Holes in Music Room. 3 Tiles with Holes in Practice Room 1. 2 Tiles with Scuffs in Practice Room 2. Material remains in FAIR condition overall. No other changes as of this date.
02/10/2021	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RISK ASSESSMENT CATEGORY

COMMENTS

QTY
(APPROXIMATE)

PHYSICAL DAMAGE (P:)
WATER DAMAGE (W:)

02/18/2022	This Material is unchanged as of this date.
08/17/2022	Additional Damage Observed. 1 Missing Tile with Brown Mastic Exposed on North Wall of Stage. No other changes as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

MULTI-PURPOSE BUILDING

MUSIC ROOM, PRACTICE ROOMS (2), AND STAGE

WALL TILE MASTIC

1,410 SF

P: Less Than 5%

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

10/16/2008	Mastic/Adhesive for 1'x 1' Wall Tile. This Material is in GOOD condition as of this date.
12/01/2011	Quantity changed from 890 SF to 1,410 SF. No other changes as of this date.
03/30/2017	Damage Observed. <5% Physical Damage in the form of 2 Tiles Missing with Mastic Exposed on Stage. Material is in FAIR condition overall. No other changes as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	Additional Damage Observed. 6 Tiles with Holes in Music Room. 3 Tiles with Holes in Practice Room 1. 2 Tiles with Scuffs in Practice Room 2. Material remains in FAIR condition overall. No other changes as of this date.
02/10/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	Additional Damage Observed. 1 Missing Tile with Brown Mastic Exposed on North Wall of Stage. No other changes as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
RISK ASSESSMENT CATEGORY	COMMENTS			

MULTI-PURPOSE BUILDING

PRACTICE ROOM, AND BAND ROOM OFFICE

VINYL WALL COVER MASTIC

2,960 SF

P: Less Than 5%

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

03/06/2007	Mastic/Adhesive for Vinyl Wall Cover, (on 4'x8' Pressed Wood Wall Panel over Gypsum Wallboard System). This Material is in GOOD condition as of this date.
02/03/2020	This Material is unchanged as of this date.
08/28/2020	Damage Observed. <5% Physical Damage in the form of 1 SF of Torn and Missing Wall Cover around wall Outlet, on the West Wall in the Band Room. Material condition changed from GOOD to FAIR overall. Friability updated from Non-Friable to Friable. No other changes as of this date.
02/10/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

MULTI-PURPOSE BUILDING

STAGE, BAND ROOM, MULTI-PURPOSE ROOM, AND PRACTICE ROOM

CEILING TILE

8,500 SF

P: Less Than 5%

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

09/12/2005	1'x1' Ceiling Tile. This Material is in GOOD condition as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SIERRAMONT MIDDLE SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RISK ASSESMENT CATEGORY

COMMENTS

QTY
(APPROXIMATE)

PHYSICAL DAMAGE (P:)
WATER DAMAGE (W:)

08/16/2023	Damage Observed. <5% Physical Damage in the form of 5 EA Tiles with Water Stains, 1.5 EA Tiles missing with Brown Mastic Exposed, 1 EA Tile is Loose and 1 SF of Black Mold in Multi-purpose Room. Material changed from Non-Friable to Friable. Material condition changed from GOOD to FAIR overall. No other changes as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

MULTI-PURPOSE BUILDING

STAGE, BAND ROOM, MULTI-PURPOSE ROOM, AND PRACTICE ROOM

CEILING TILE MASTIC

8,500 SF

P: Less Than 5%

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

09/12/2005	Mastic/Adhesive for 1'x1' Ceiling Tile. This Material is in GOOD condition as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	Damage Observed. <5% Physical Damage in the form of 5 EA Tiles with Water Stains, 1.5 EA Tiles missing with Brown Mastic Exposed, 1 EA Tile is Loose and 1 SF of Black Mold in Multi-purpose Room. Material changed from Non-Friable to Friable. Material condition changed from GOOD to FAIR overall. No other changes as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.


End Of Report, Total Of 12 Pages

Sierramont

Middle School

3155 Kimlee Dr, San Jose

Supply Containers

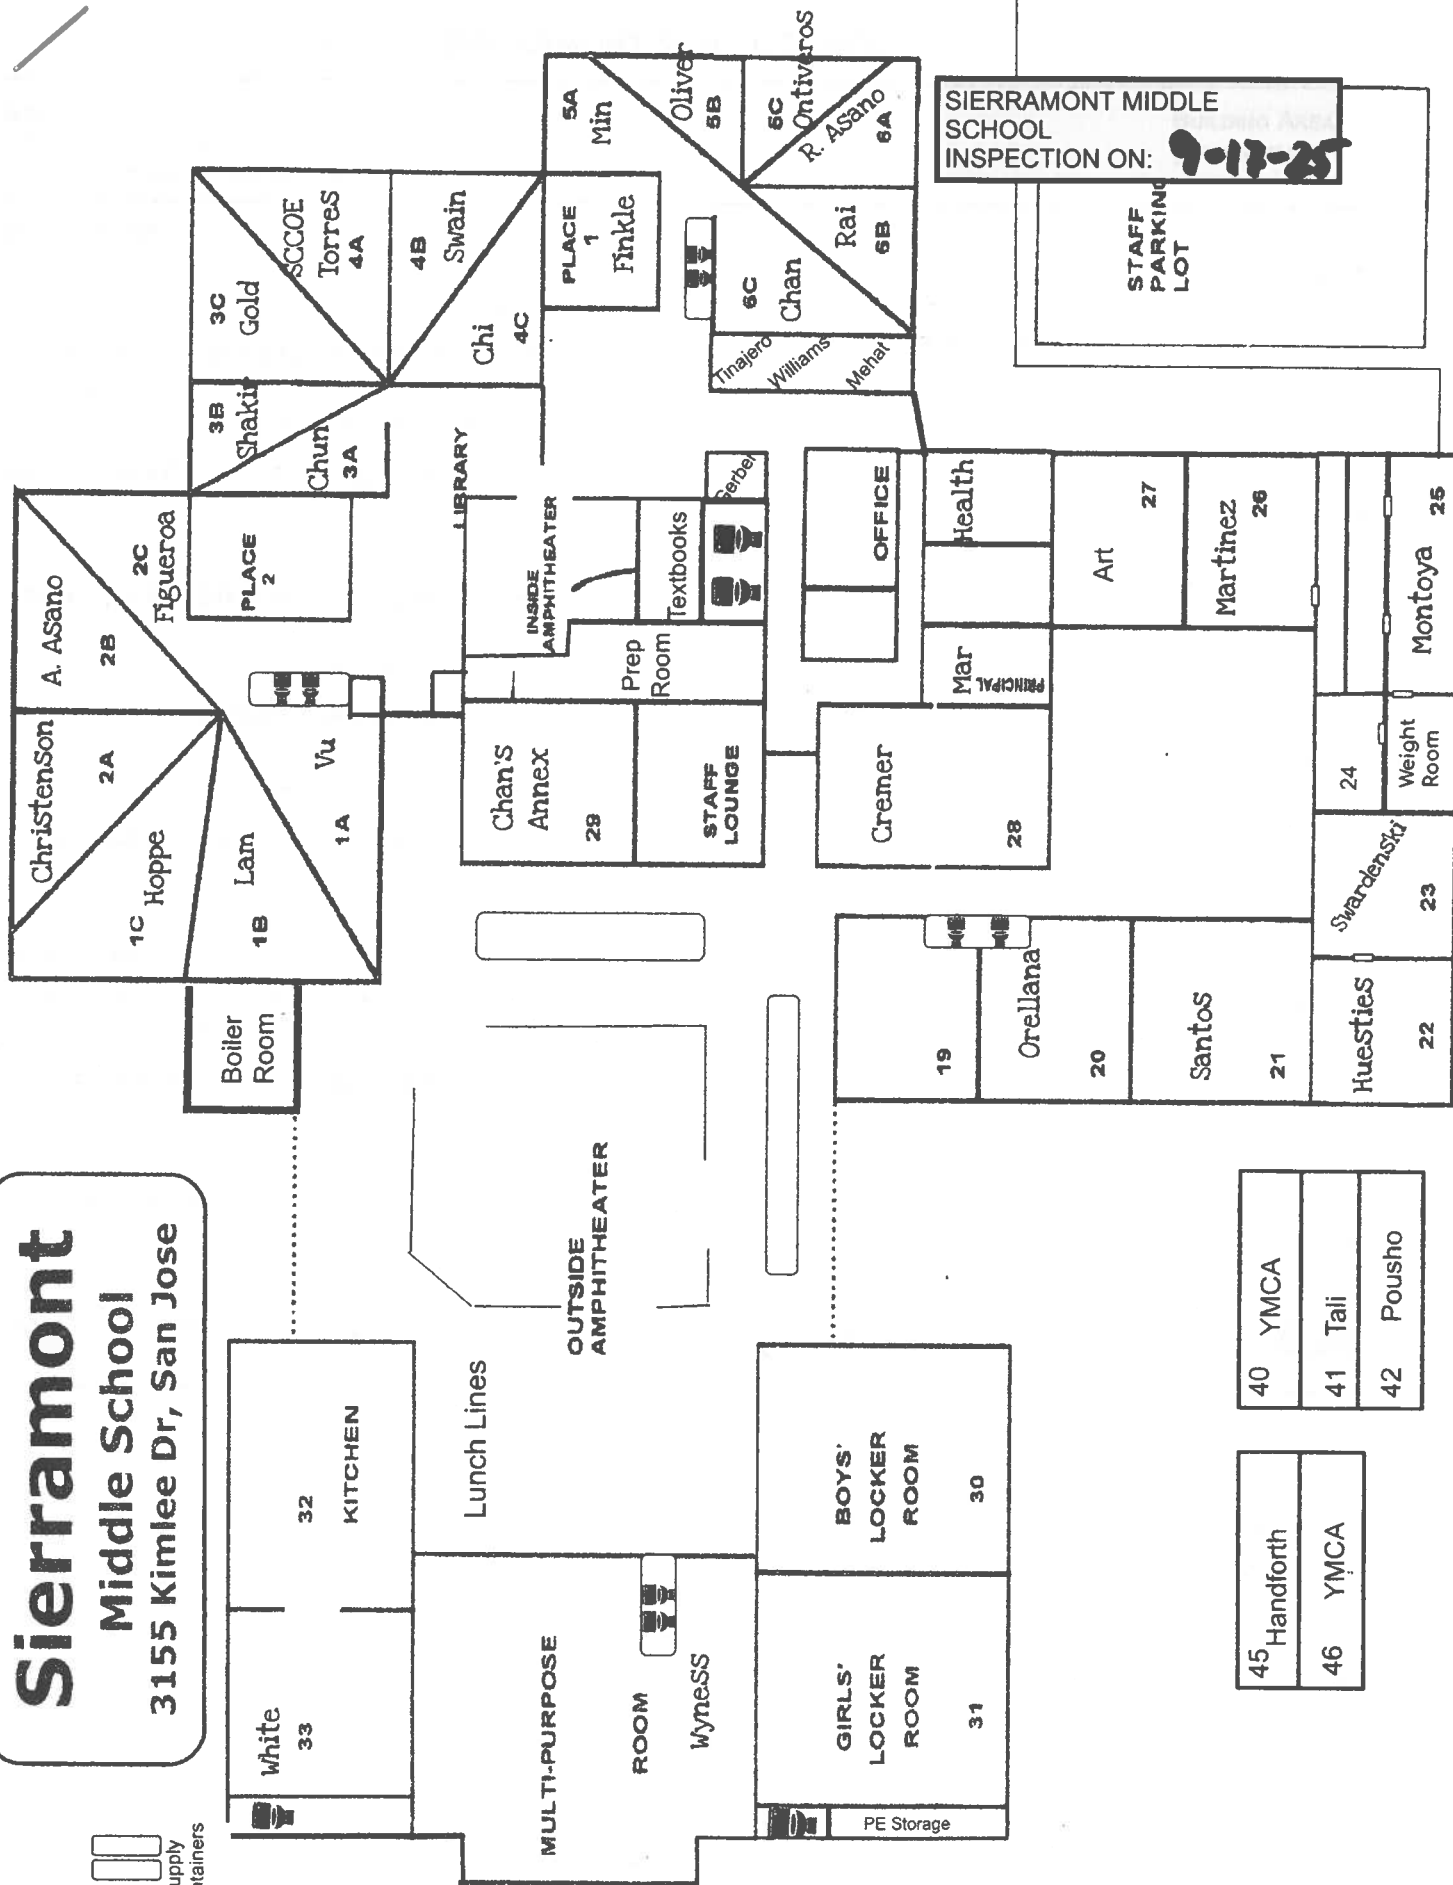

SIERRAMONT MIDDLE SCHOOL
INSPECTION ON: 9-17-25

STAFF PARKING LOT



40	YMCA
41	Tali
42	Pousho

45	Handforth
46	YMCA

Sierramont

Middle School

3155 Kimlee Dr, San Jose

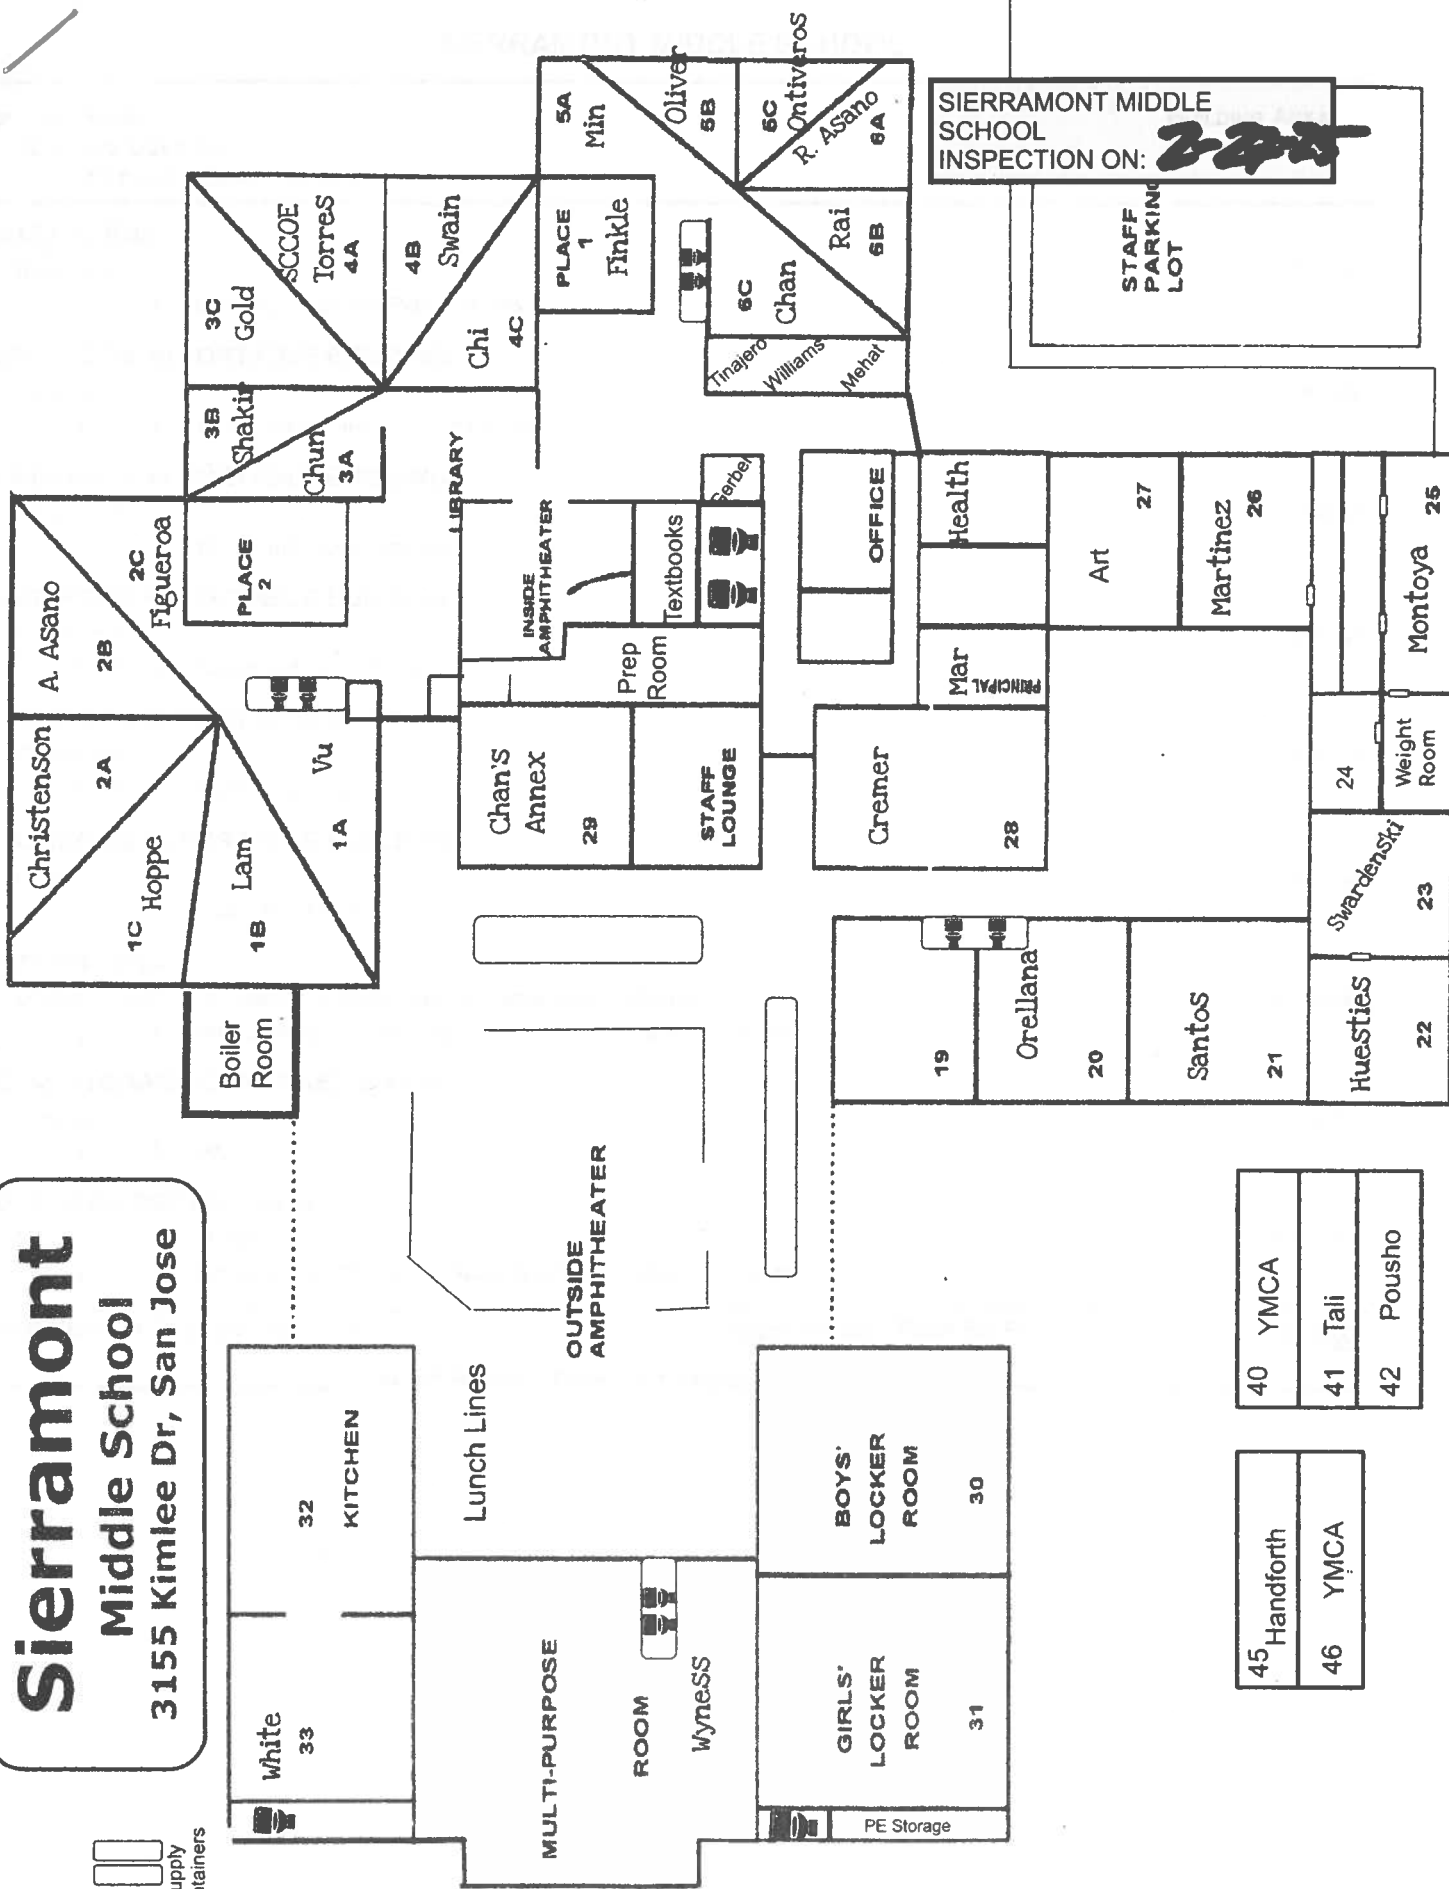


SIERRAMONT MIDDLE SCHOOL
INSPECTION ON: **2-2-11**


STAFF
PARKING
LOT

Sierramont

Middle School
3155 Kimlee Dr, San Jose




Supply
Containers

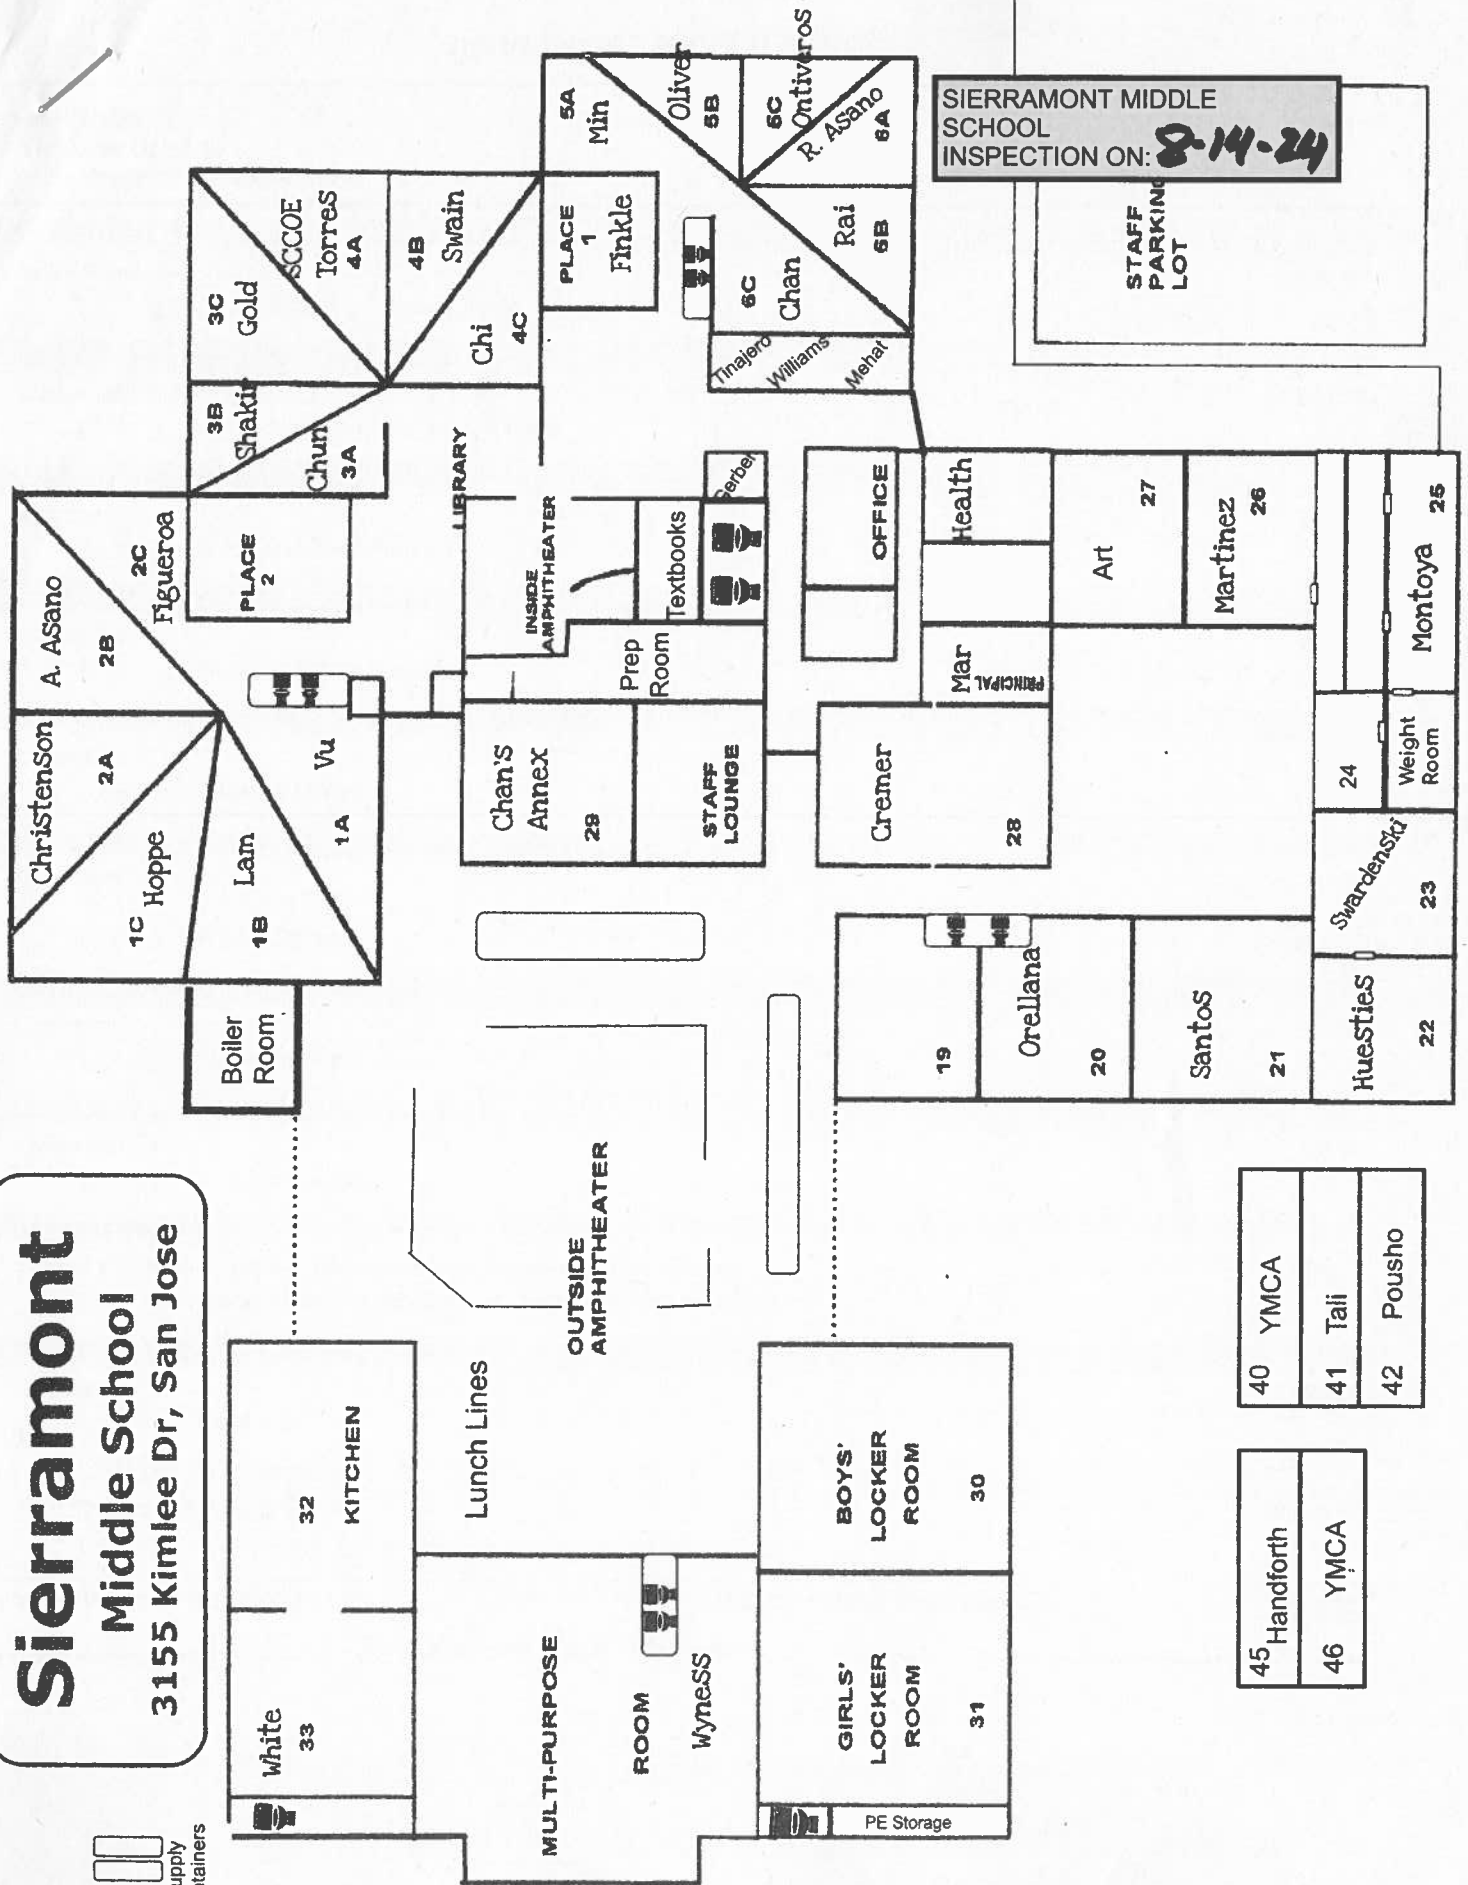


Sierramont

Middle School
3155 Kimlee Dr, San Jose

Supply Containers

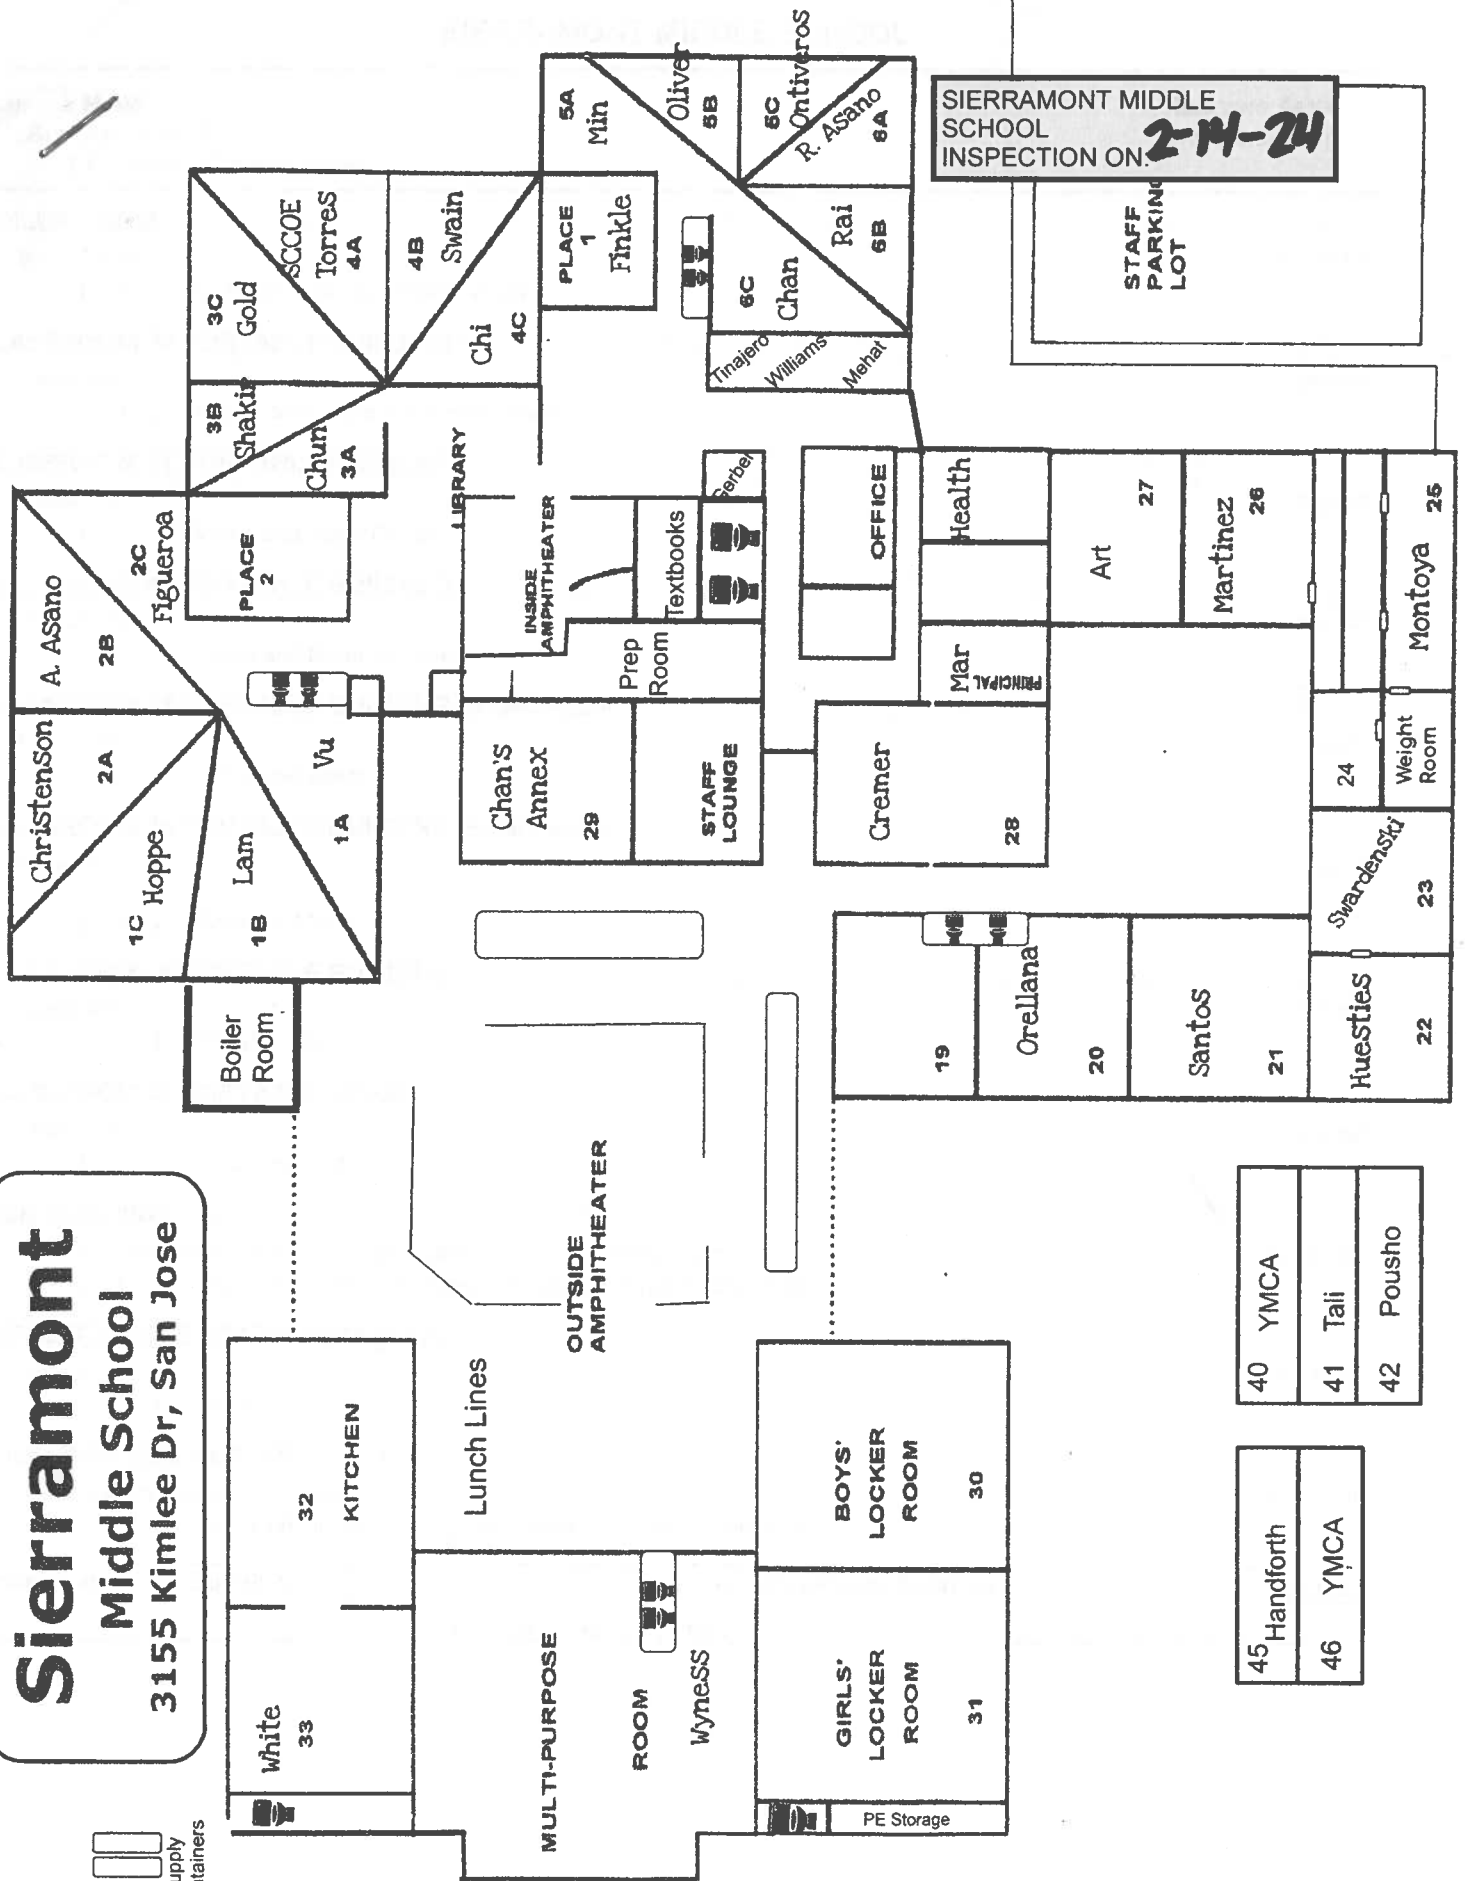

SIERRAMONT
MIDDLE SCHOOL
 3155 KIMLEE DR. SJ 95132
 2013-14

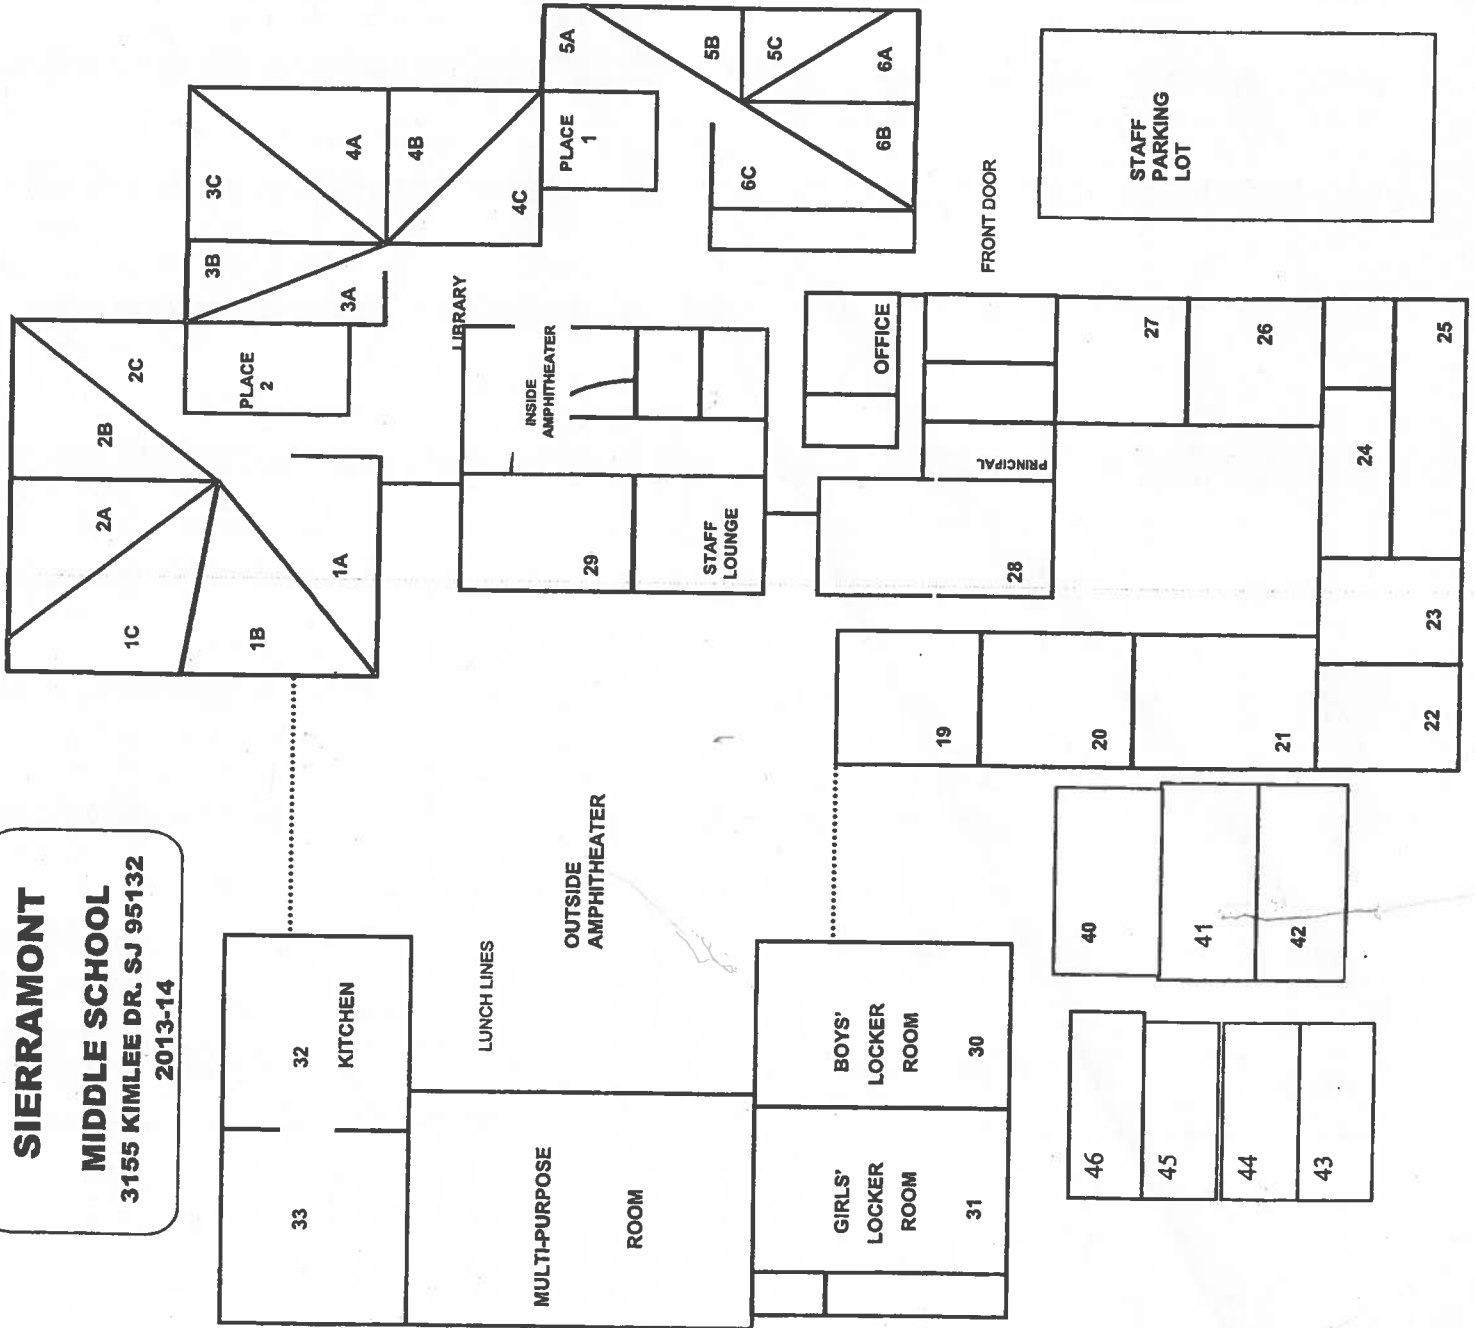

Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

SIERRAMONT MIDDLE SCHOOL
 INSPECTED ON 08-16-2023

SIERRAMONT


MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 2/15/23

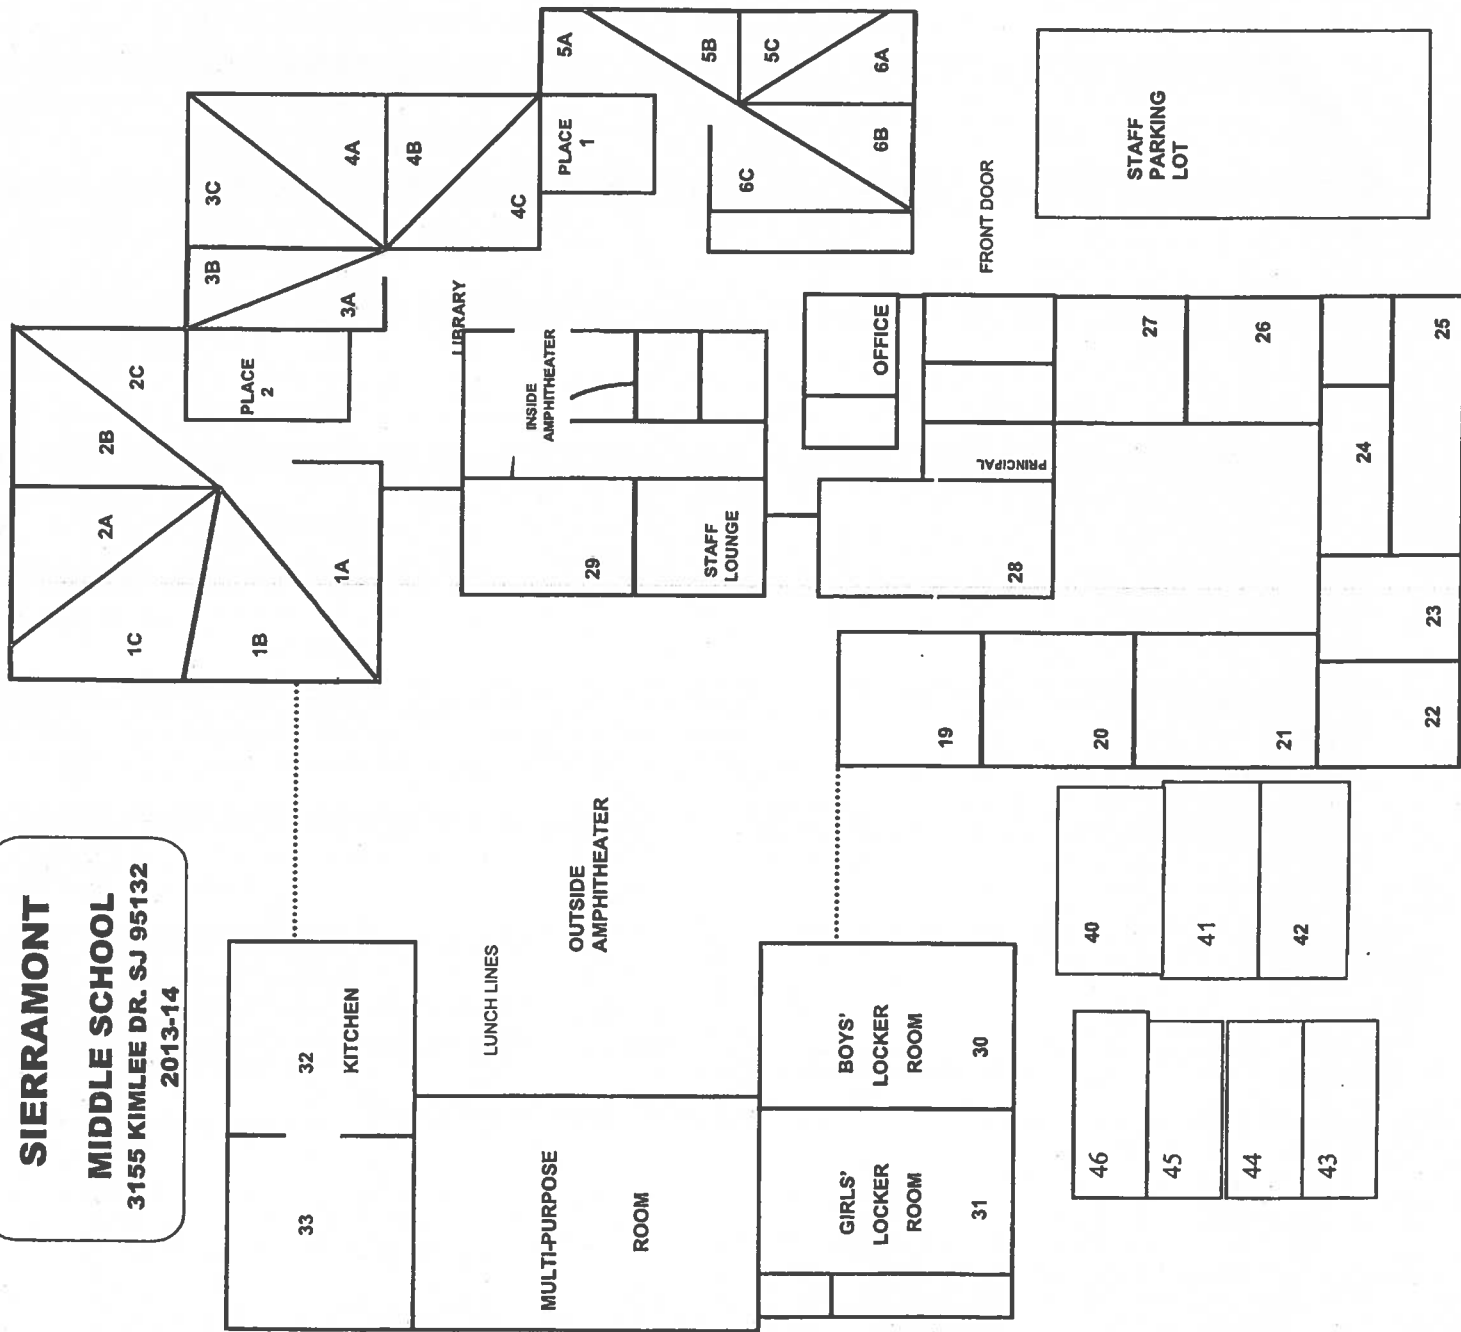


SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

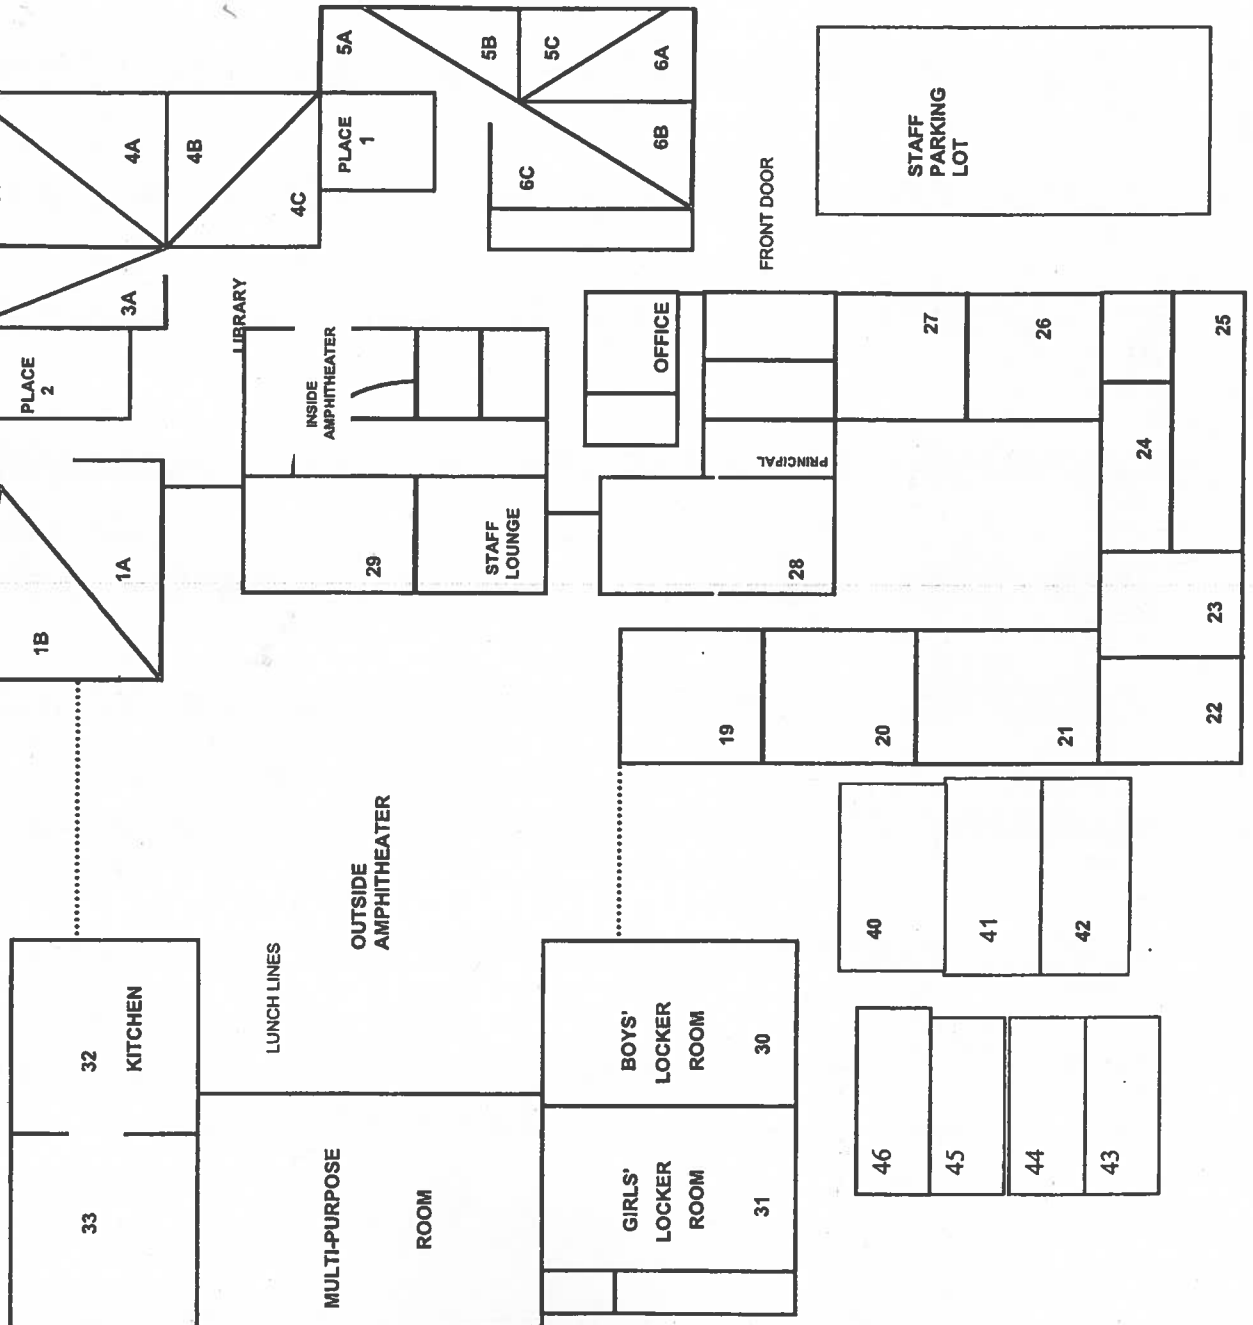


SIERRAMONT MIDDLE SCHOOL INSPECTED ON: 08-17-2022	
Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

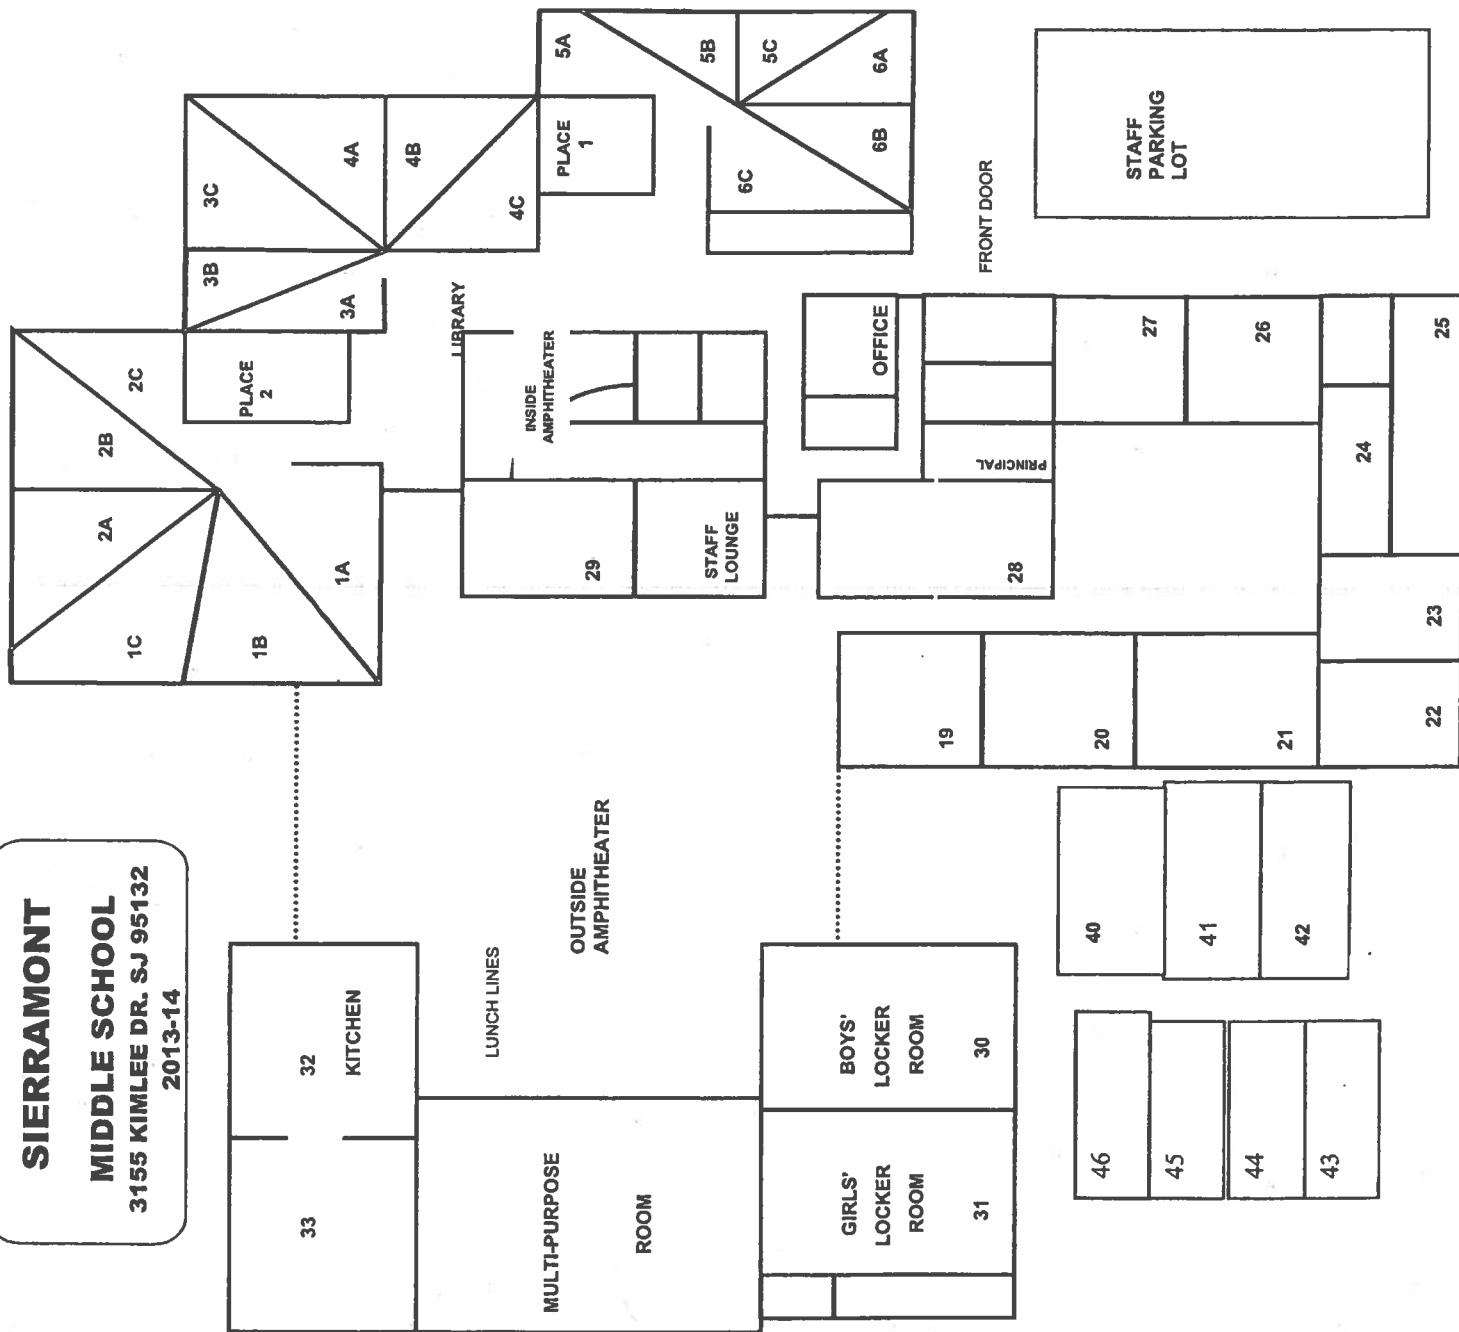

SIERRAMONT MIDDLE SCHOOL

INSPECTED ON: 02-18-2022


Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figuerola
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

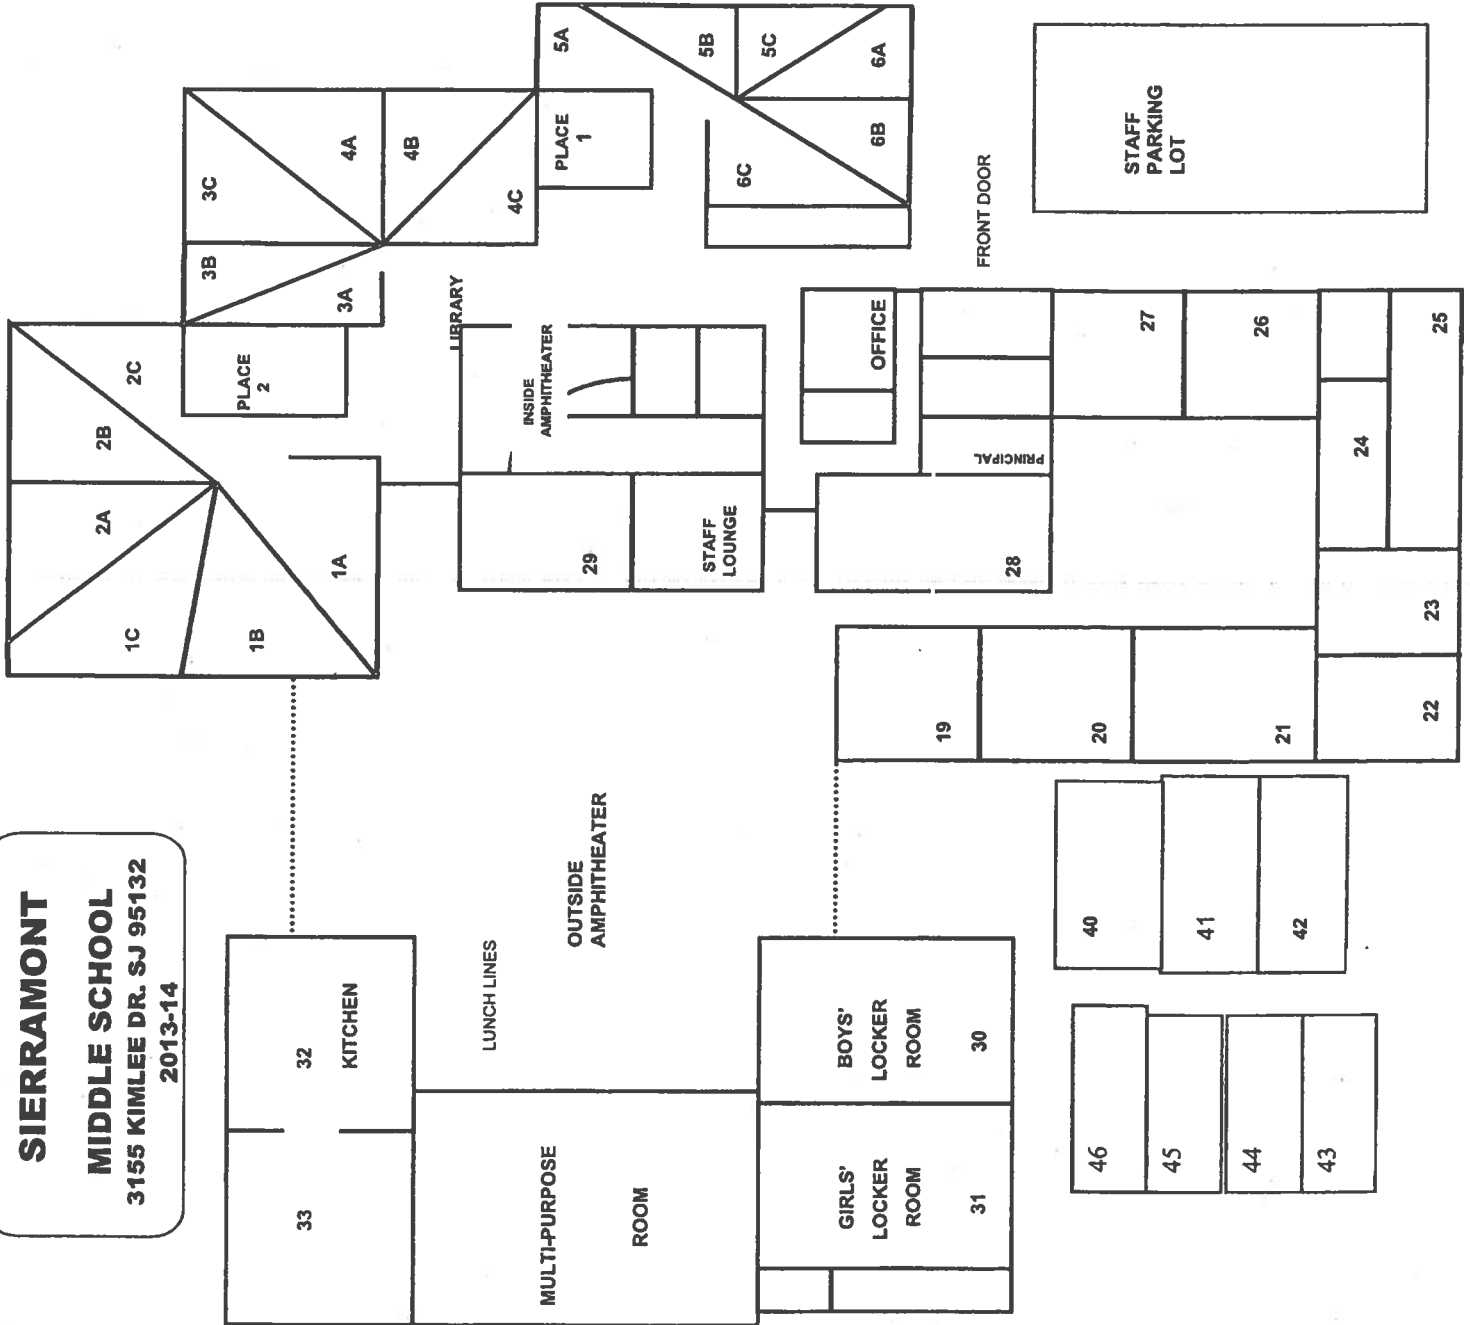


SIERRAMONT MIDDLE SCHOOL	
INSPECTED ON: 8/11/21	
Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

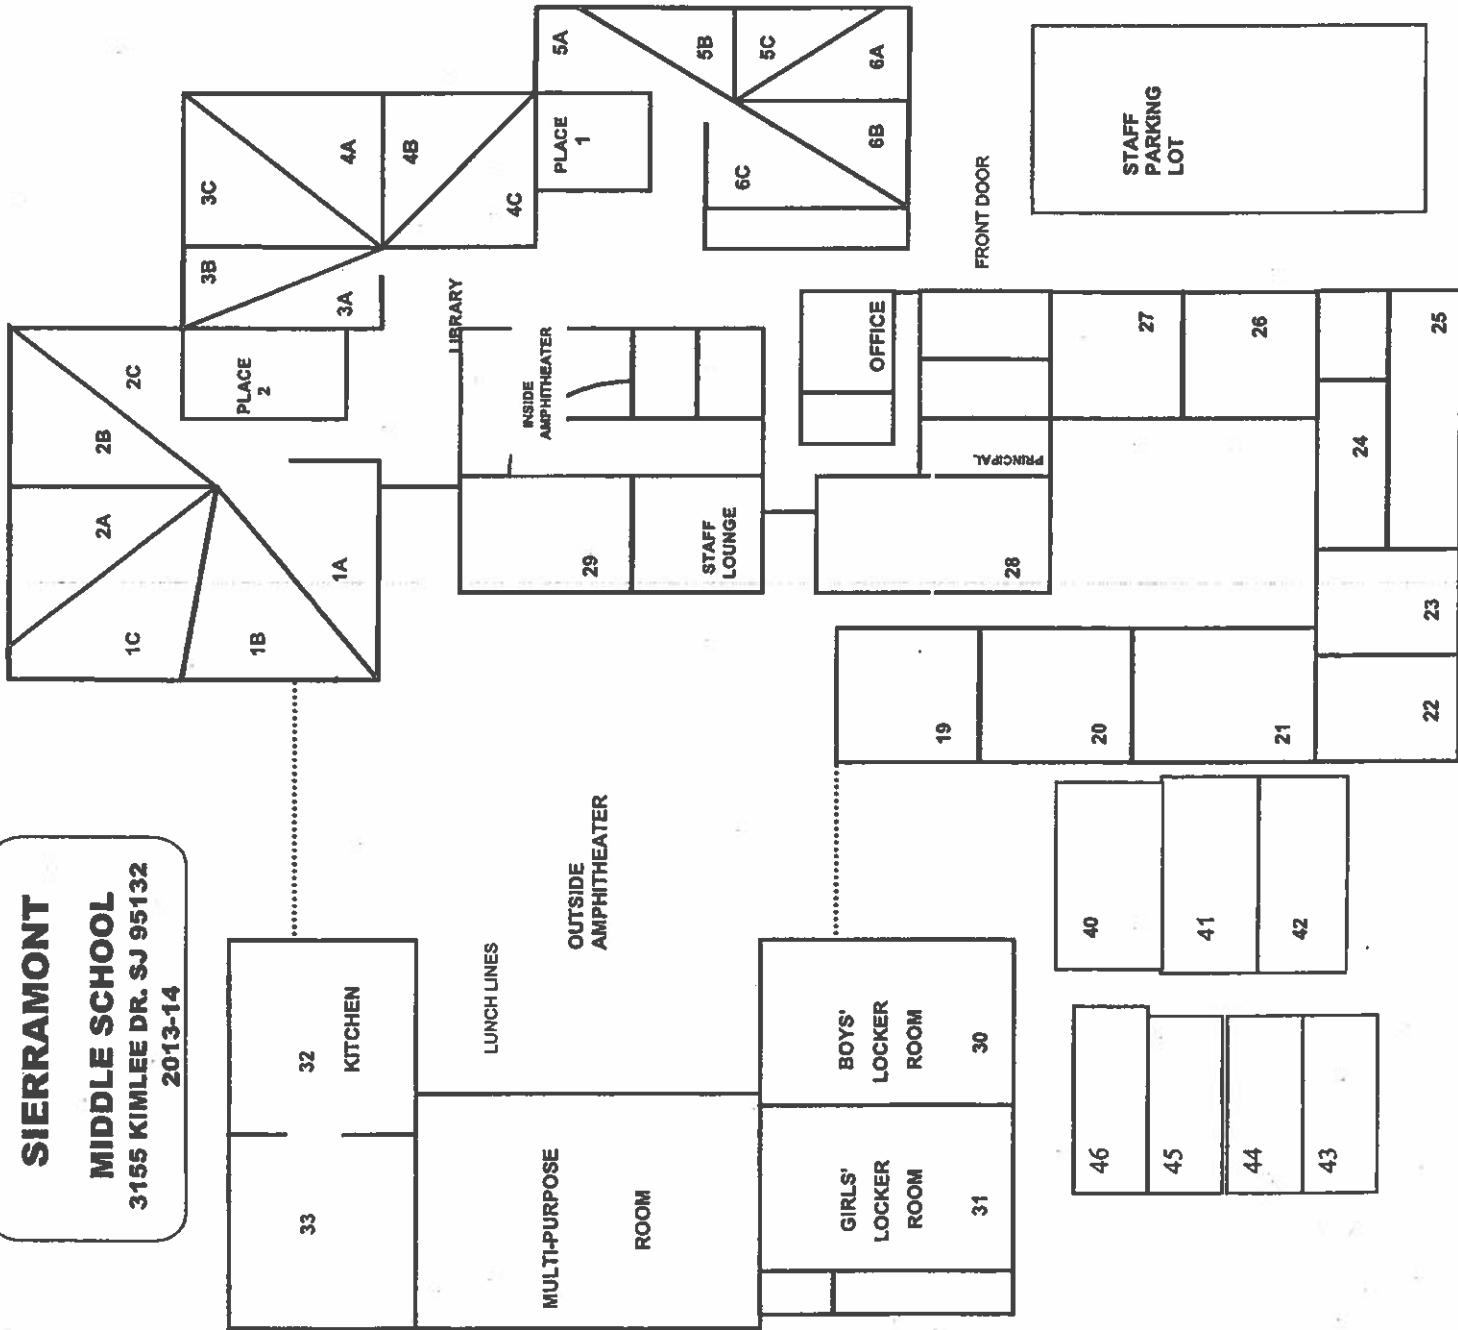


Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

SIERRAMONT MIDDLE SCHOOL

INSPECTED ON: 2/10/21

SIERRAMONT
MIDDLE SCHOOL
 3155 KIMLEE DR. SJ 95132
 2013-14

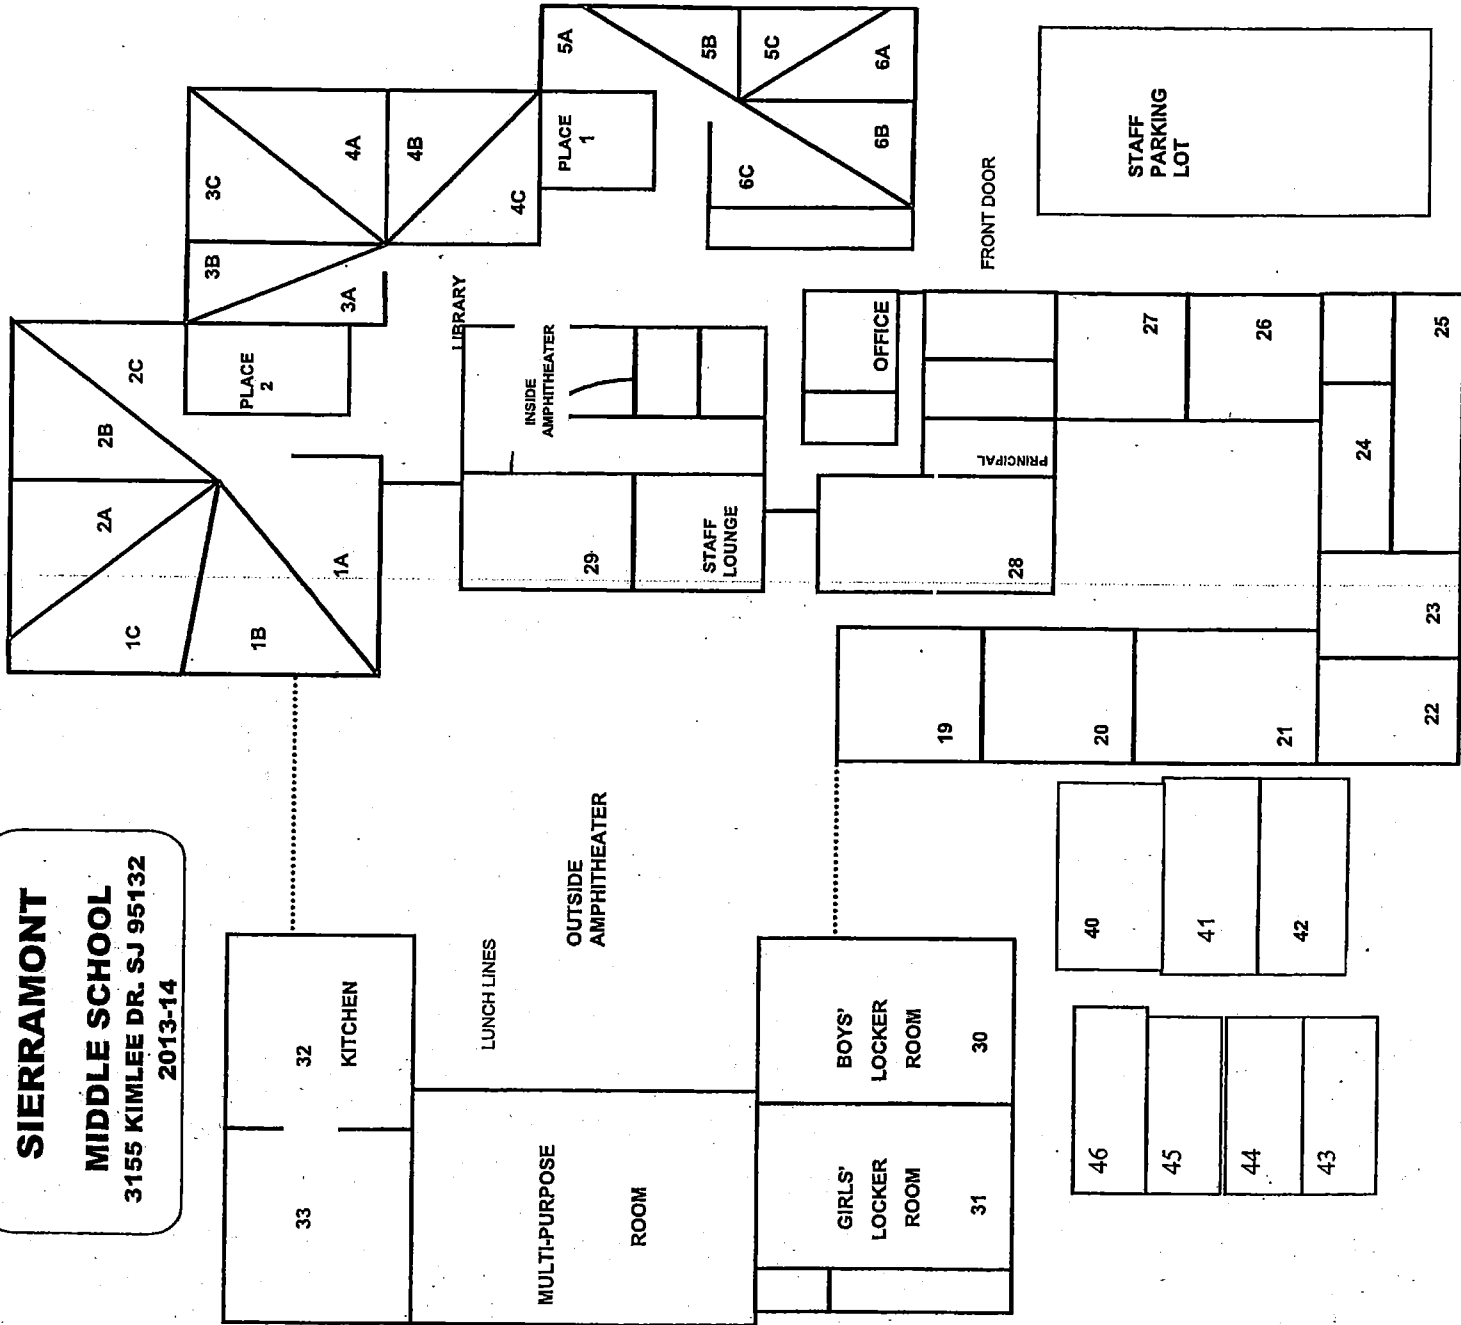

Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

SIERRAMONT MIDDLE SCHOOL
 INSPECTED ON: 8/28/20

SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132


2013-14

SIERRAMONT MIDDLE SCHOOL

INSPECTED ON:

2.3.2020

Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

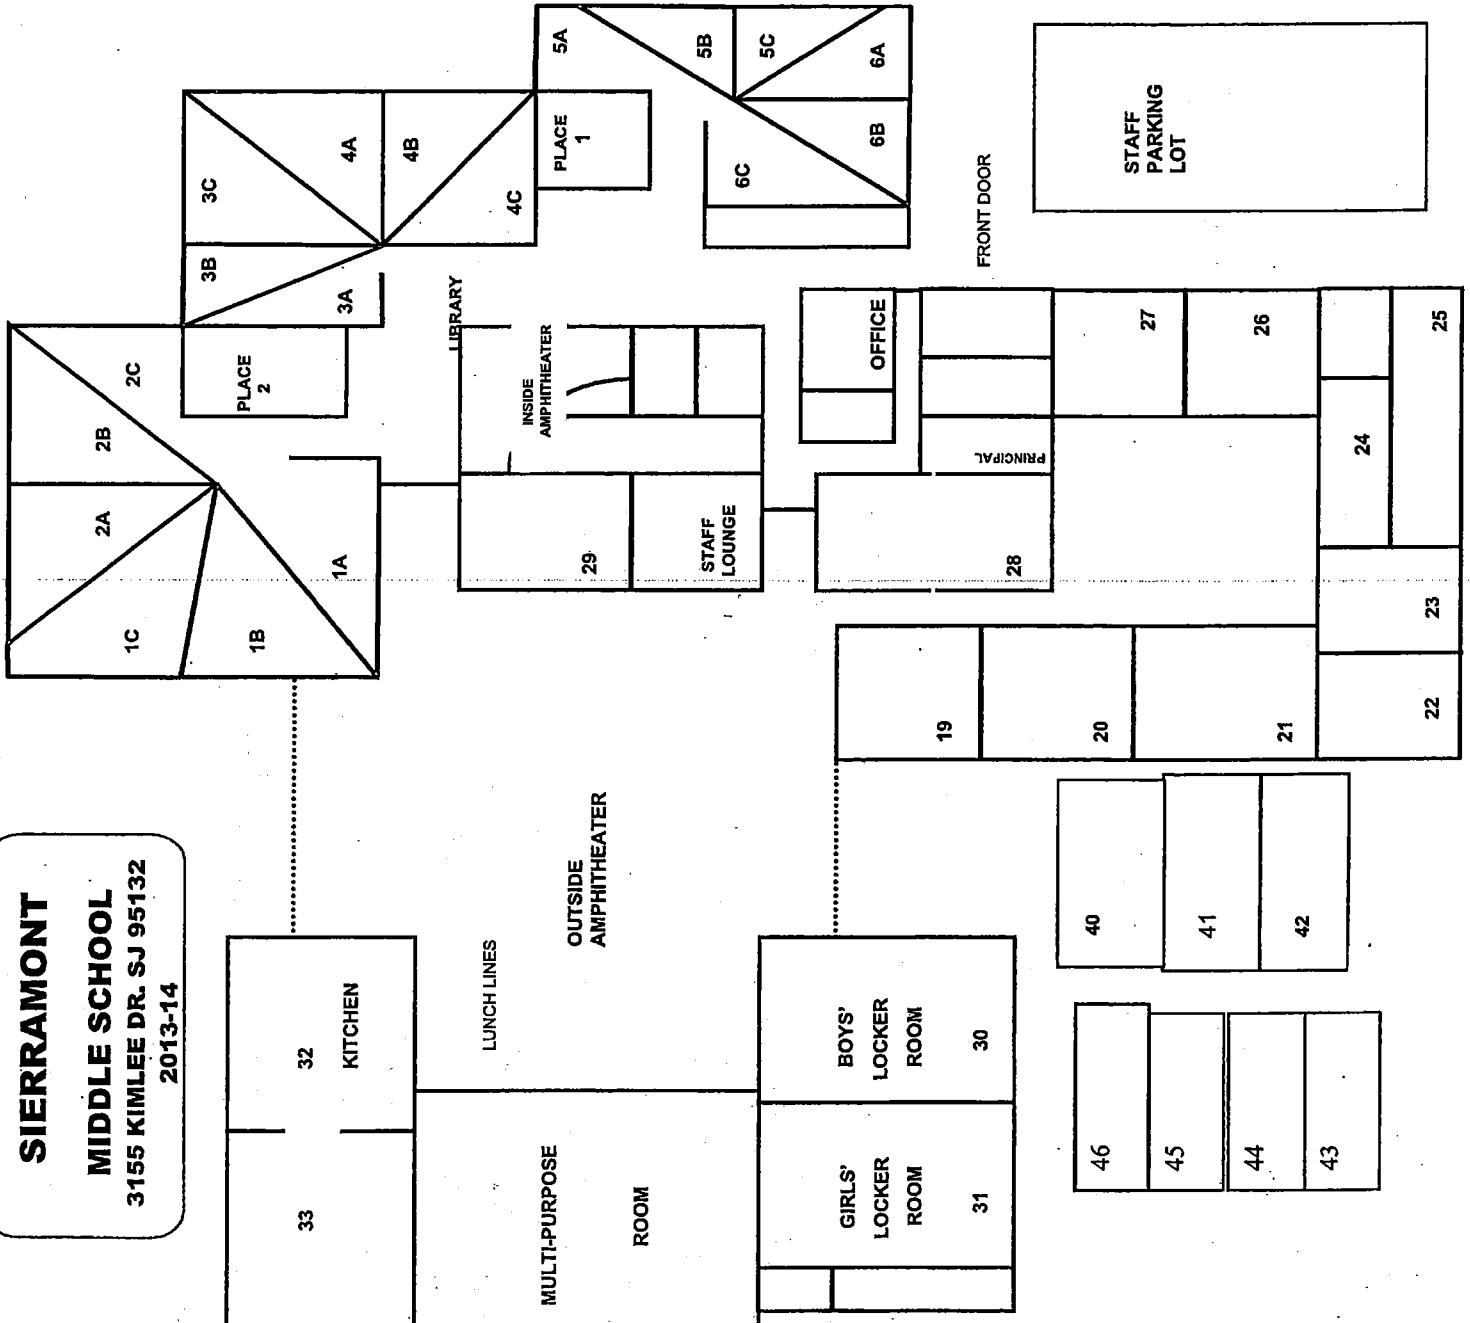


SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

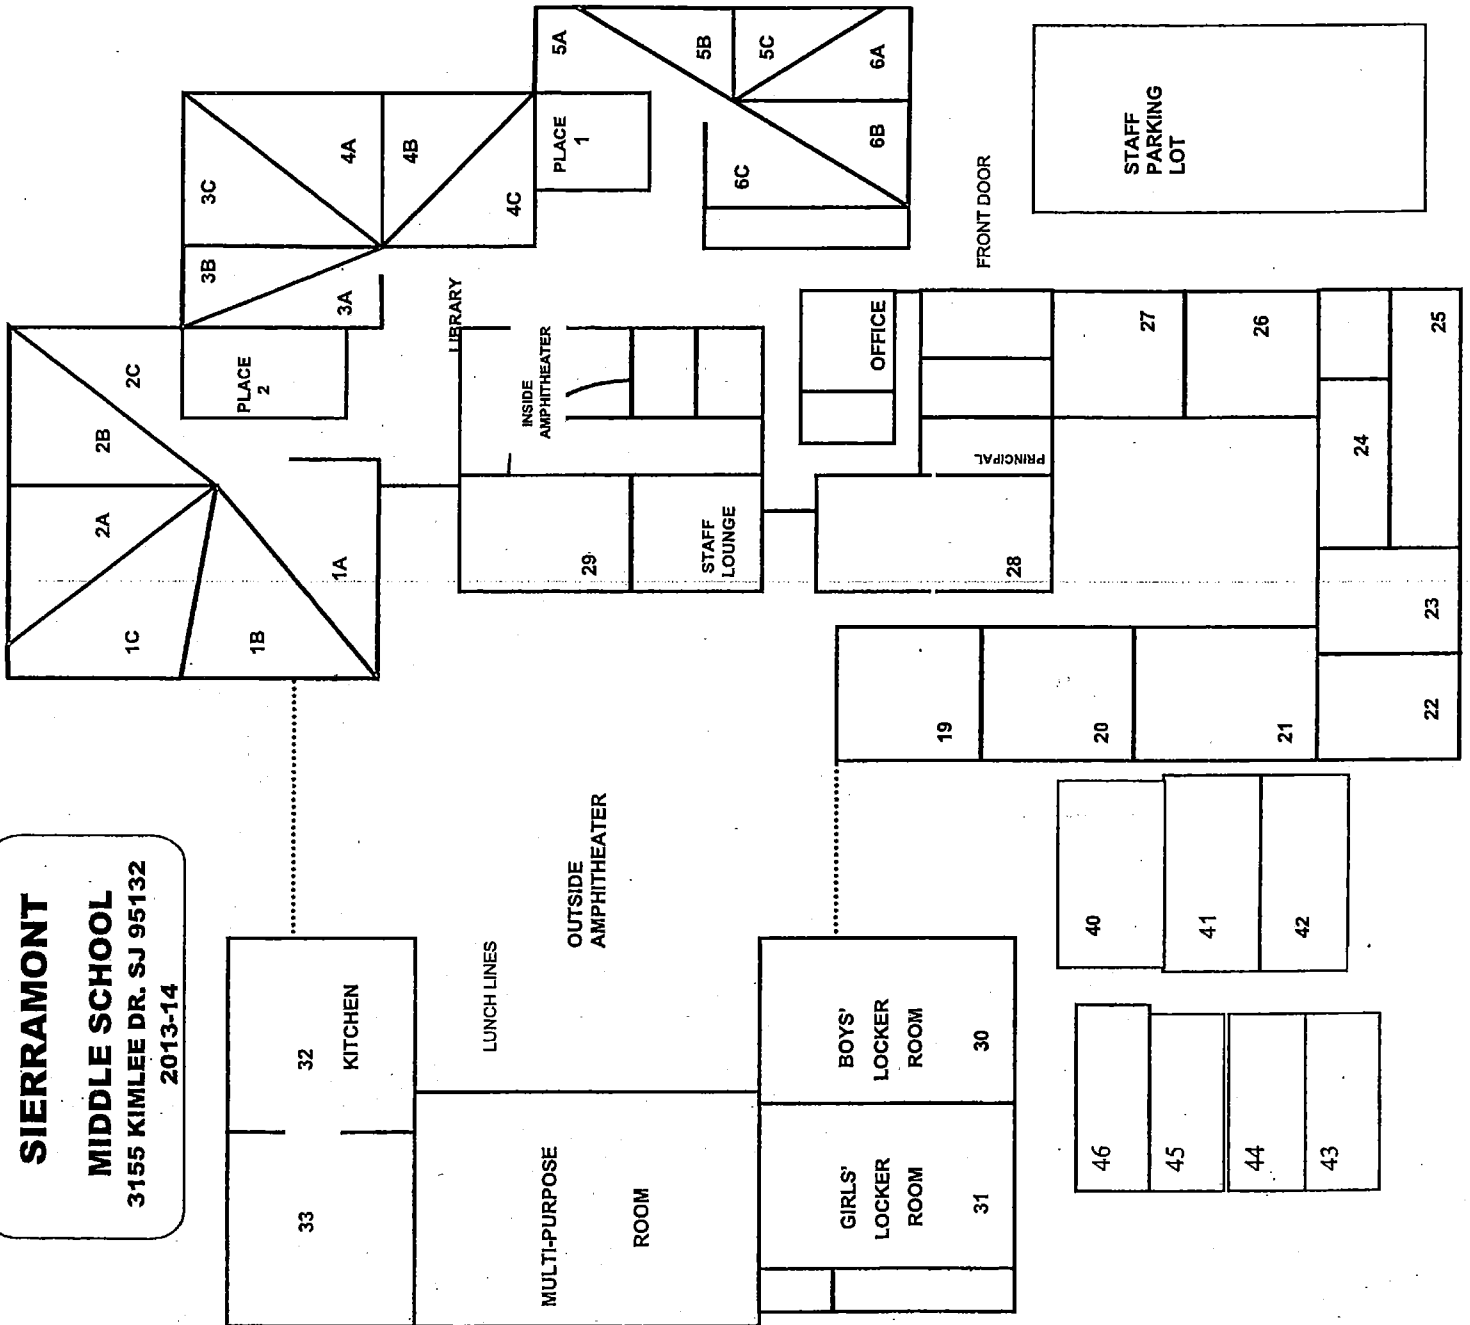

Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

SIERRAMONT MIDDLE SCHOOL


INSPECTED ON: 8-14-19

SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

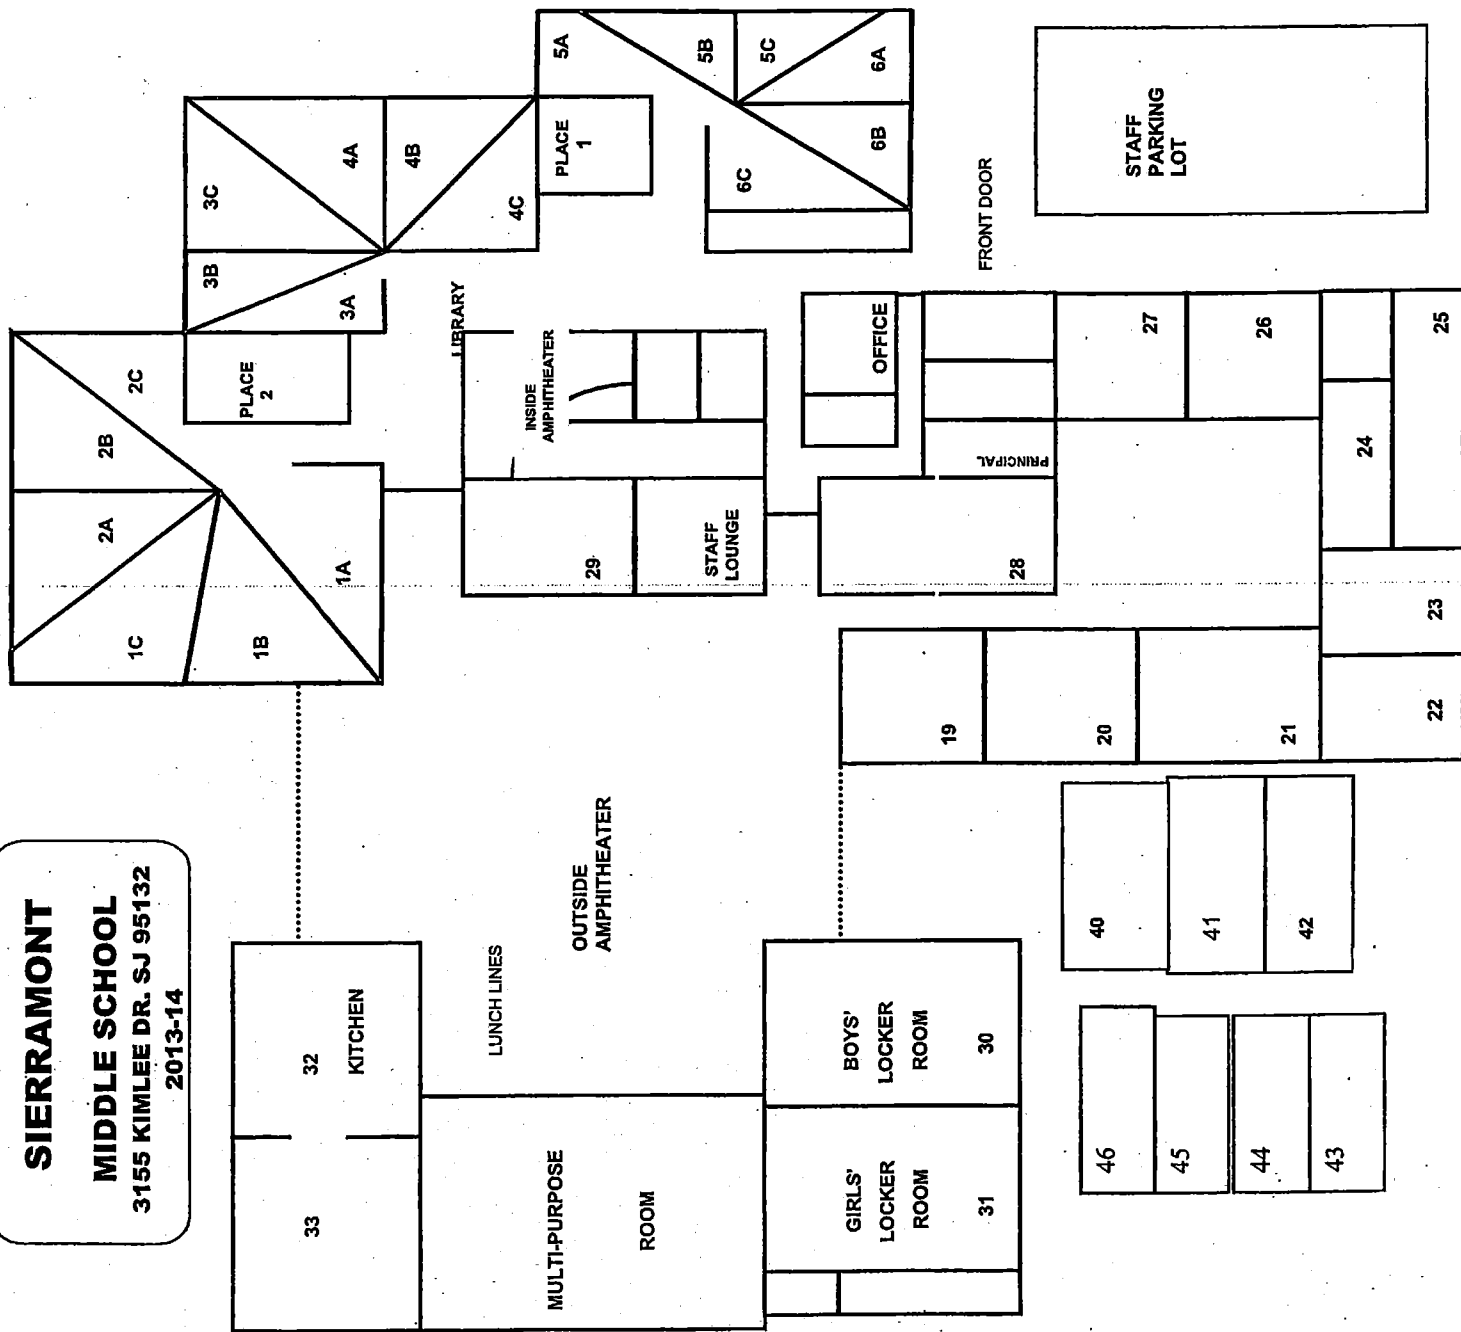

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 02-06-2019


Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

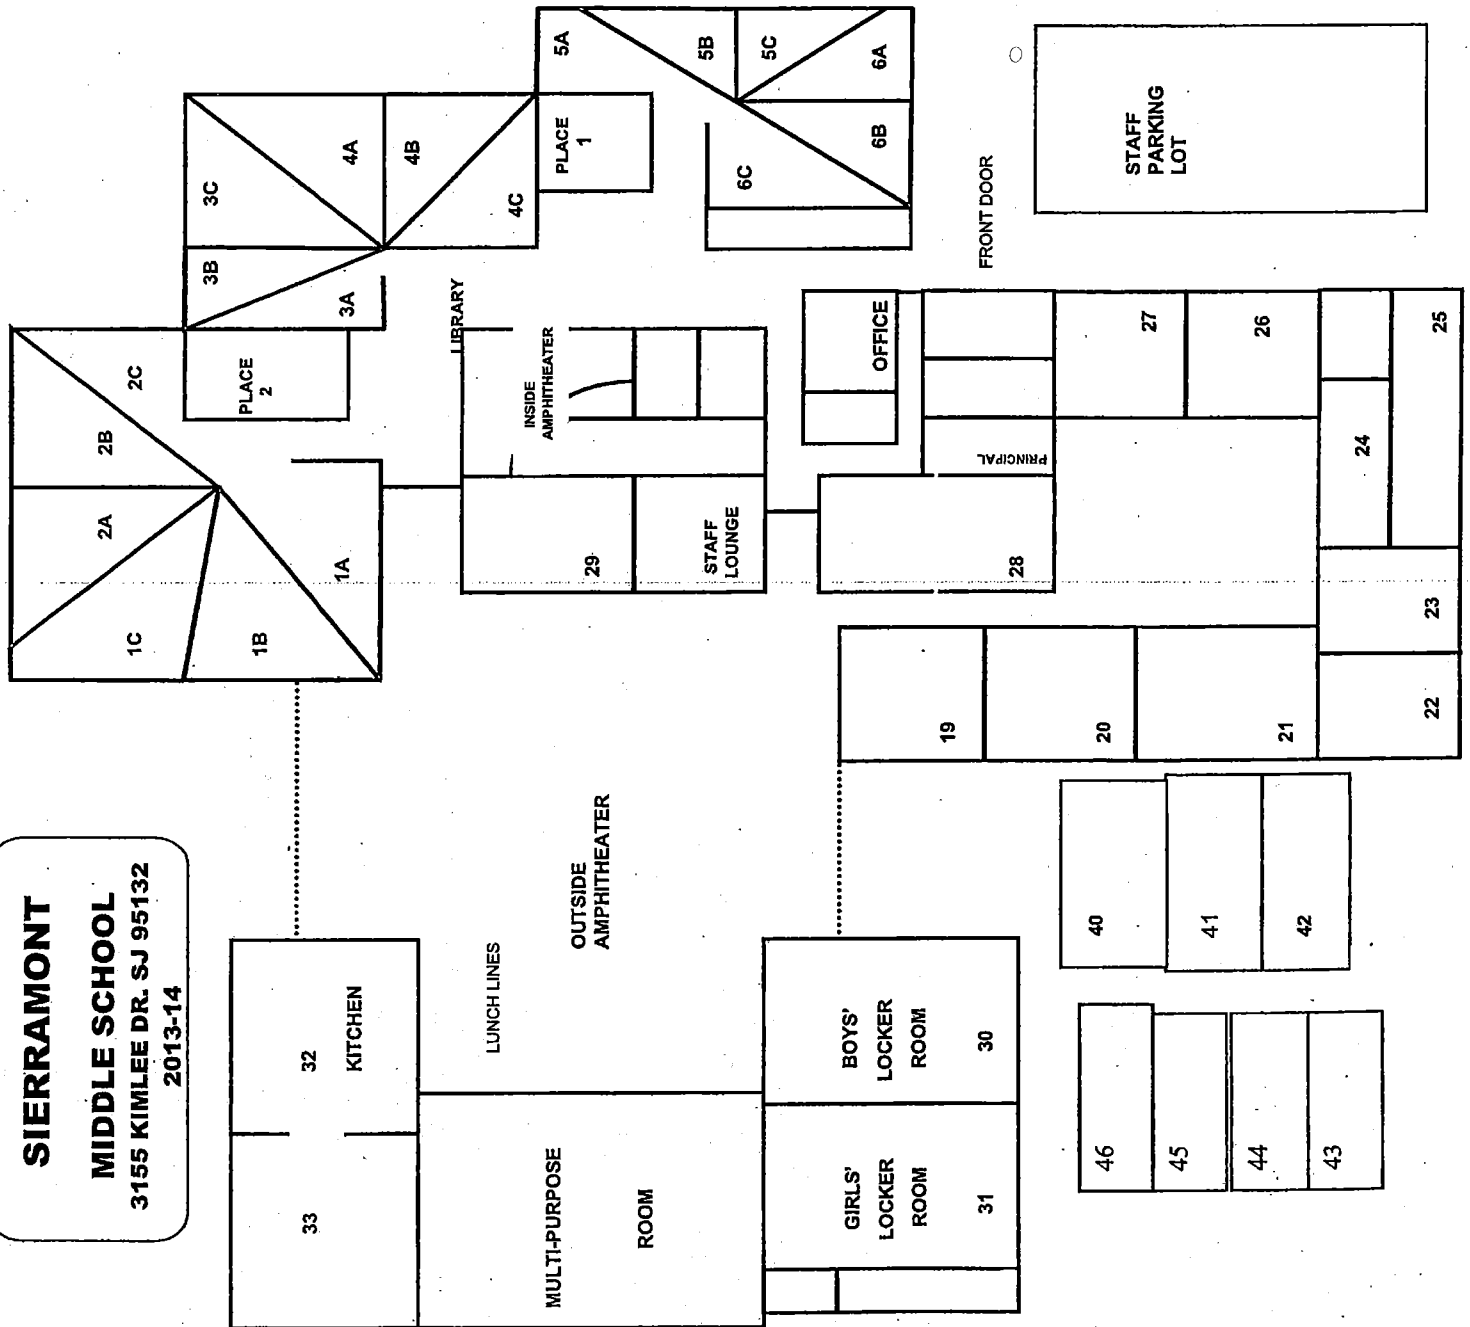


SIERRAMONT MIDDLE SCHOOL	
INSPECTED ON: 8/15/18	
Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

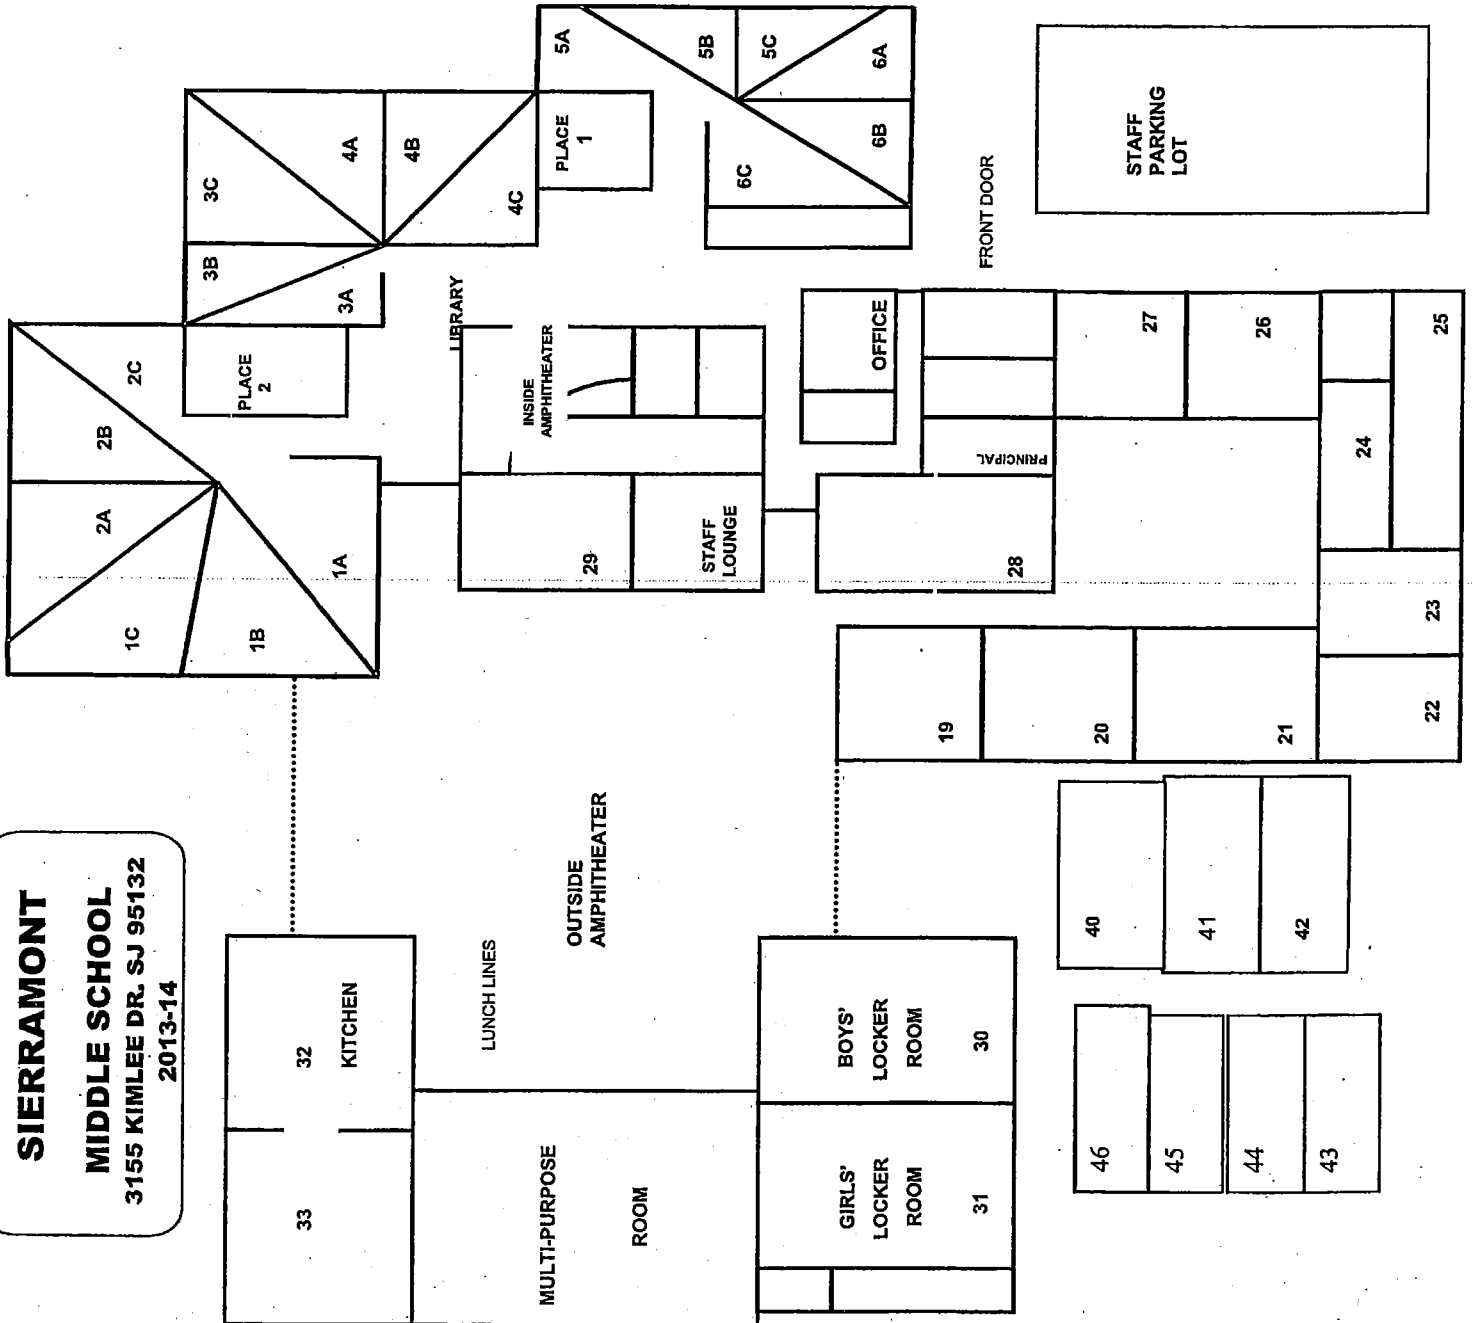


SIERRAMONT MIDDLE SCHOOL	
INSPECTED ON: 2/4/8	
Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

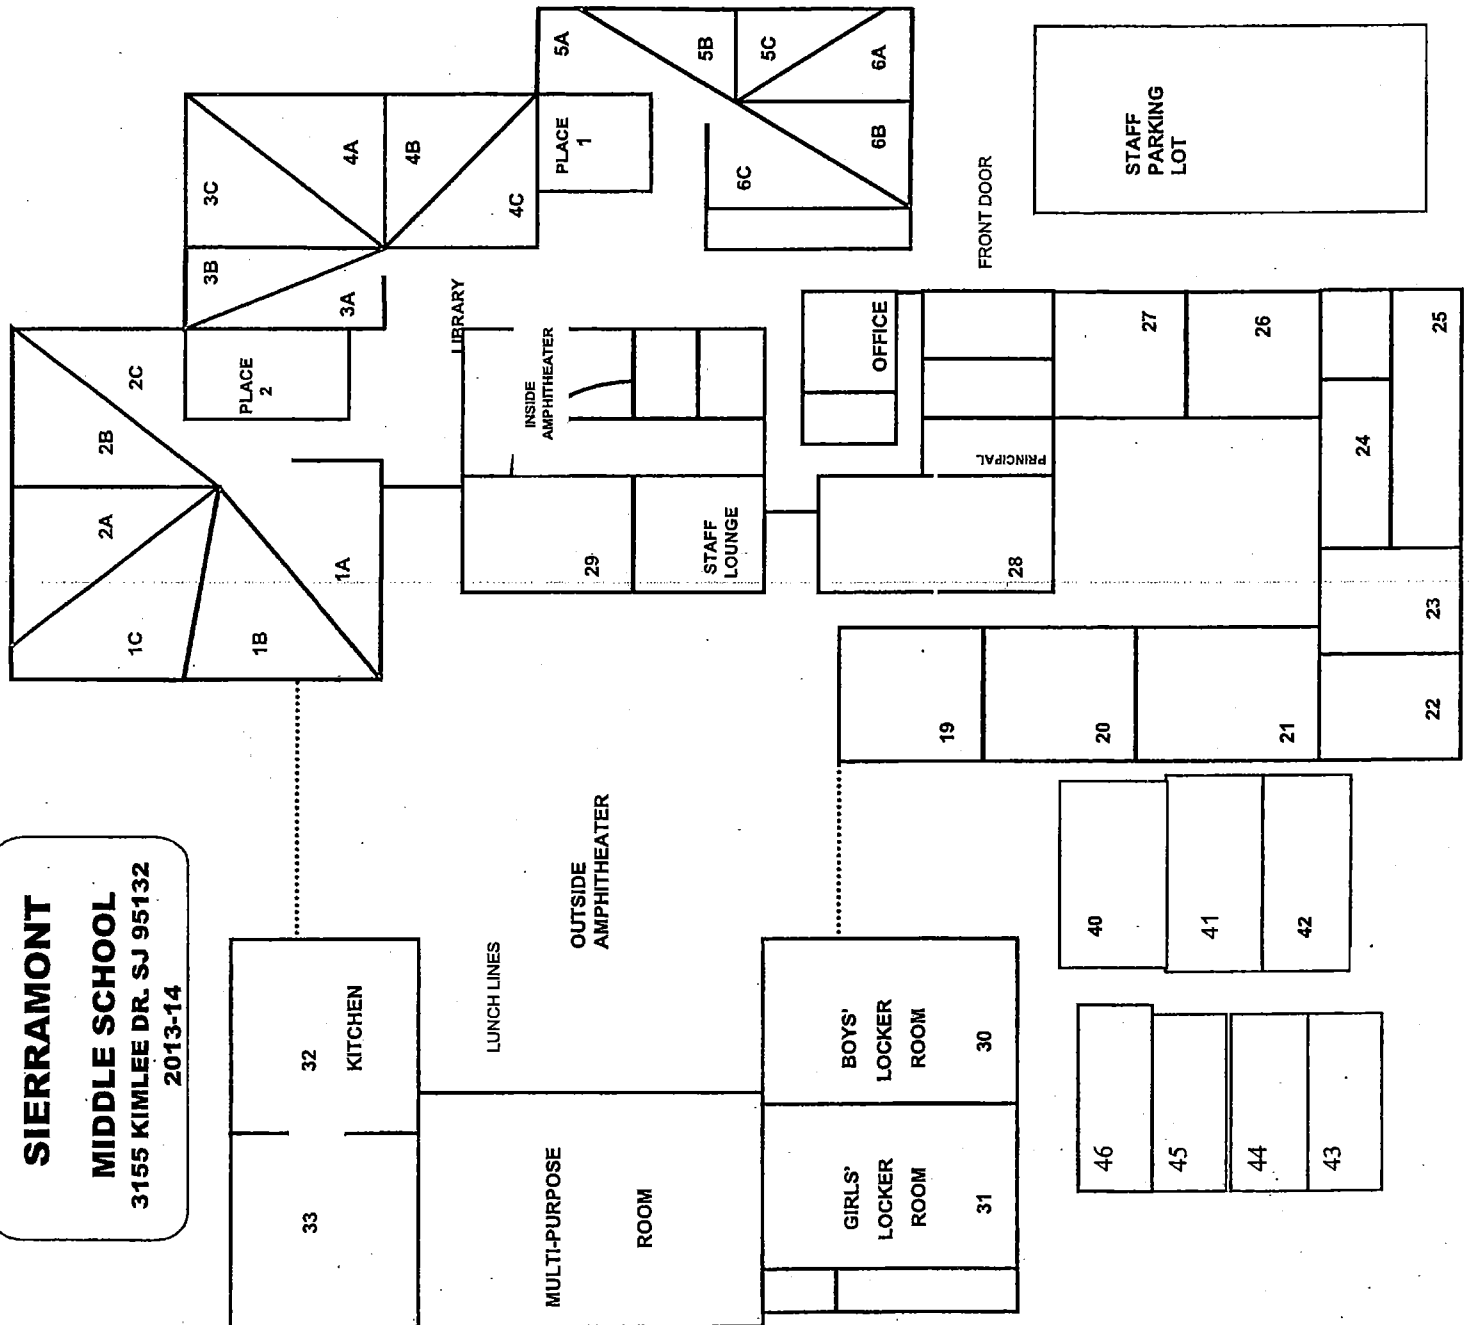

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 9/1/17

Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cramer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh





SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132


2013-14

22

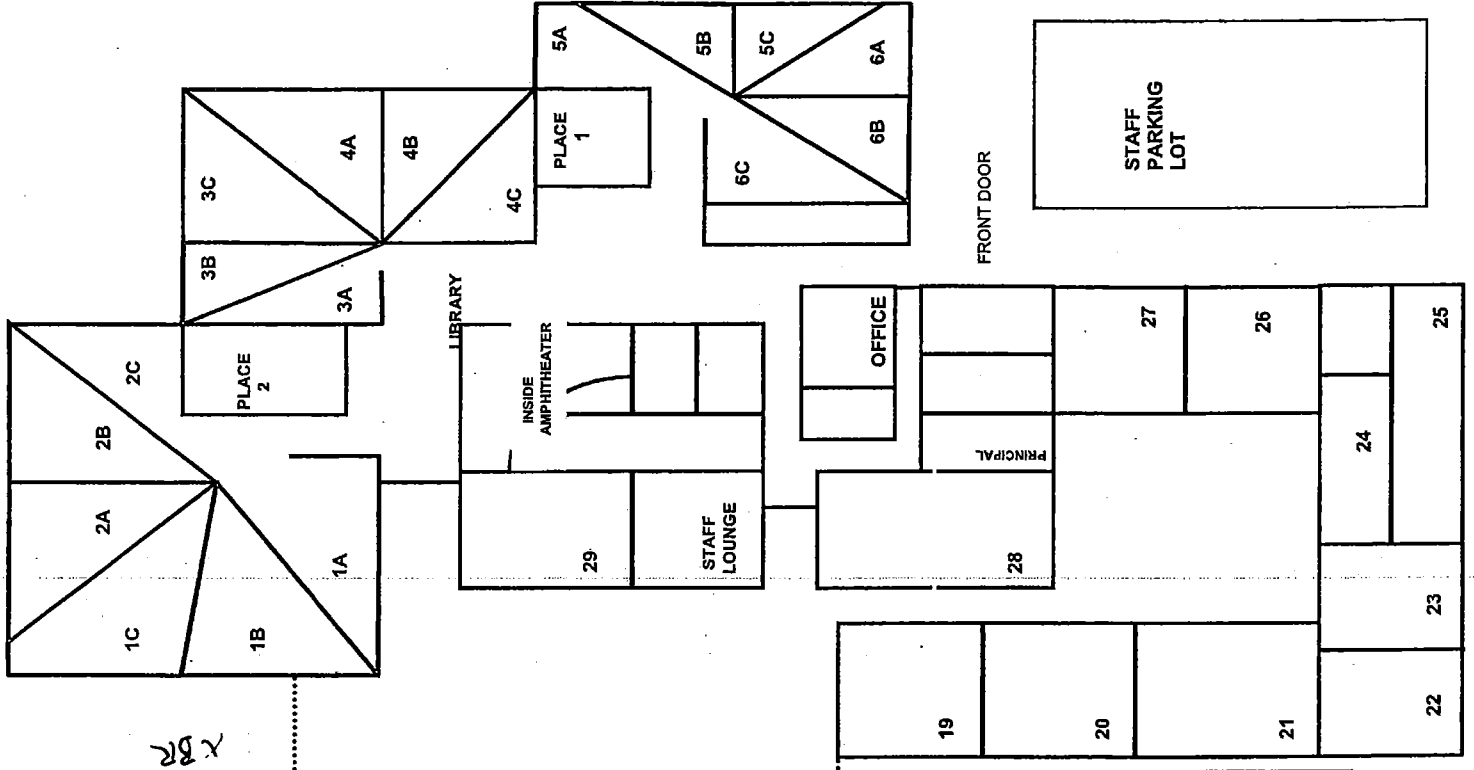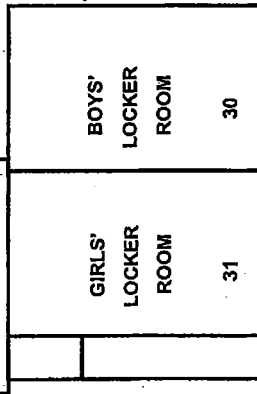

Room	Teacher
1A	Vu
1B	Gairaud
1C	Hoppe
2A	Christensen
2B	Ross
2C	Raisch
Place 2	Ridley
3A	Chun
3B	Shakir
3C	Gold
4A	Parodi
4B	Da Silva
4C	Chi
Place 1	Asano
5A	Liu
5B	Palla
5C	Ontiveros
6A	Perry
6B	Rai
6C	Johnson
19	Pfeiffer
20	Edens
21	Wiebe
22	Huesties
23	Singh
25	Mahal
26	Hurley
27	Lashbrook
28	Cremmer
29	Arensberg
30	Boy PE
31	Girls PE
33	McVeigh
40	Figueroa
41	Sen
42	Pousho
43	Davis
44	Lam
45	Chan
46	Balsbaugh

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 3/30/17

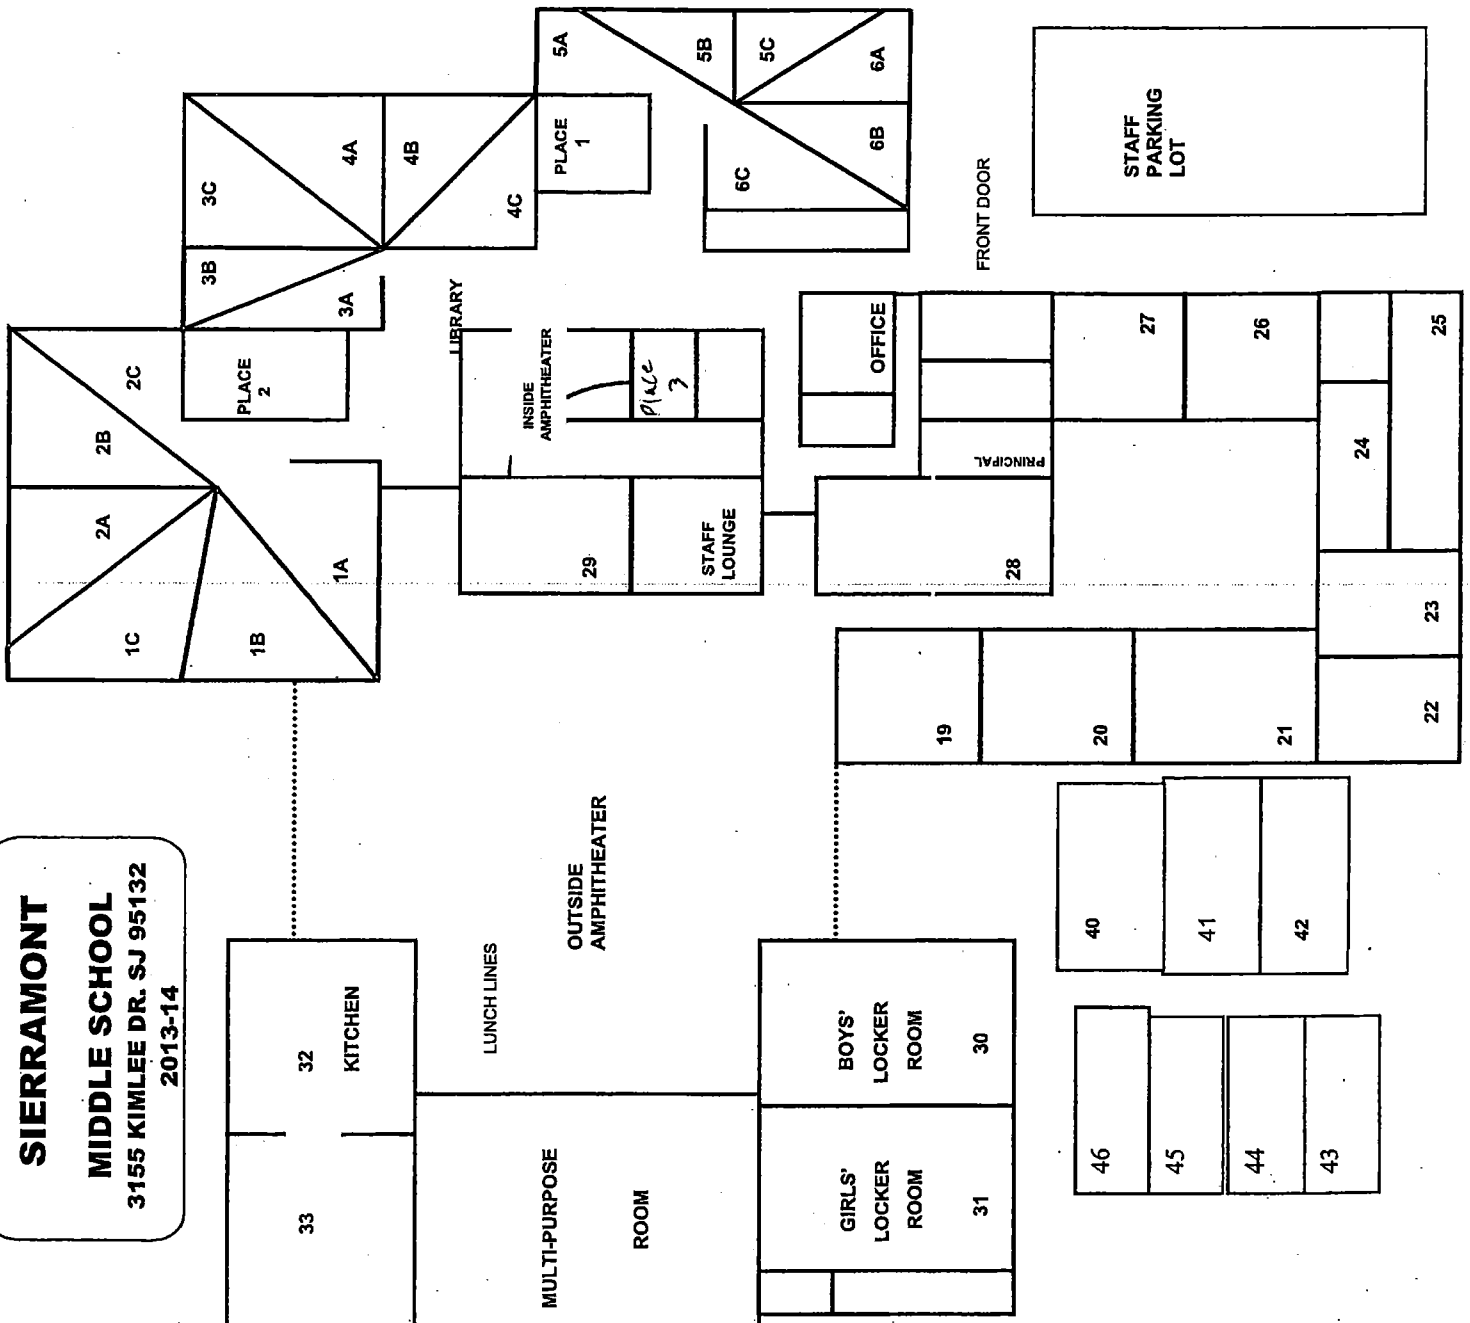


SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 03-22-2016

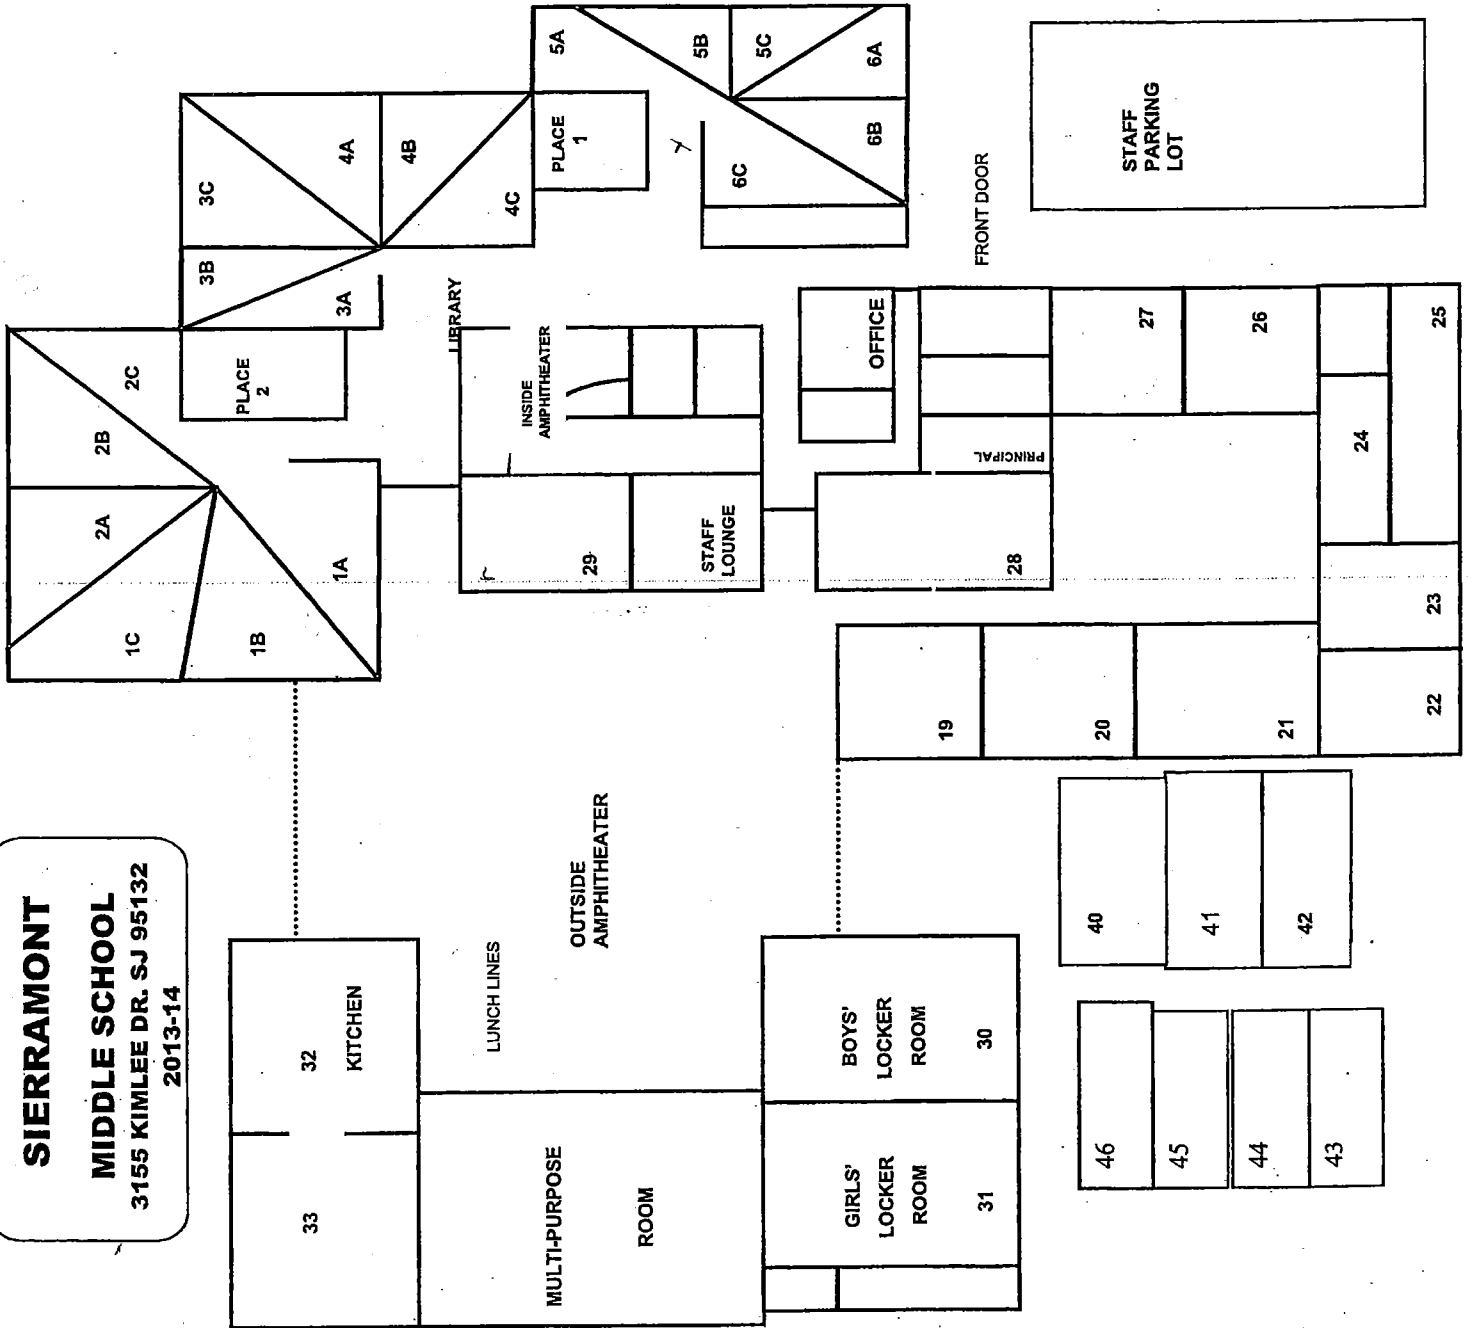


SIERRAMONT


MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 9/18/15

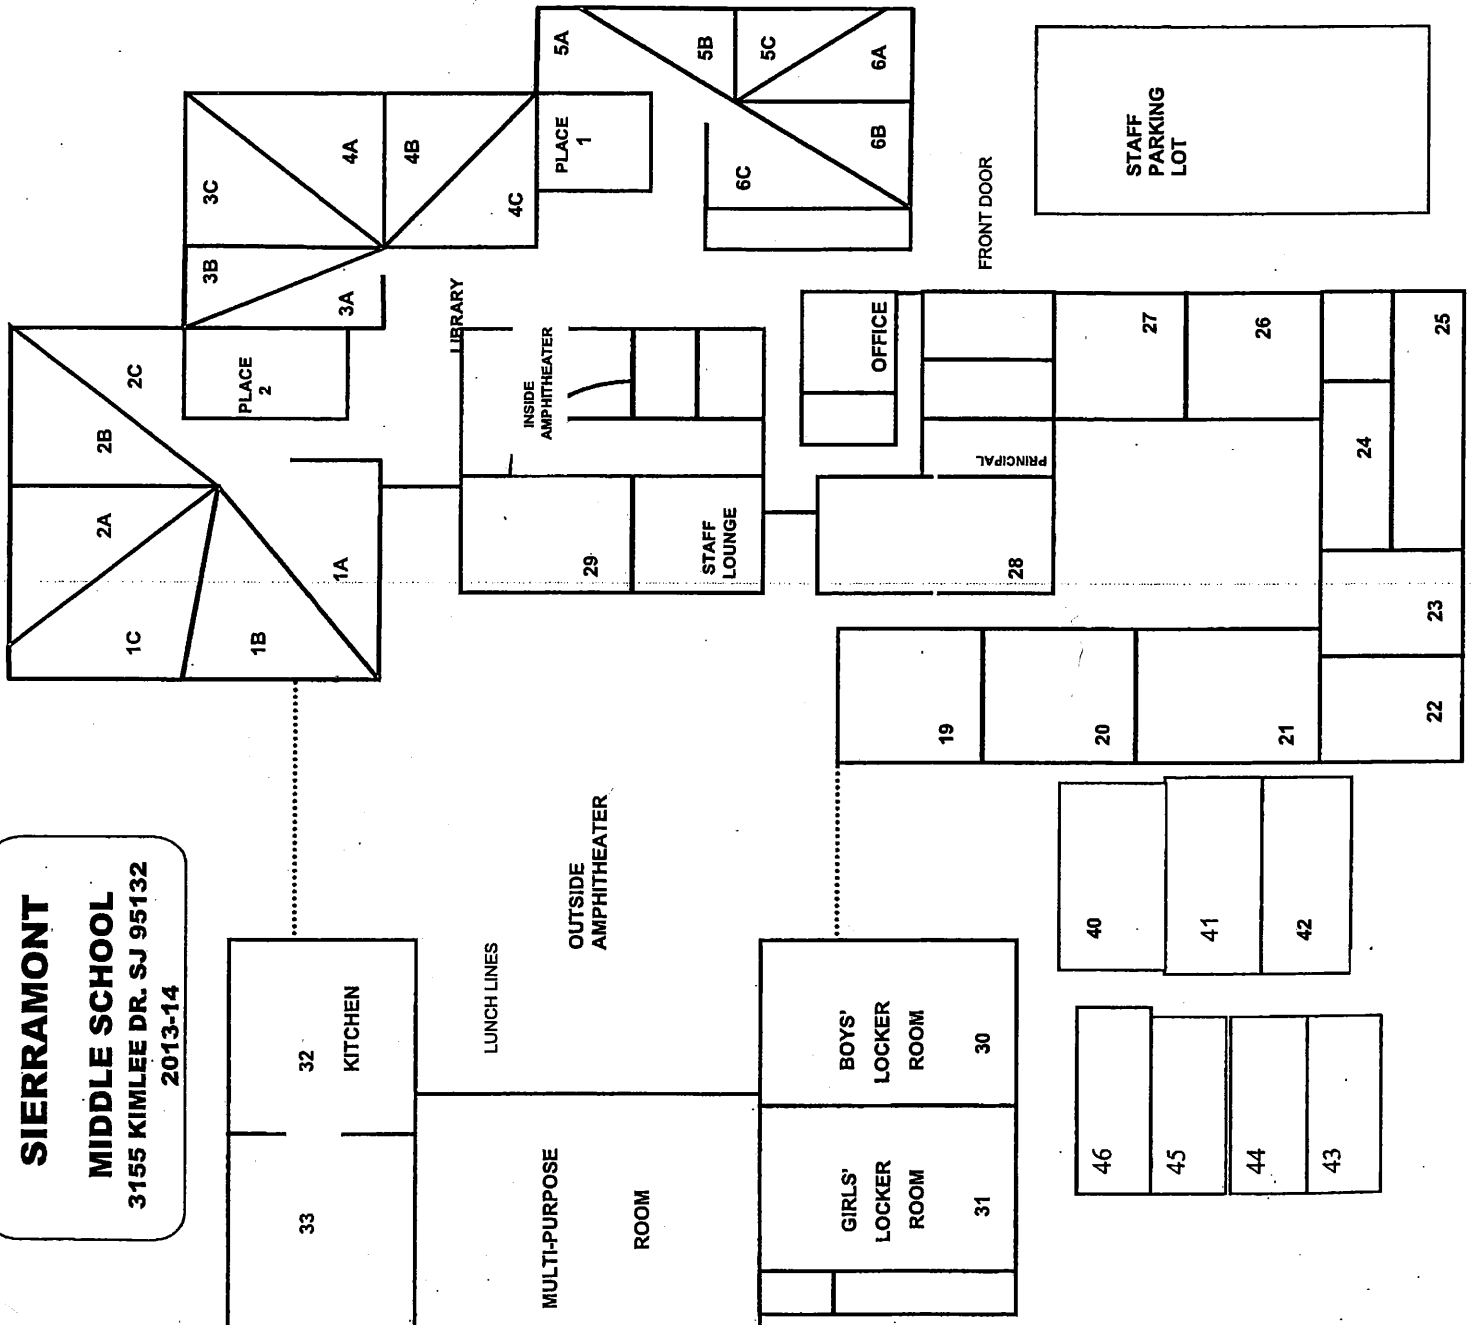

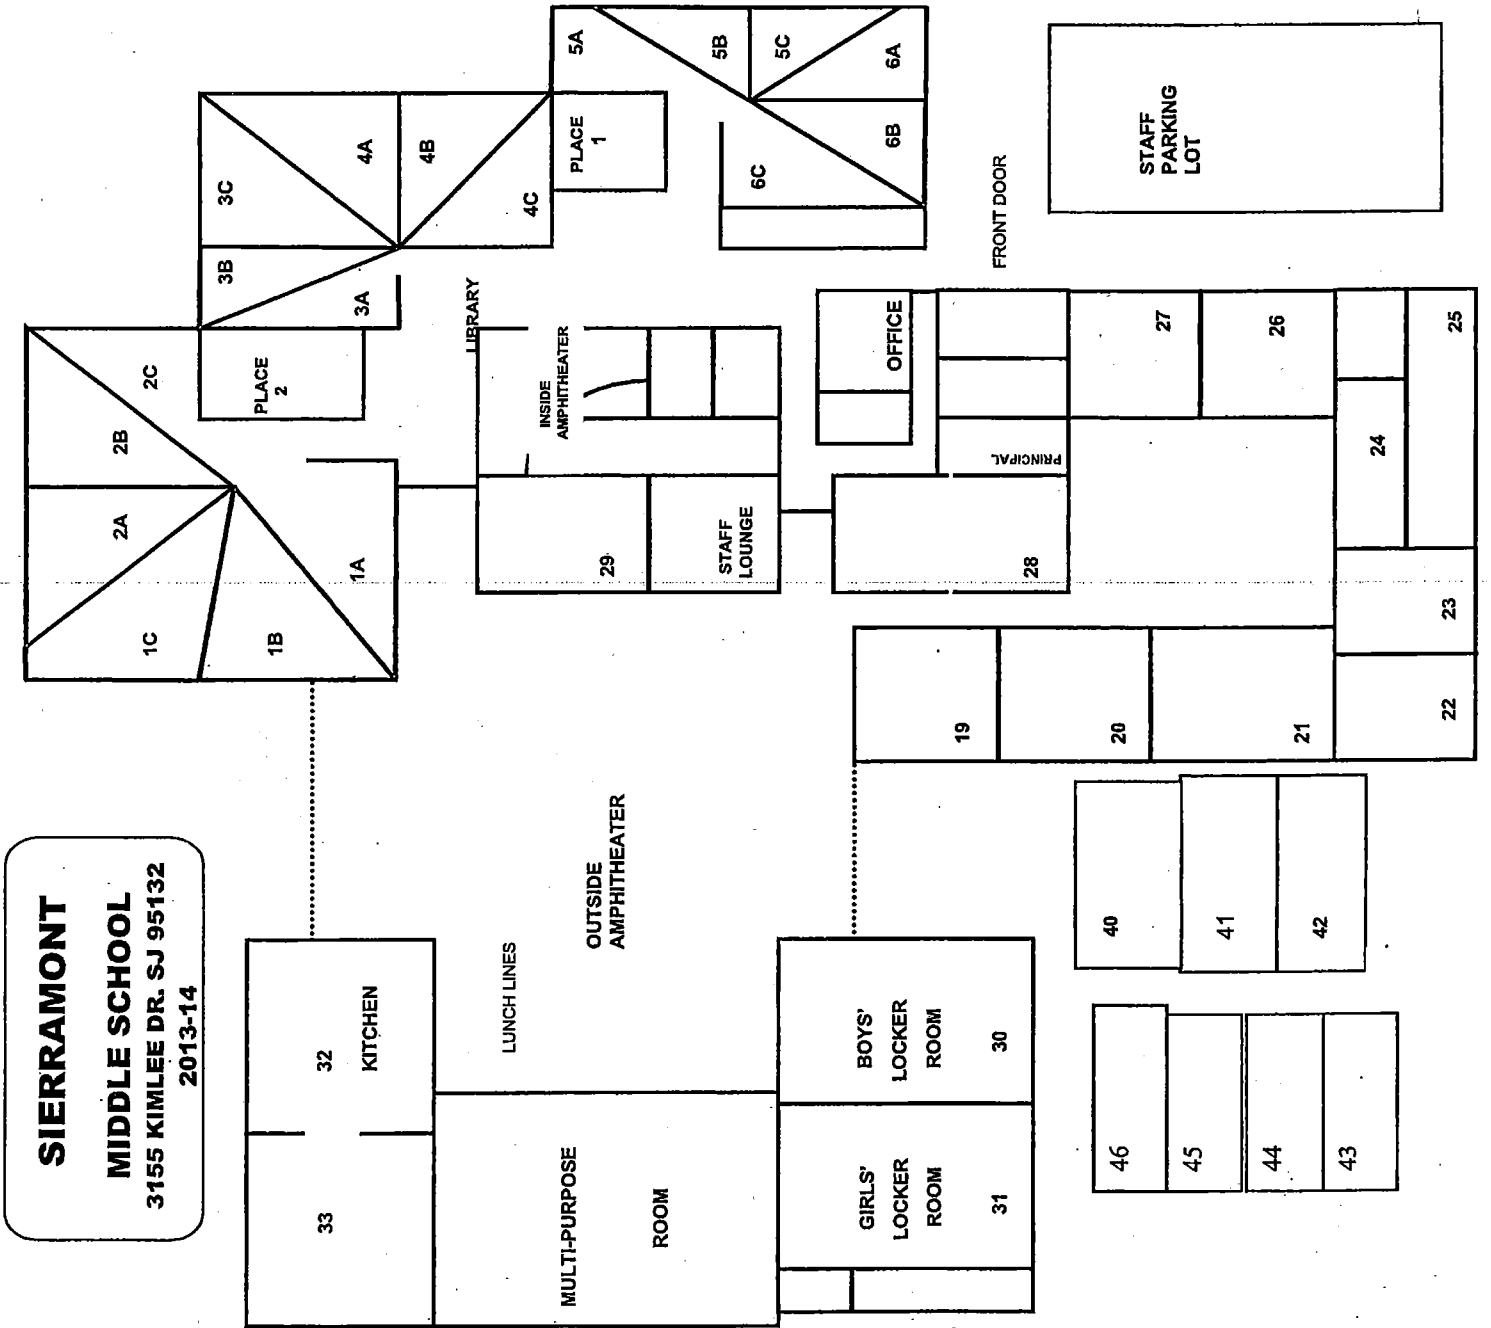

SIERRAMONT
MIDDLE SCHOOL
3155 KIMLEE DR. SJ 95132
2013-14


SIERRAMONT

MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 08-27-2014

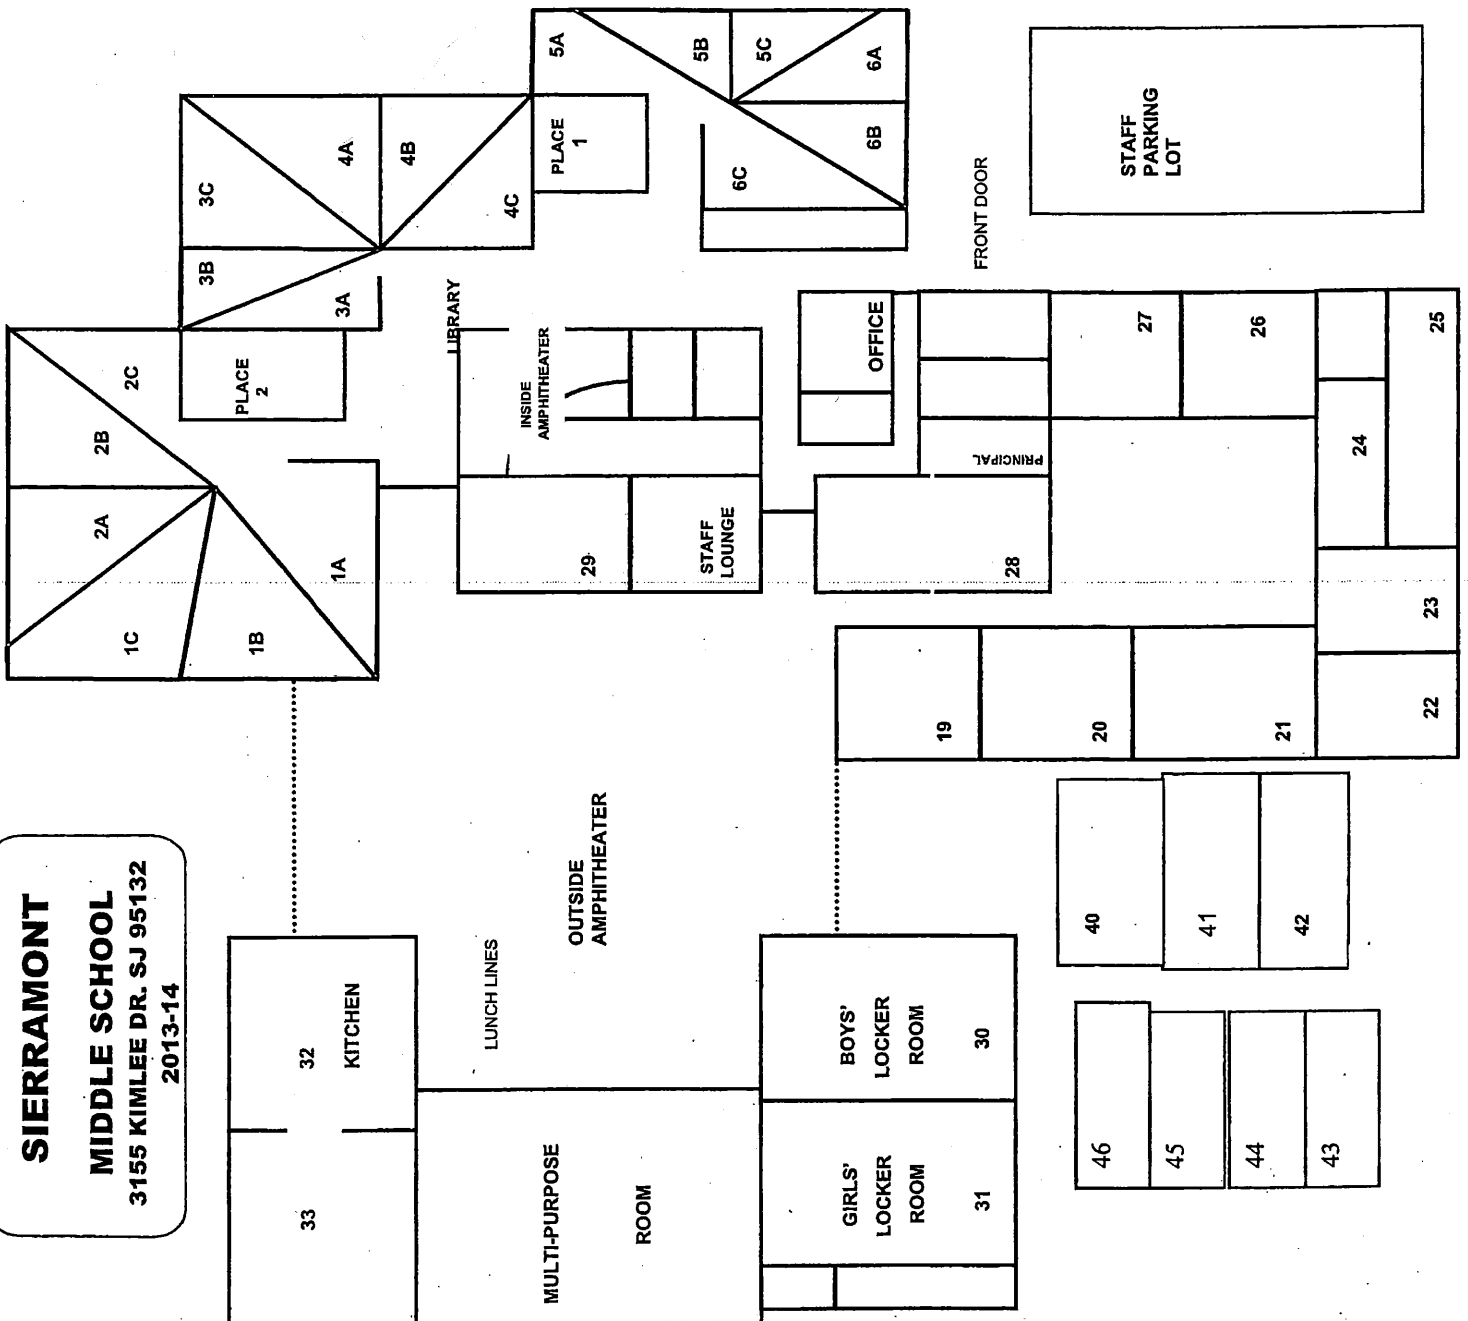


SIERRAMONT


MIDDLE SCHOOL

3155 KIMLEE DR. SJ 95132

2013-14

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 3-5-14

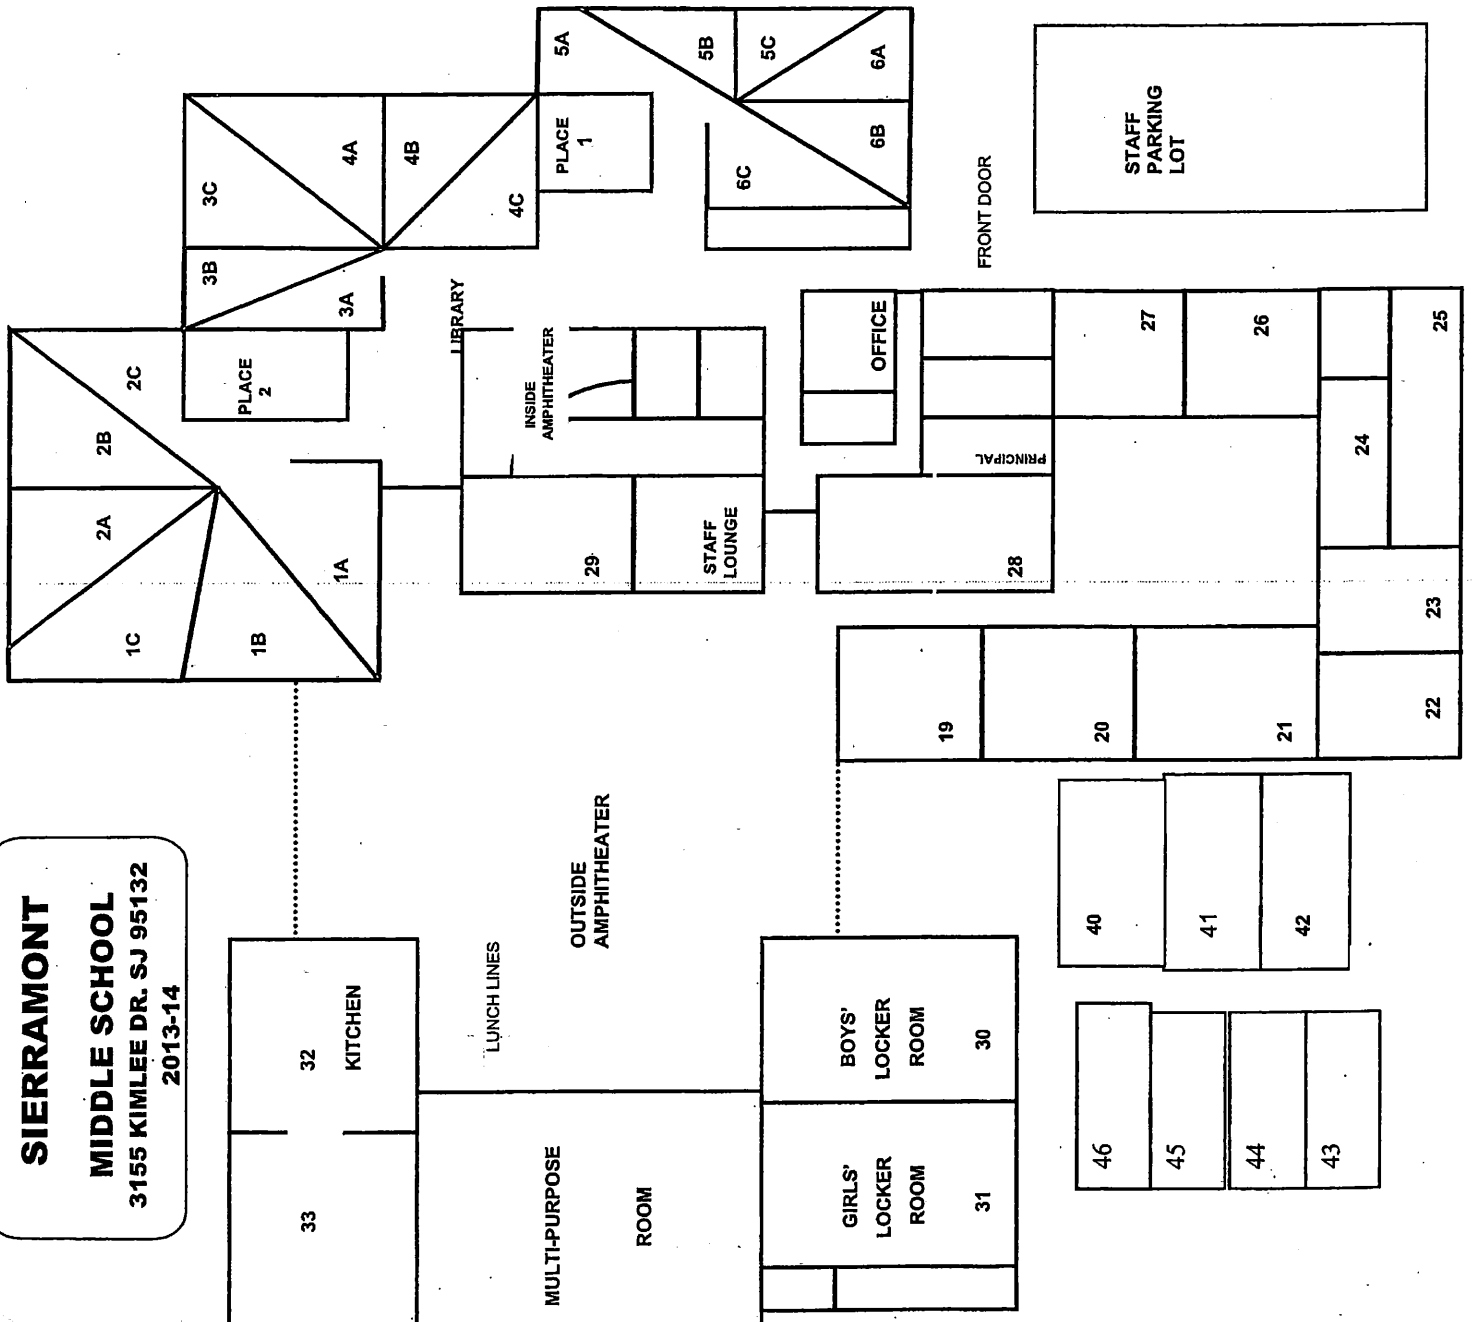


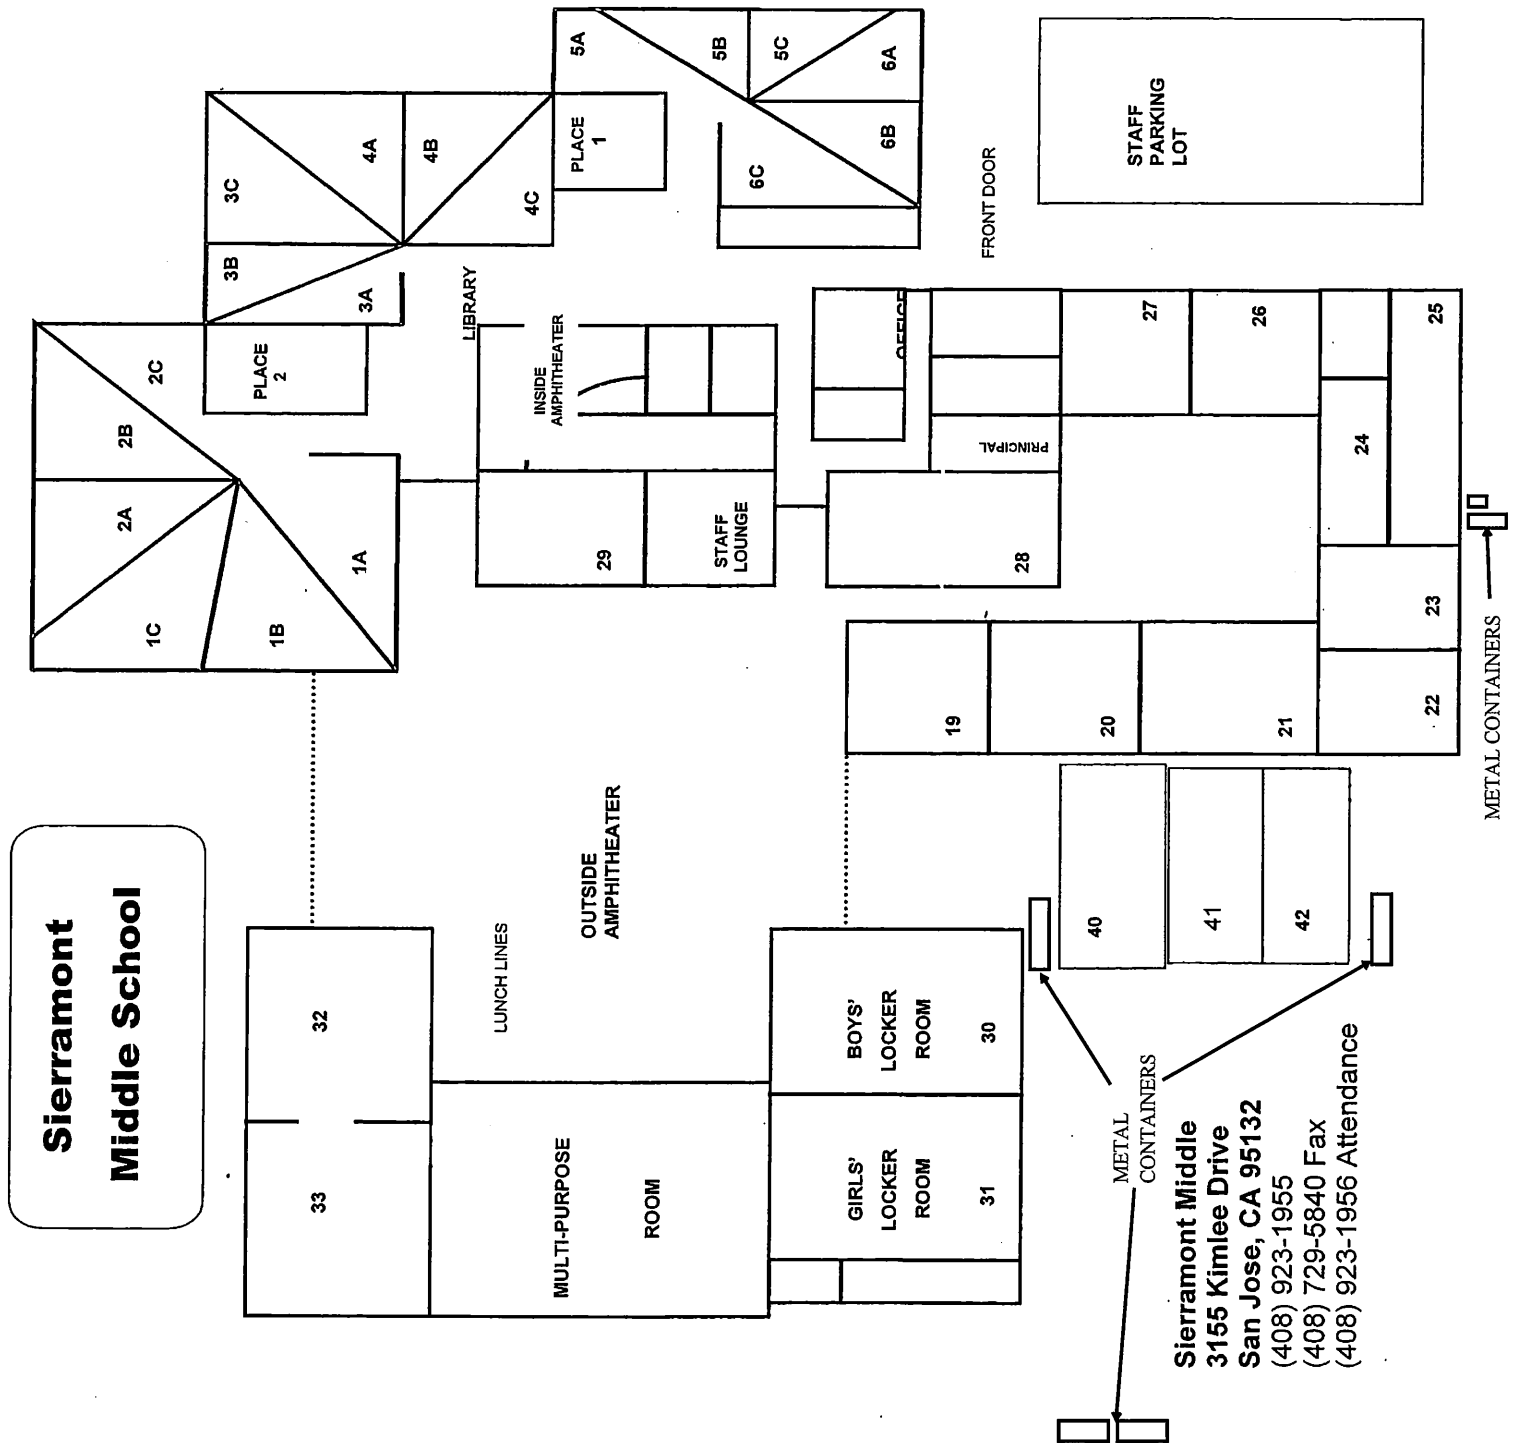

**Sierramont
Middle School**

Sierramont Middle
3155 Kimlee Drive
San Jose, CA 95132
(408) 923-1955
(408) 729-5840 Fax
(408) 923-1956 Attendance

SIERRAMONT MIDDLE SCHOOL
 INSPECTED ON: 4-4-13

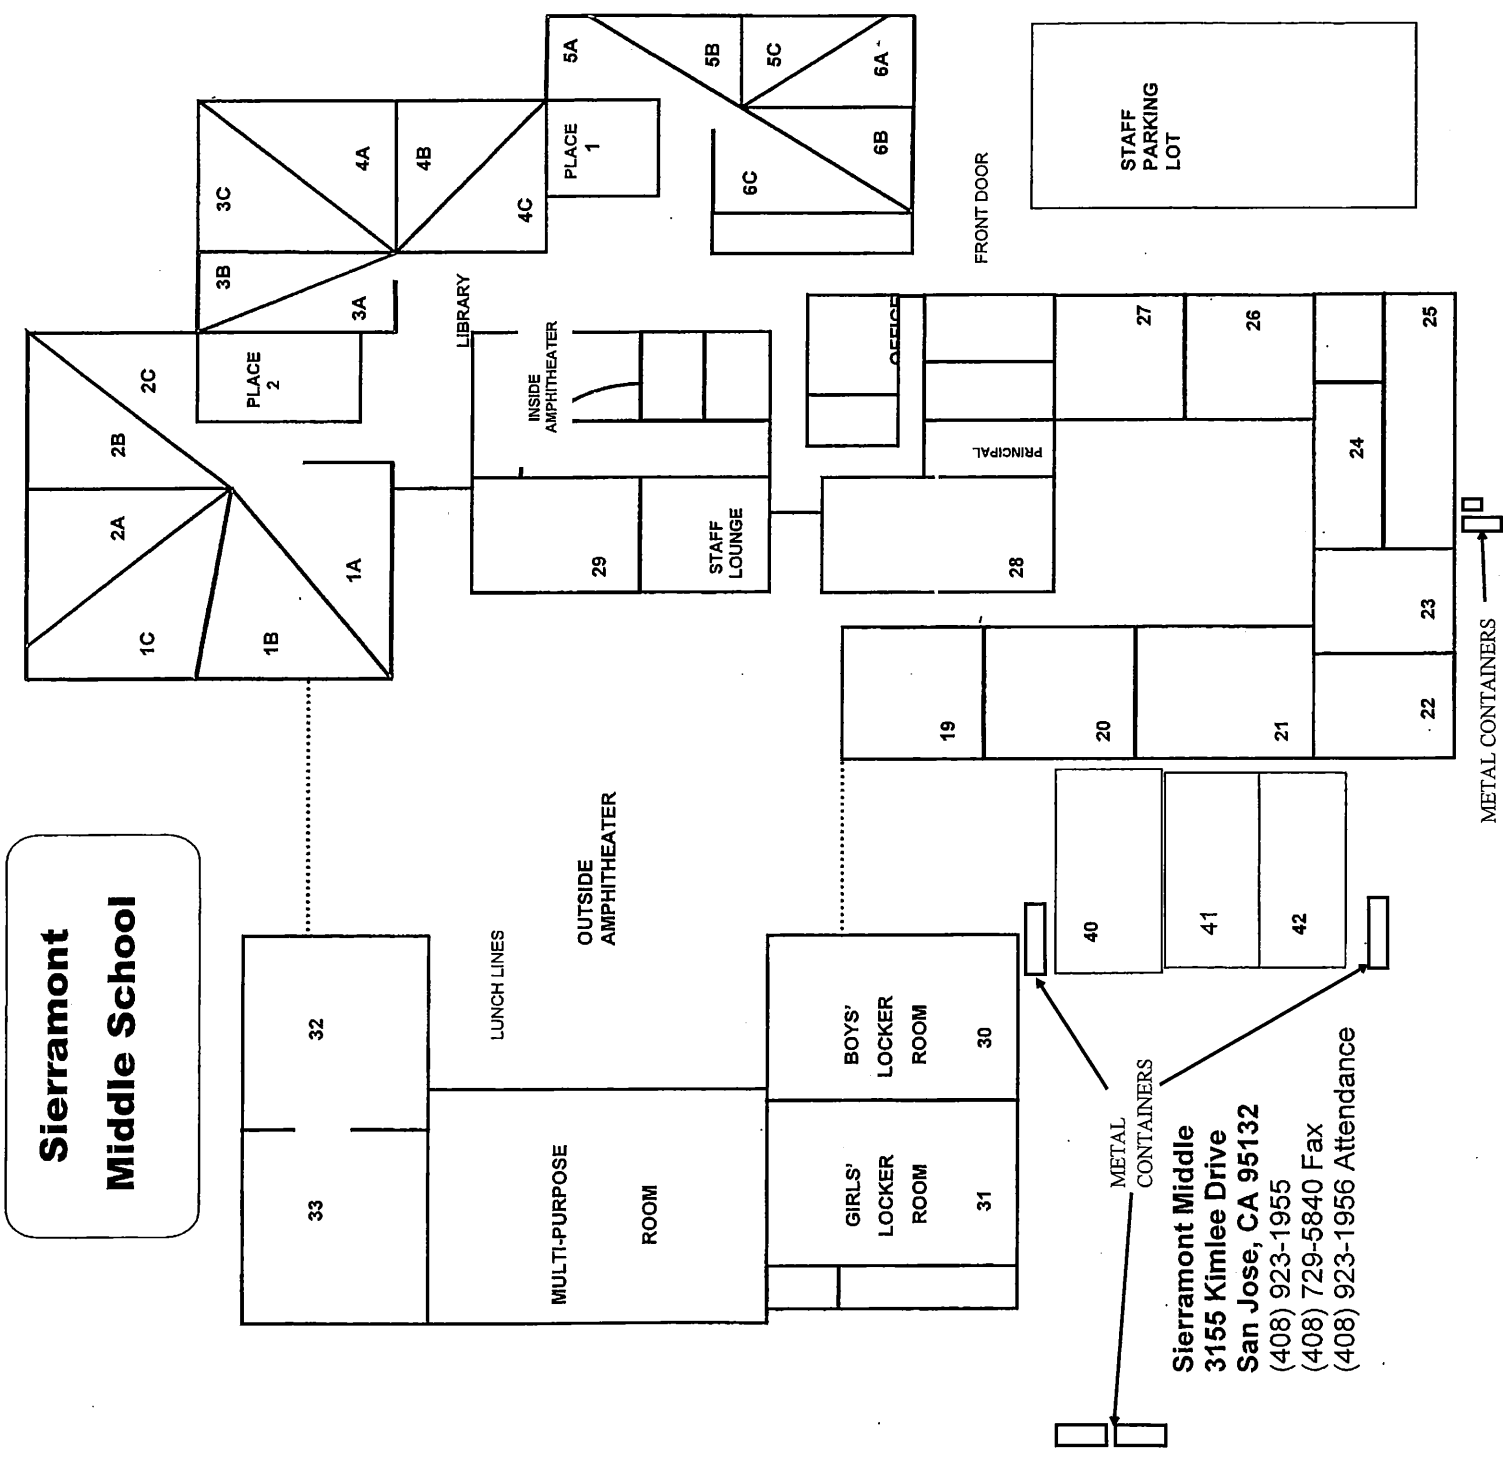


**Sierramont
Middle School**


Sierramont Middle
 3155 Kimlee Drive
 San Jose, CA 95132
 (408) 923-1955
 (408) 729-5840 Fax
 (408) 923-1956 Attendance

Sierramont Middle School

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 10-11-12

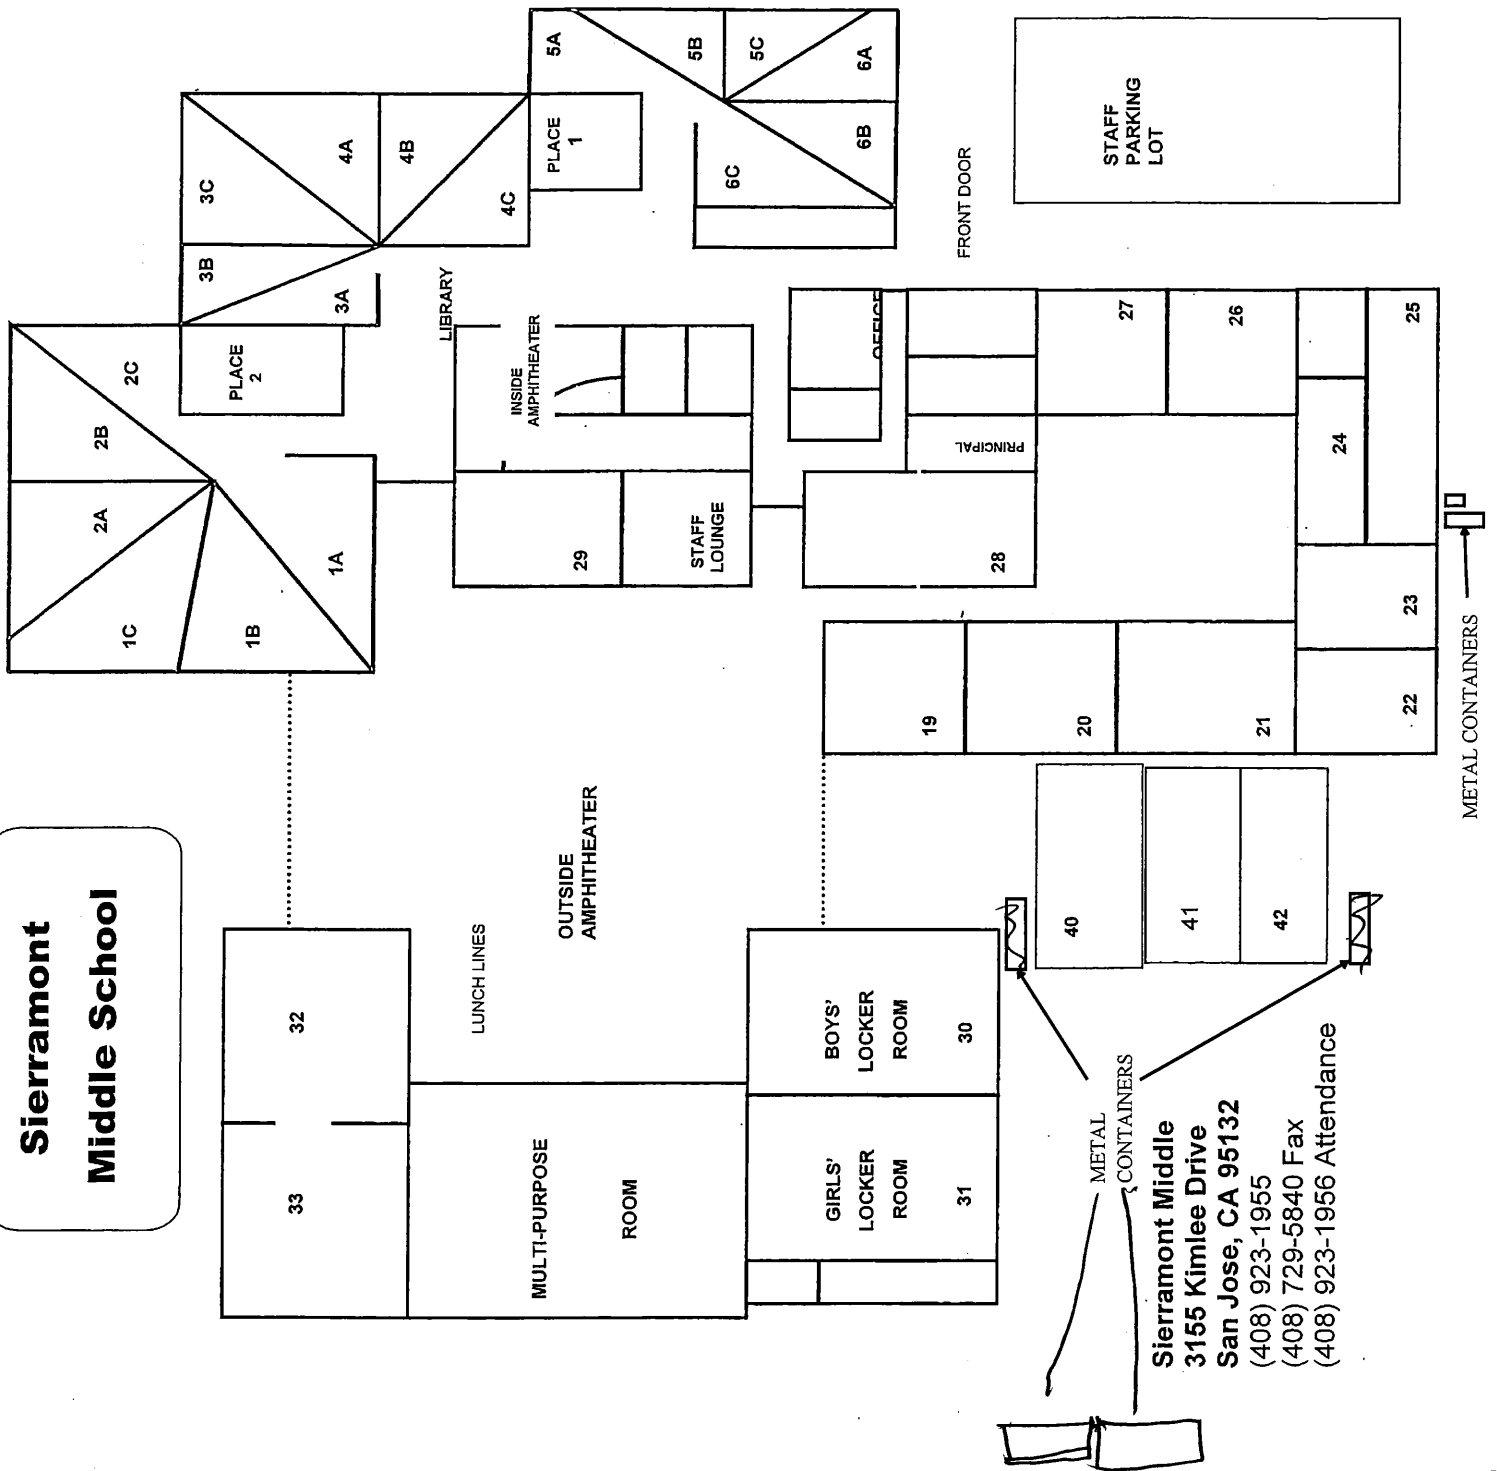


Sierramont Middle
3155 Kimlee Drive
San Jose, CA 95132
(408) 923-1955
(408) 729-5840 Fax
(408) 923-1956 Attendance

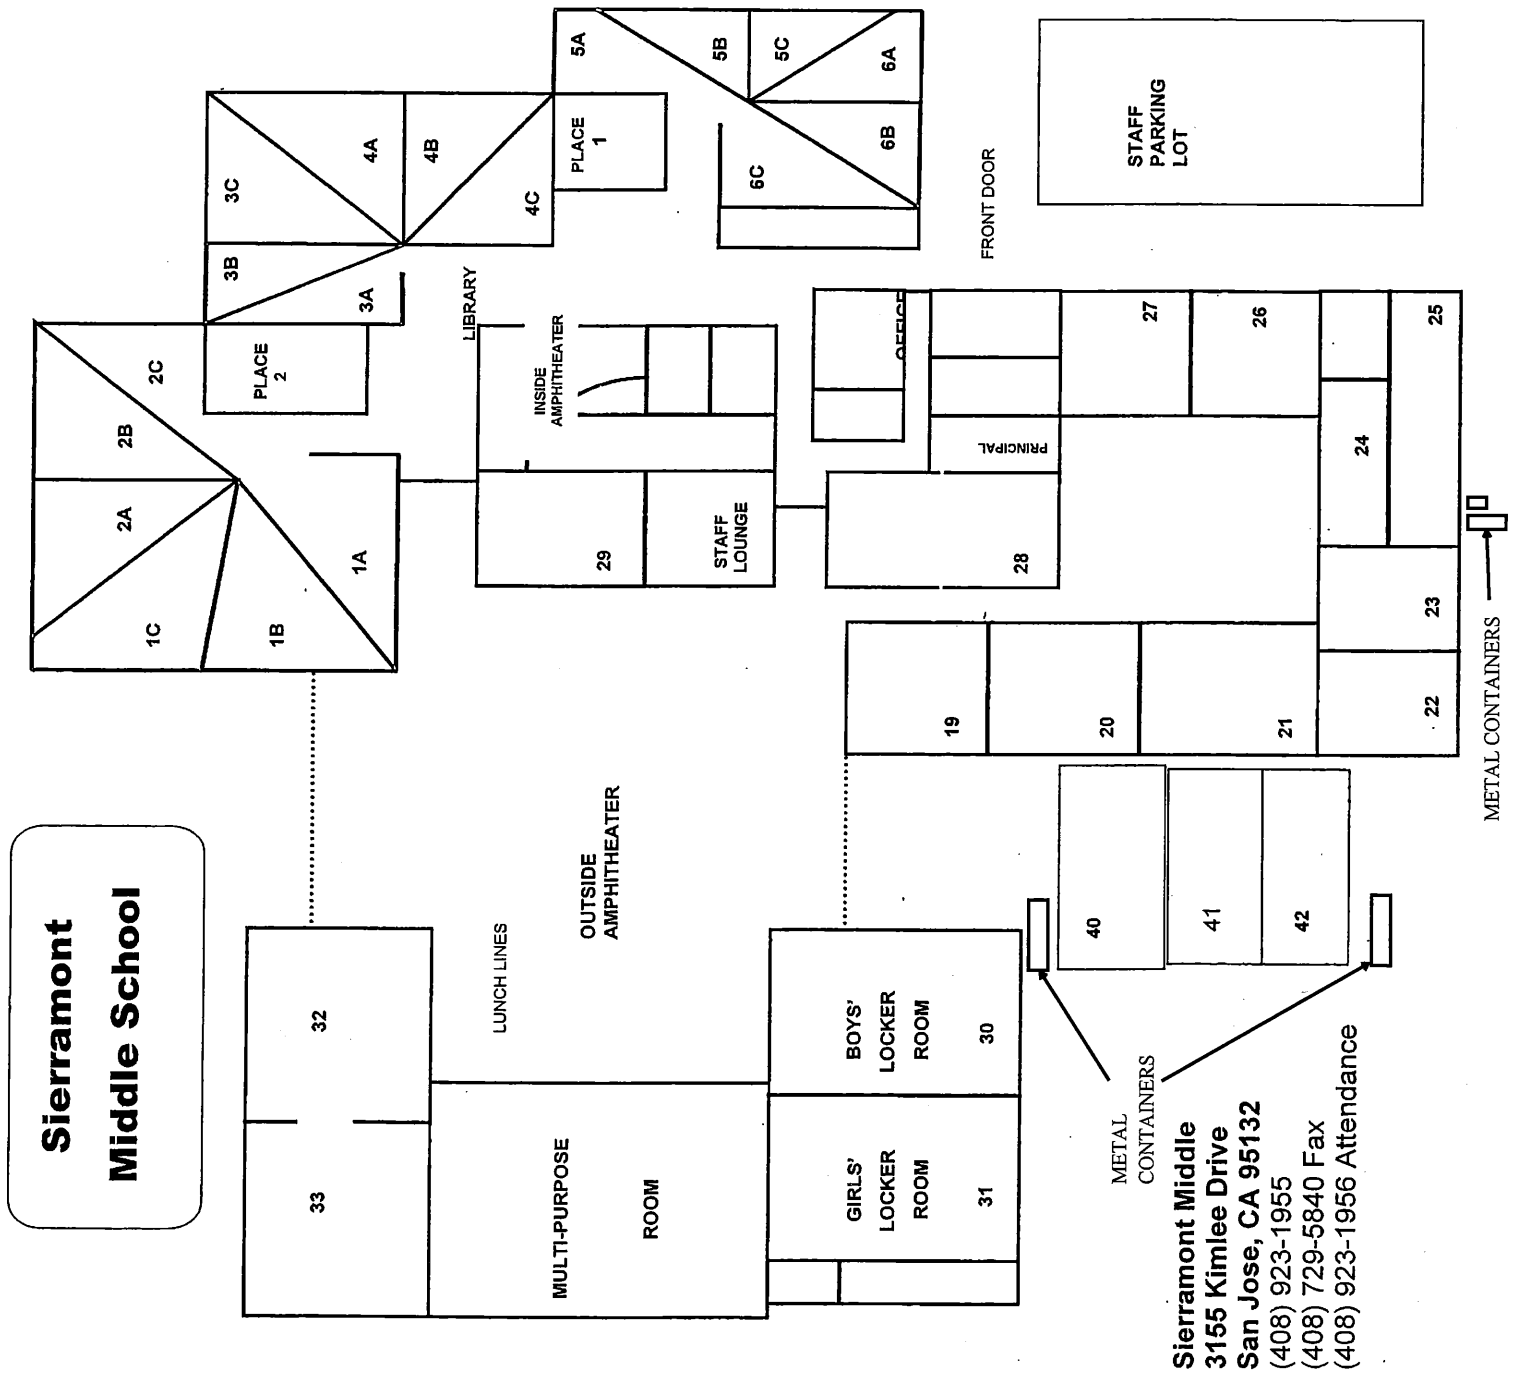


Sierramont Middle
3155 Kimlee Drive
San Jose, CA 95132
(408) 923-1955
(408) 729-5840 Fax
(408) 923-1956 Attendance

Sierramont Middle School

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 12-1-11

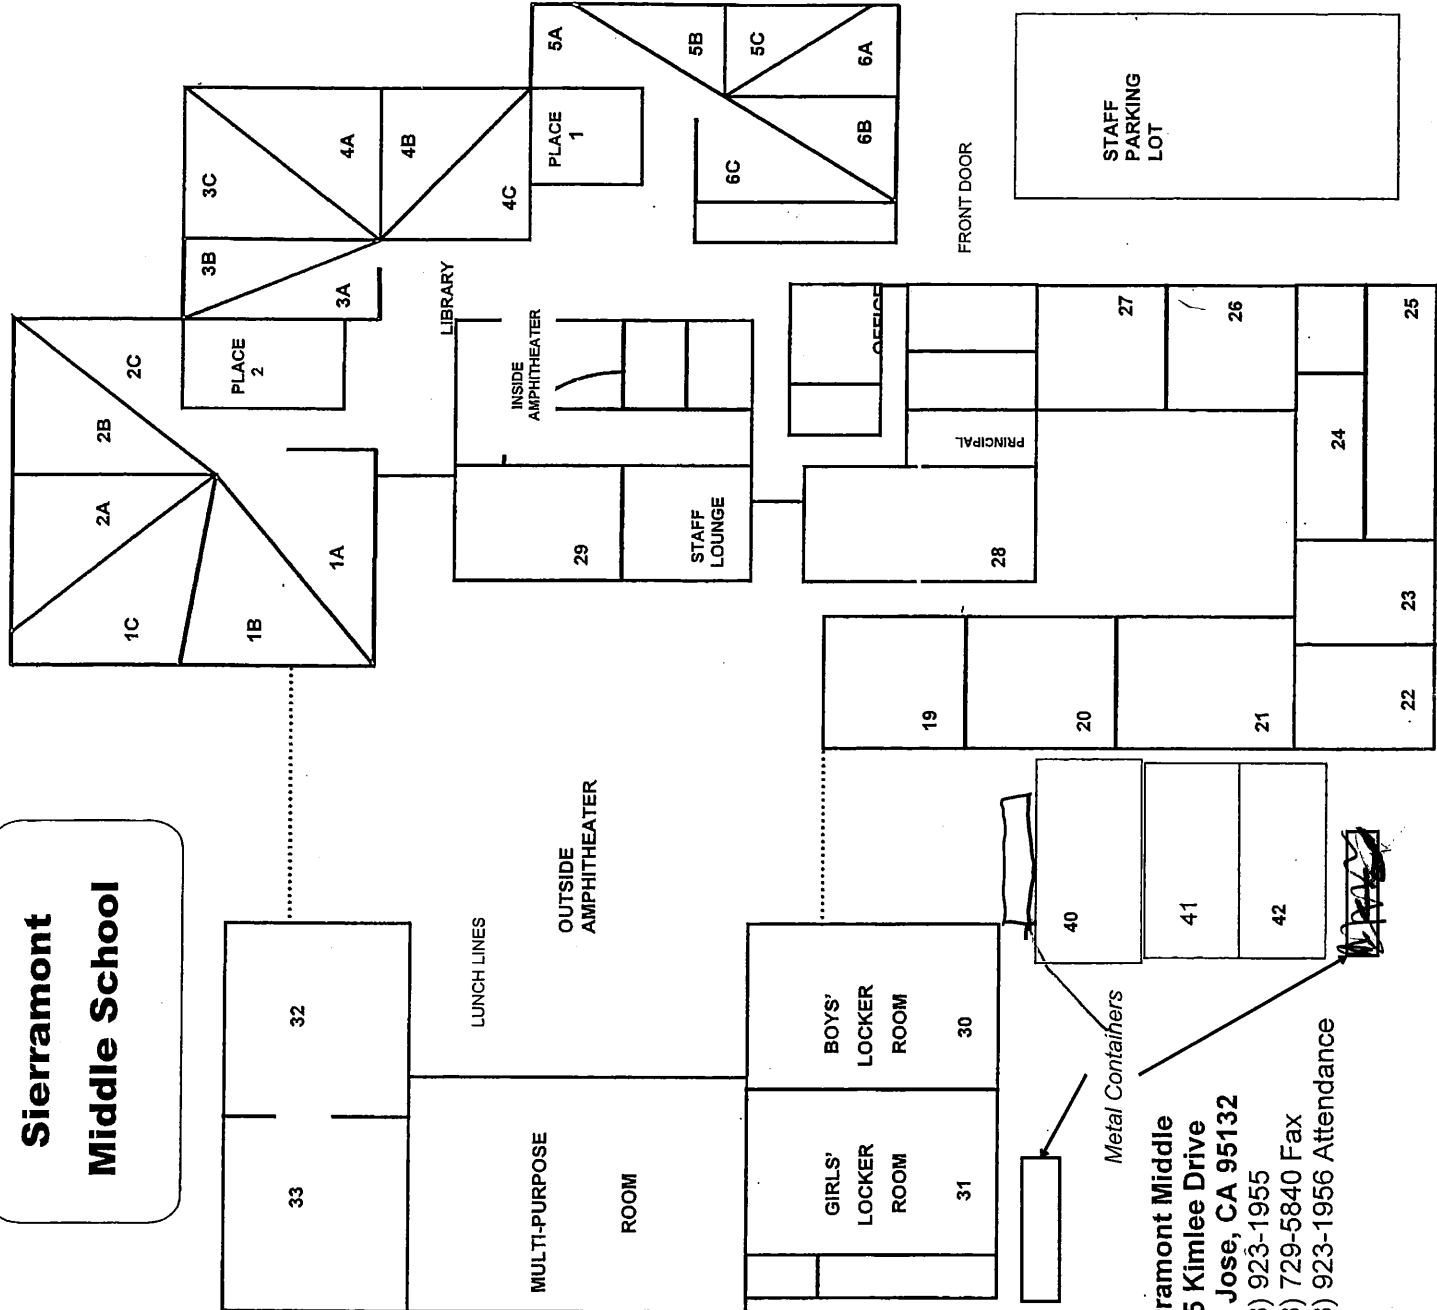

Sierramont Middle
3155 Kimlee Drive
San Jose, CA 95132
(408) 923-1955
(408) 729-5840 Fax
(408) 923-1956 Attendance

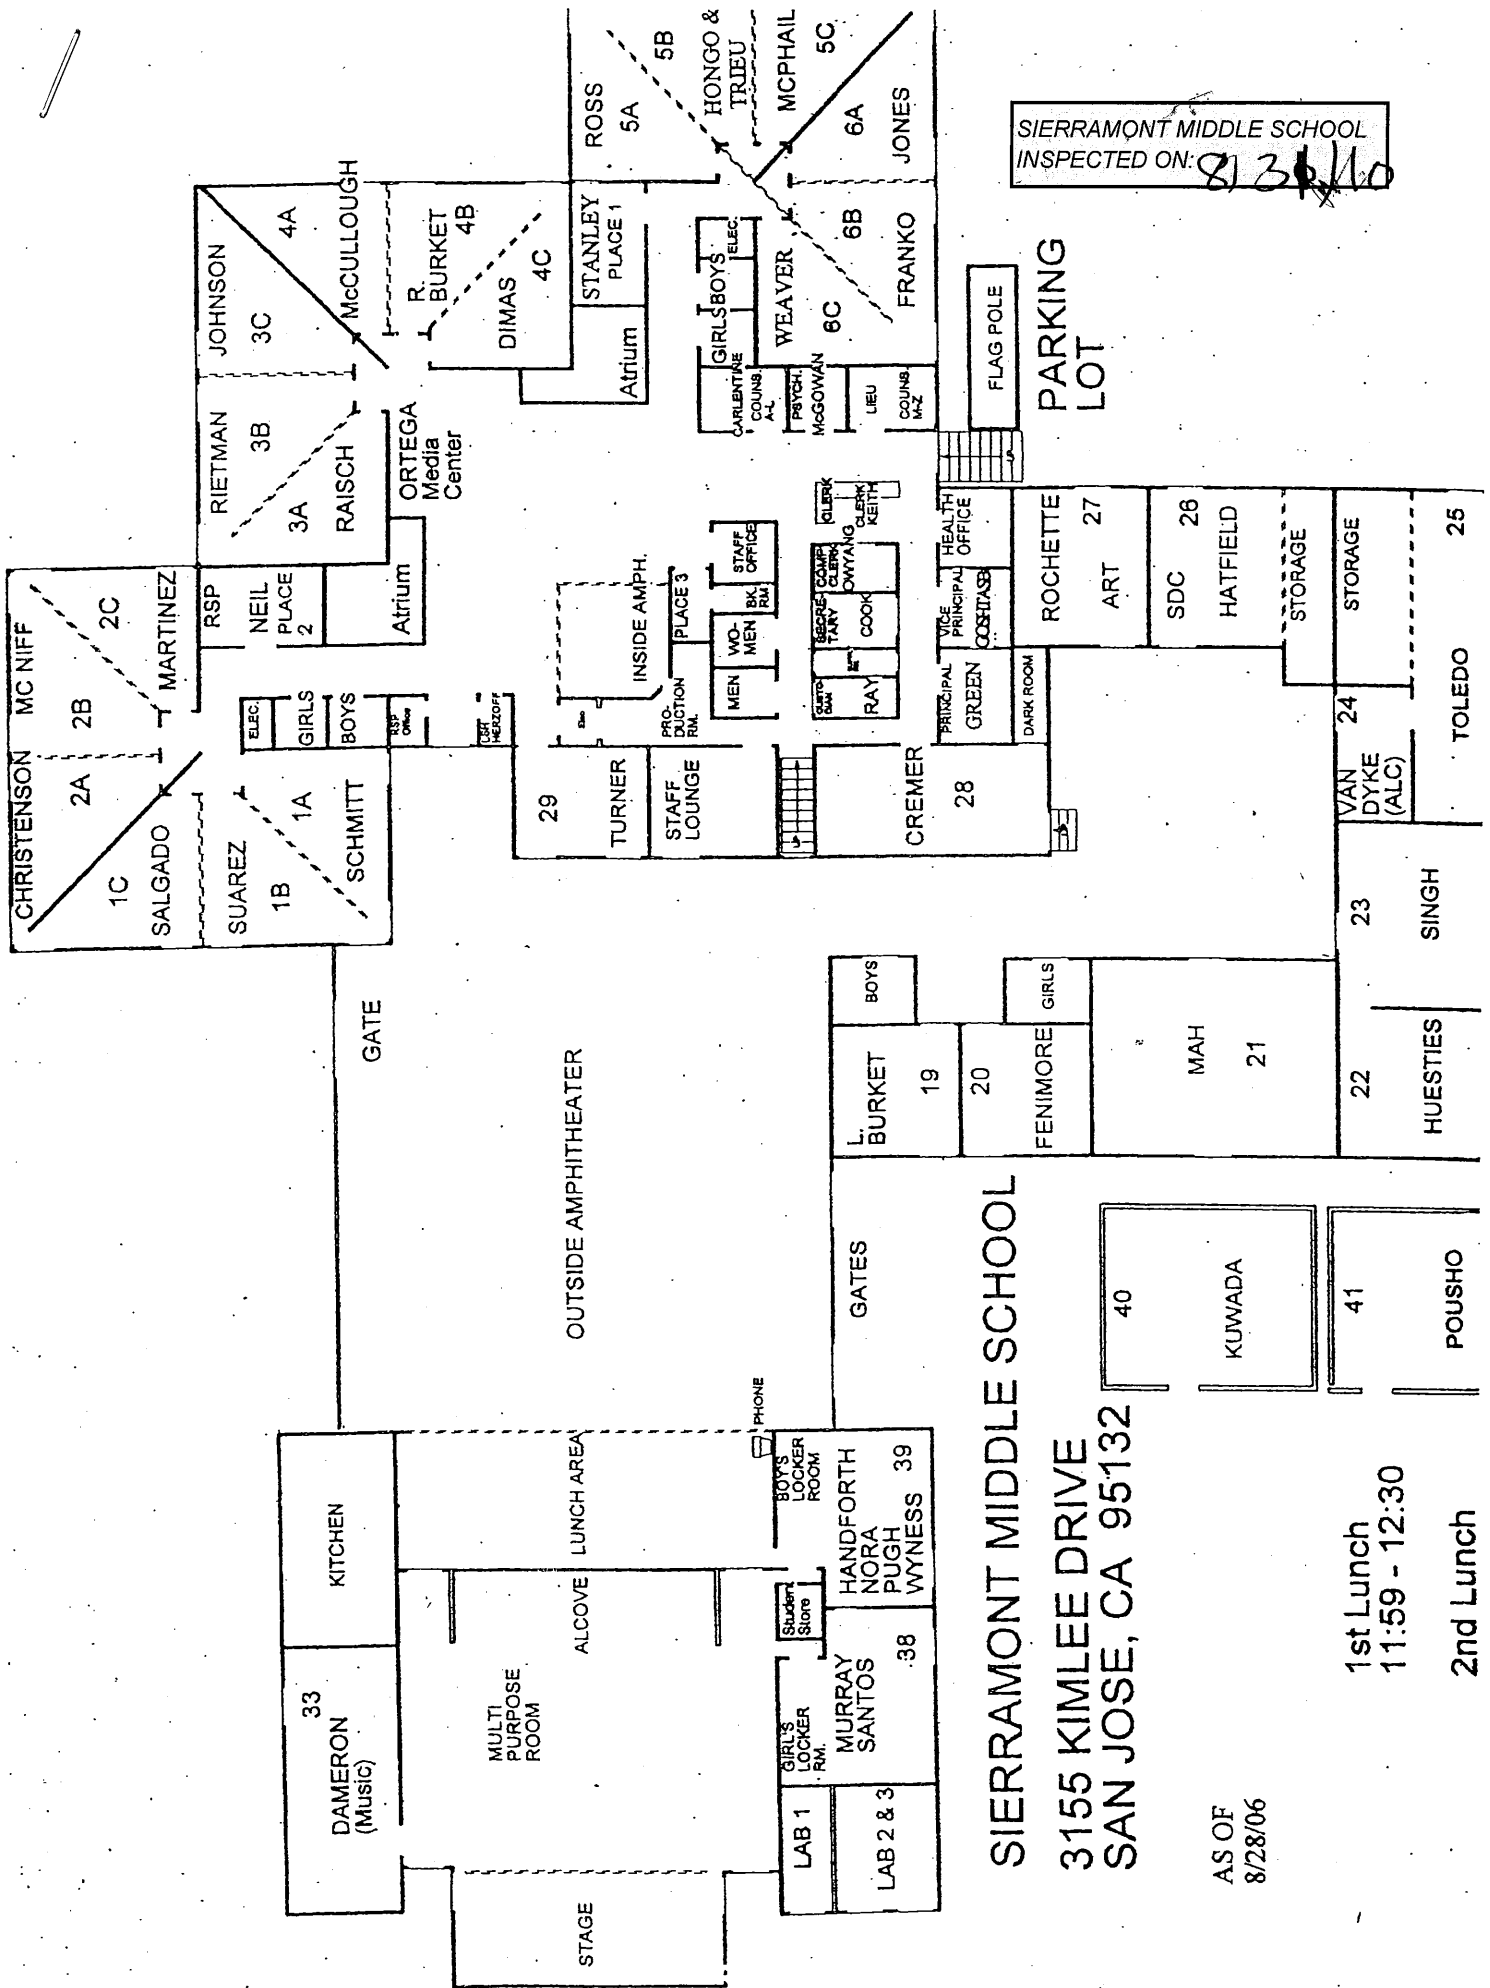


SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 8/30/10

SIERRAMONT MIDDLE SCHOOL
3155 KIMLEE DRIVE
SAN JOSE, CA 95132

AS OF
8/28/06

1st Lunch
11:59 - 12:30
2nd Lunch

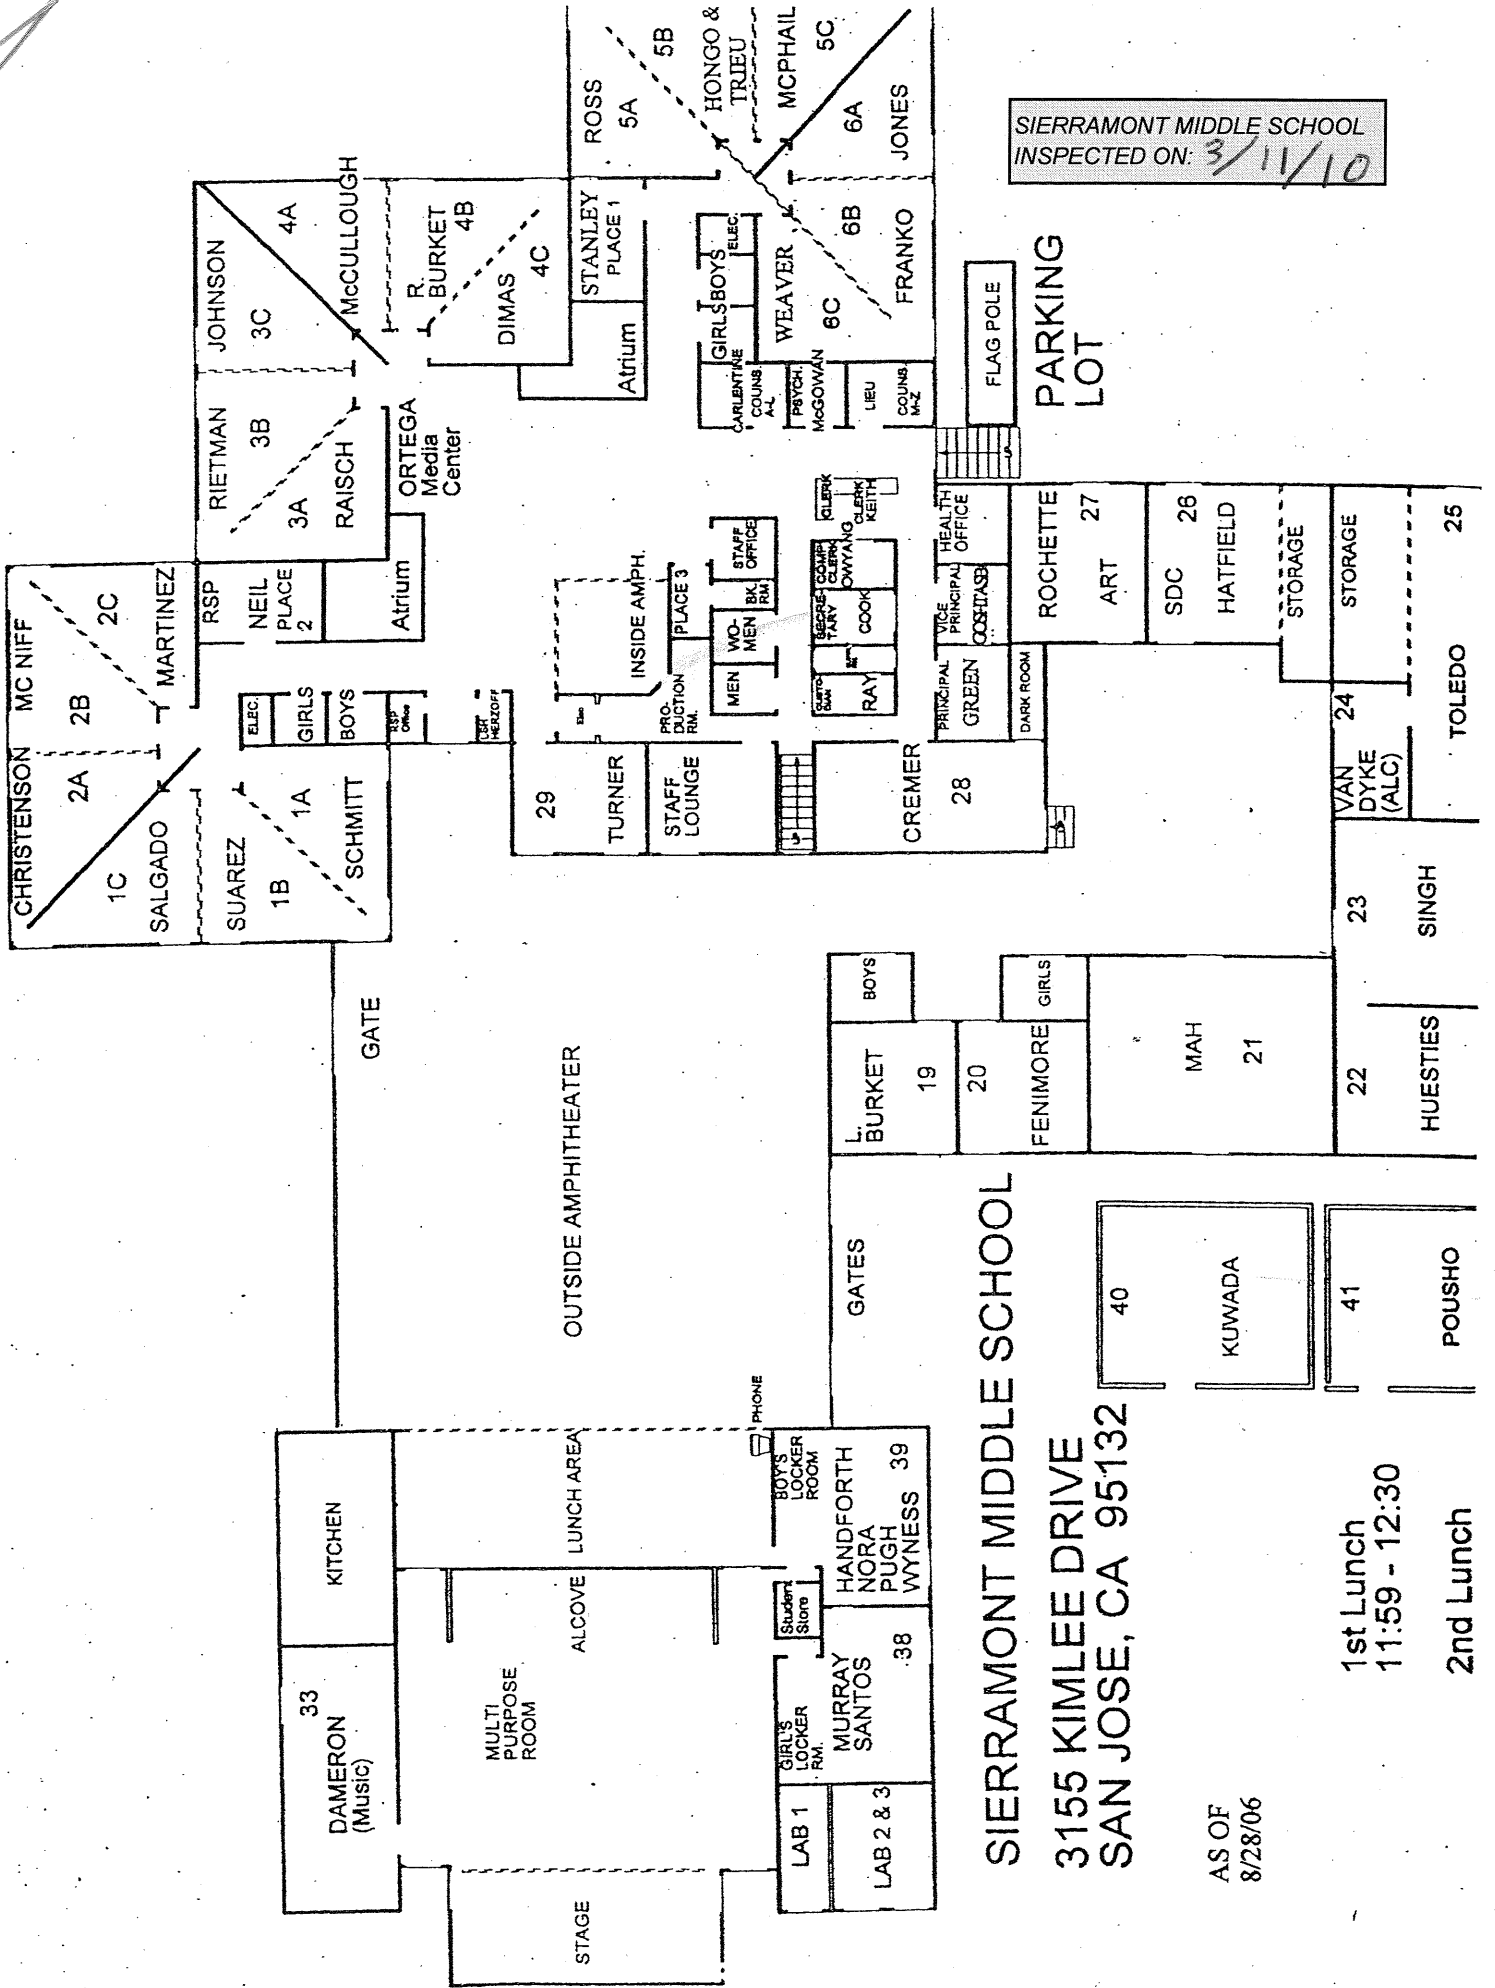


SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 3/11/10

SIERRAMONT MIDDLE SCHOOL
3155 KIMLEE DRIVE
SAN JOSE, CA 95132

AS OF
8/28/06

1st Lunch
11:59 - 12:30
2nd Lunch

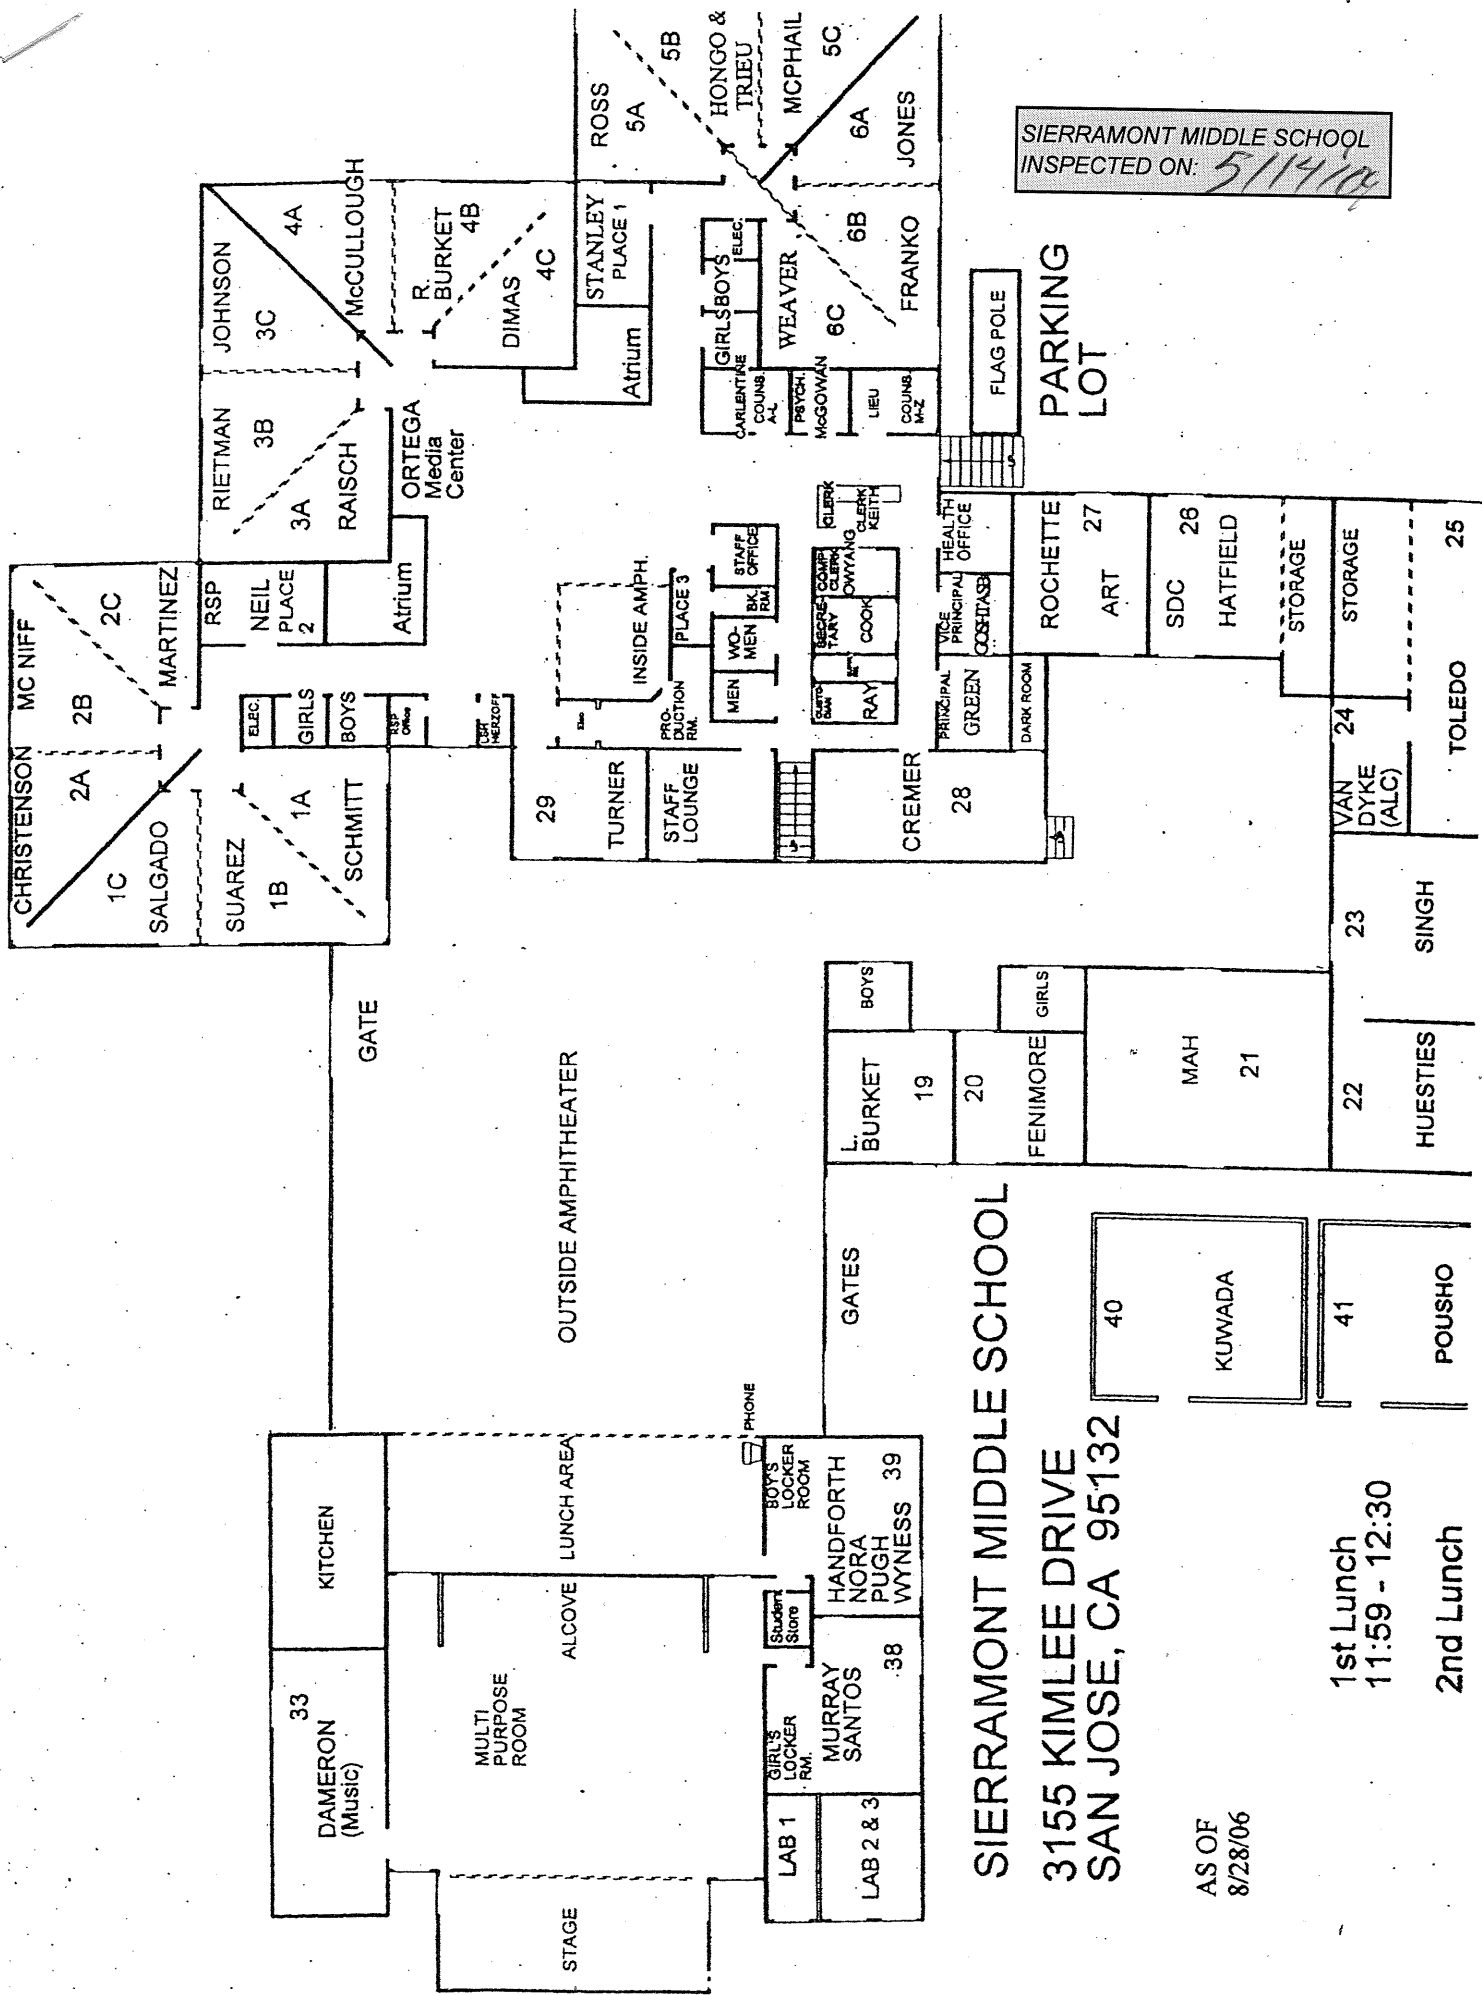


SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 5/14/06

SIERRAMONT MIDDLE SCHOOL
3155 KIMLEE DRIVE
SAN JOSE, CA 95132

AS OF
8/28/06

1st Lunch
11:59 - 12:30
2nd Lunch

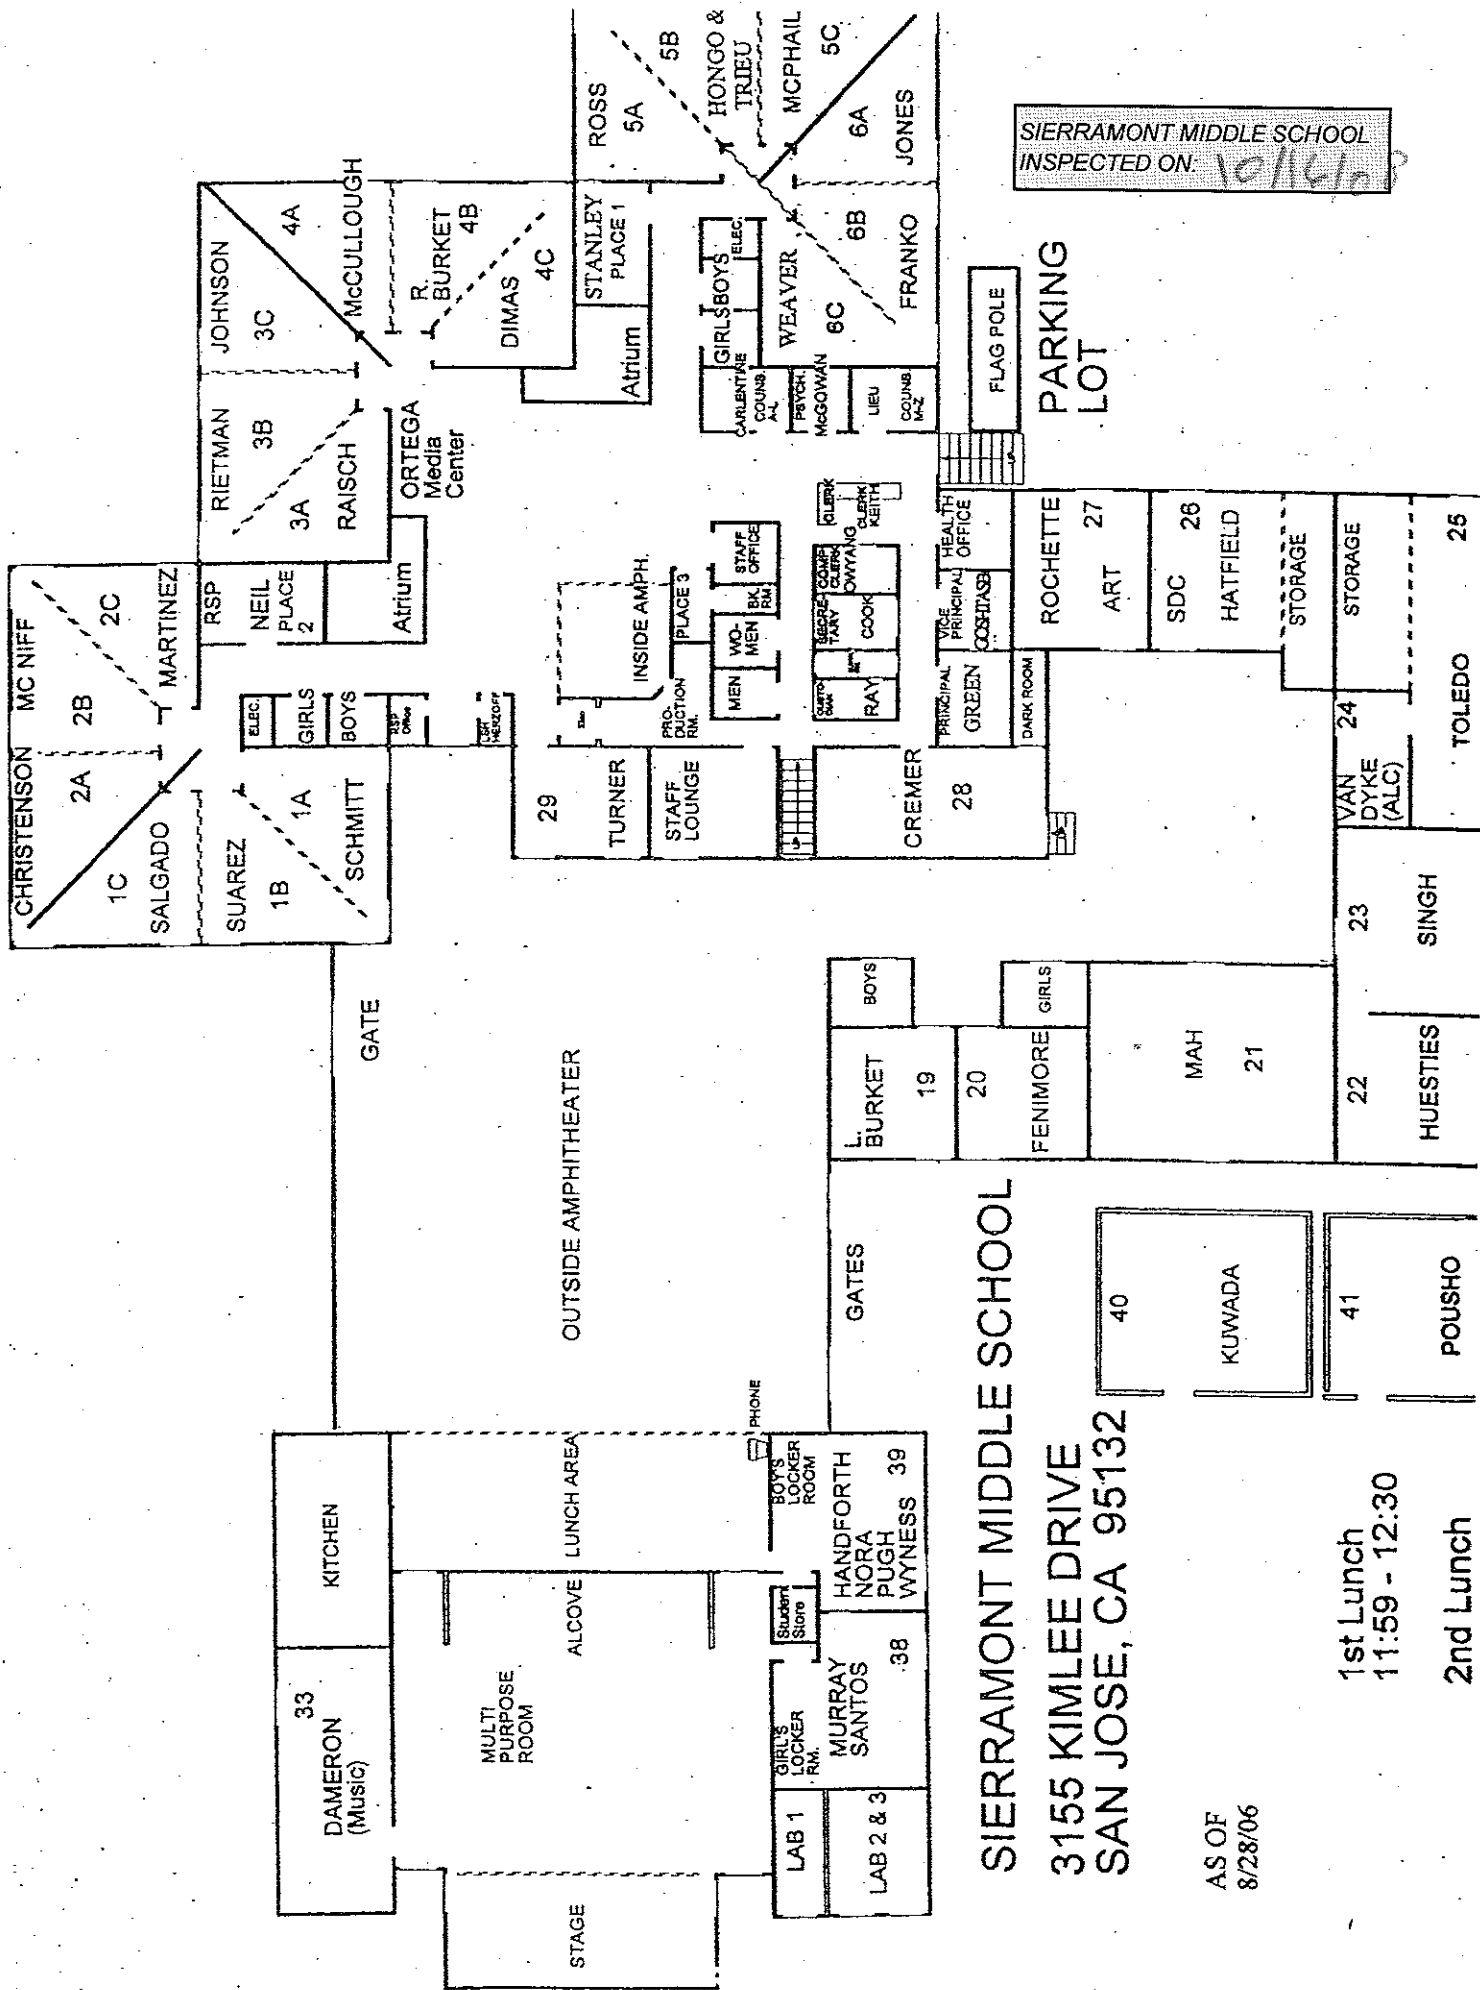

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON 10/16/08


SIERRAMONT MIDDLE SCHOOL
3155 KIMLEE DRIVE
SAN JOSE, CA 95132

AS OF
8/28/06

1st Lunch
11:59 - 12:30

2nd Lunch


SIERRAMONT MIDDLE SCHOOL
INSPECTED ON 9-16-08

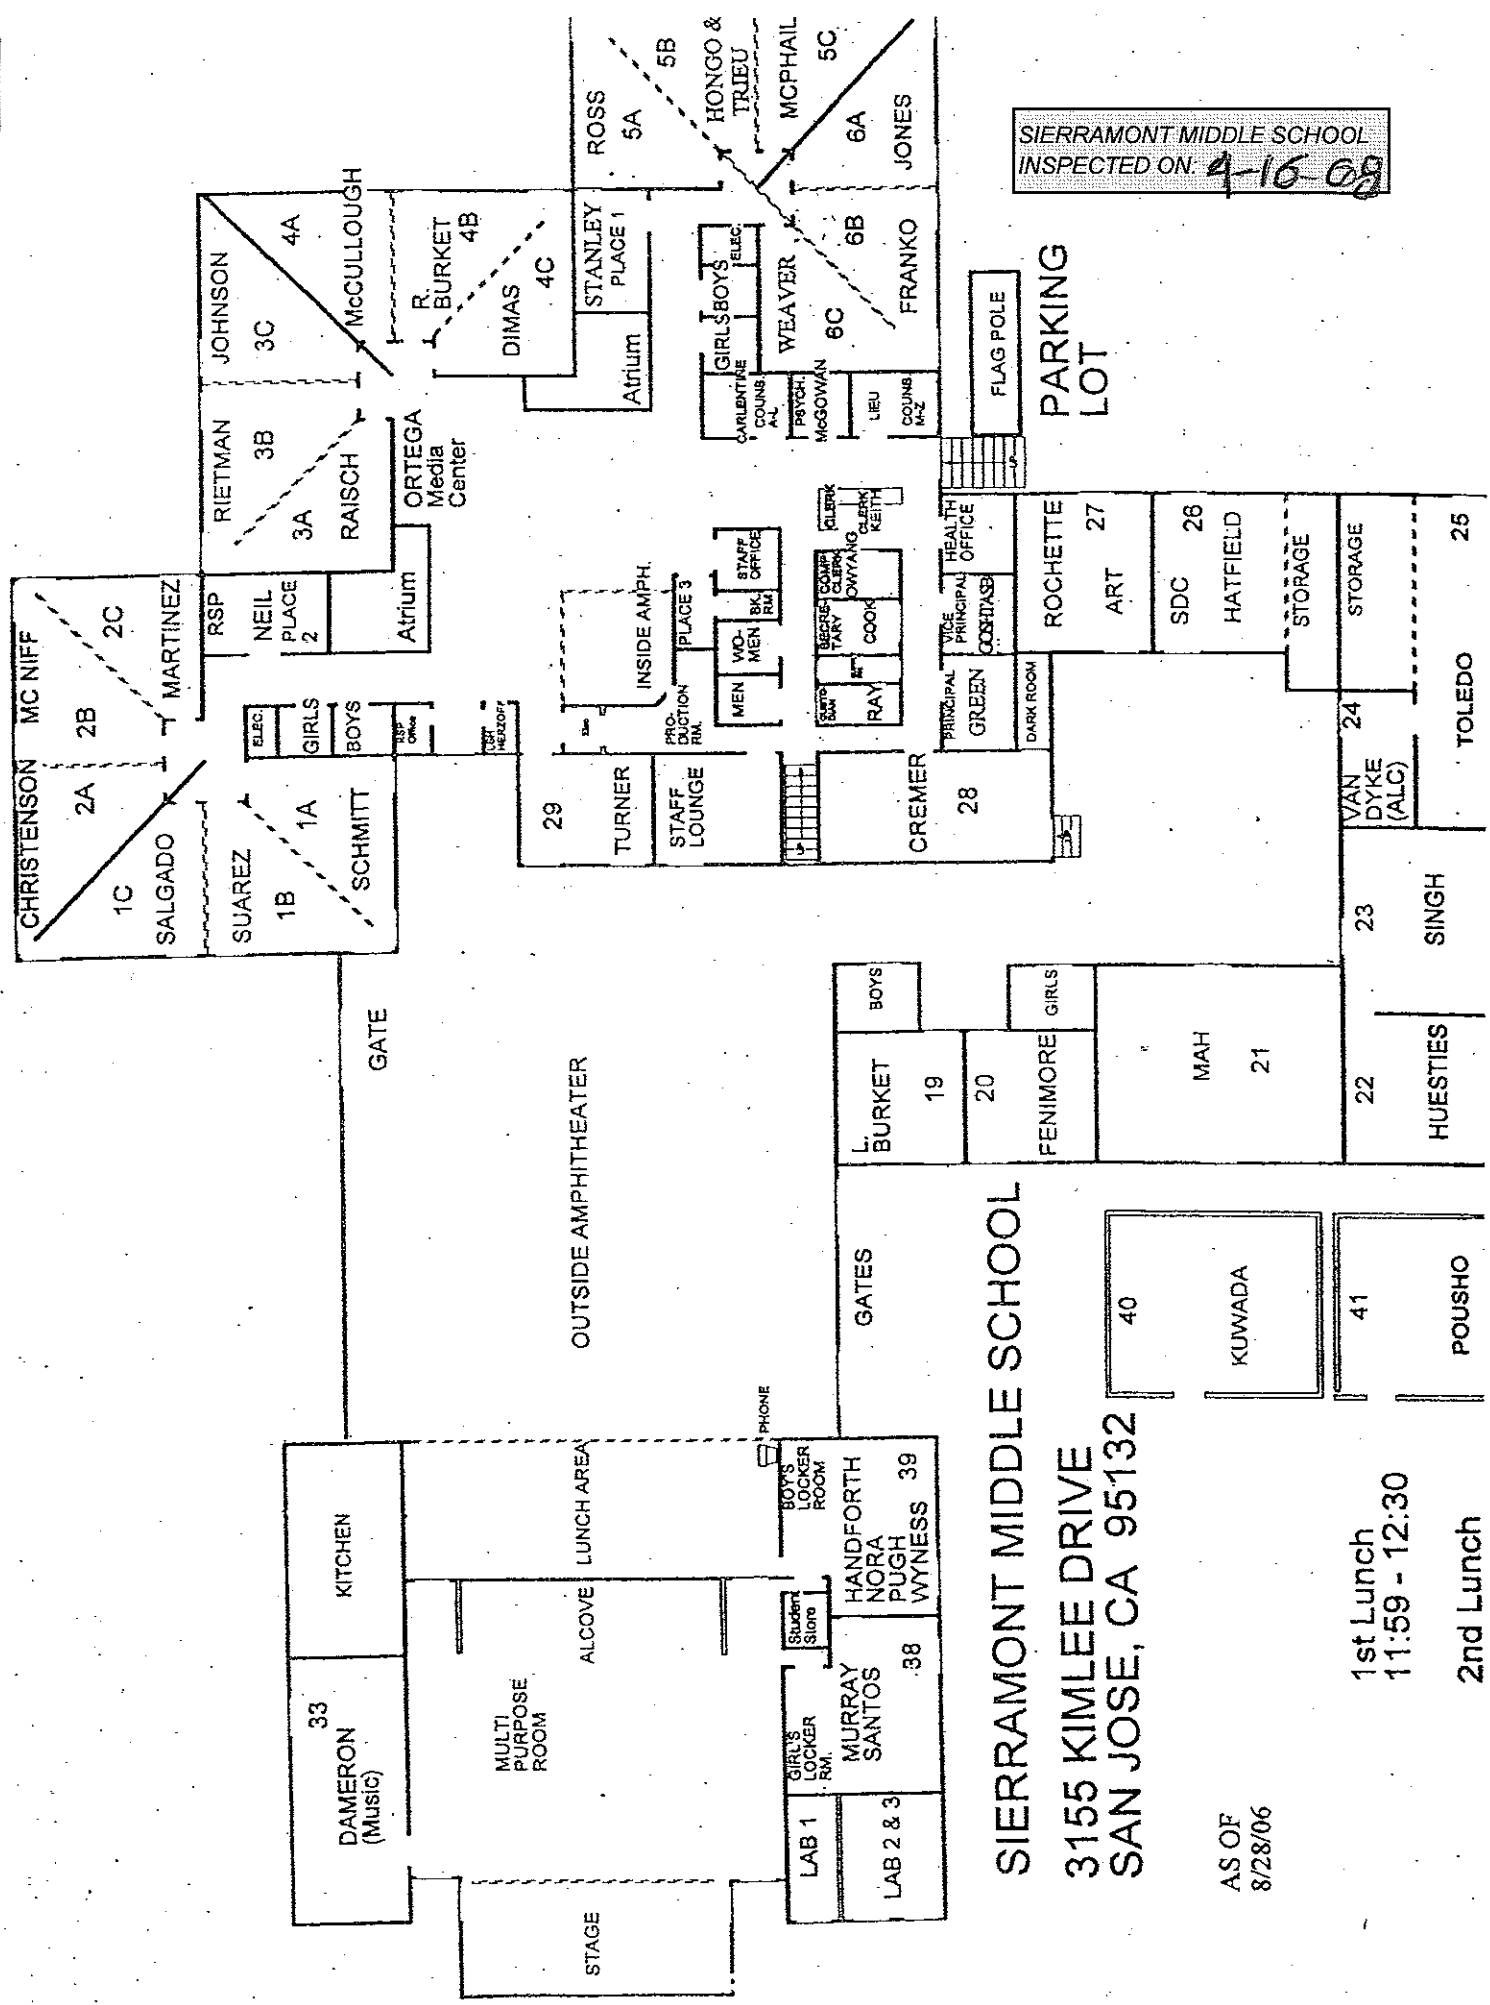

SIERRAMONT MIDDLE SCHOOL
3155 KIMLEE DRIVE
SAN JOSE, CA 95132

AS OF
8/28/06

1st Lunch
11:59 - 12:30
2nd Lunch

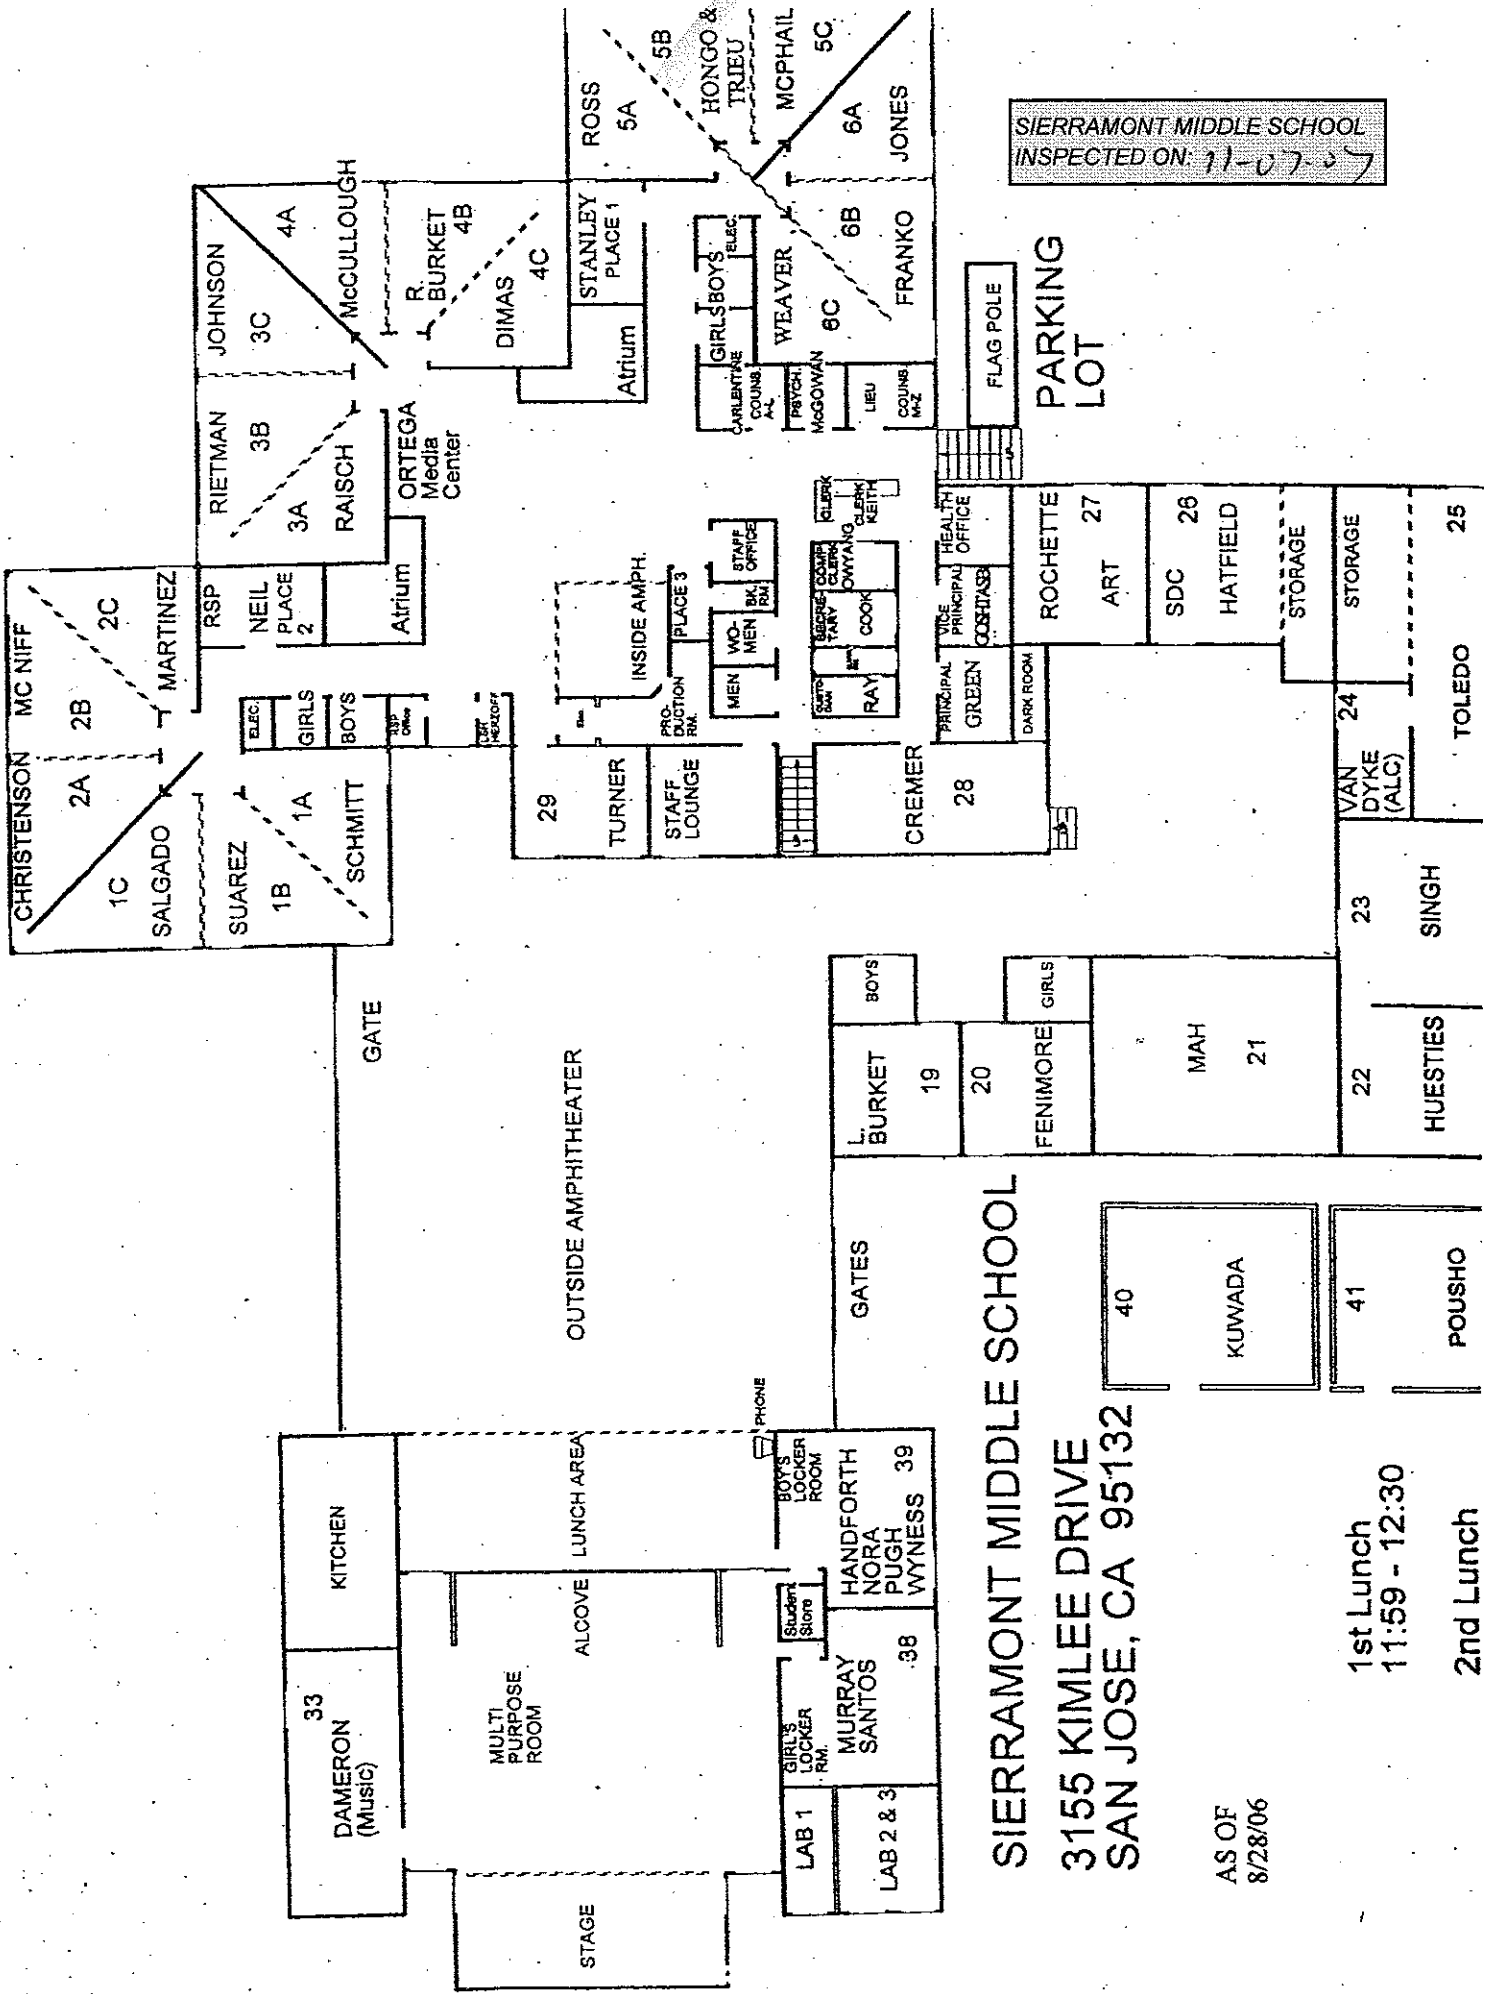


SIERRAMONT MIDDLE SCHOOL
INSPECTED ON 11-07-07

SIERRAMONT MIDDLE SCHOOL
3155 KIMLEE DRIVE
SAN JOSE, CA 95132

AS OF
8/28/06

1st Lunch
11:59 - 12:30

2nd Lunch

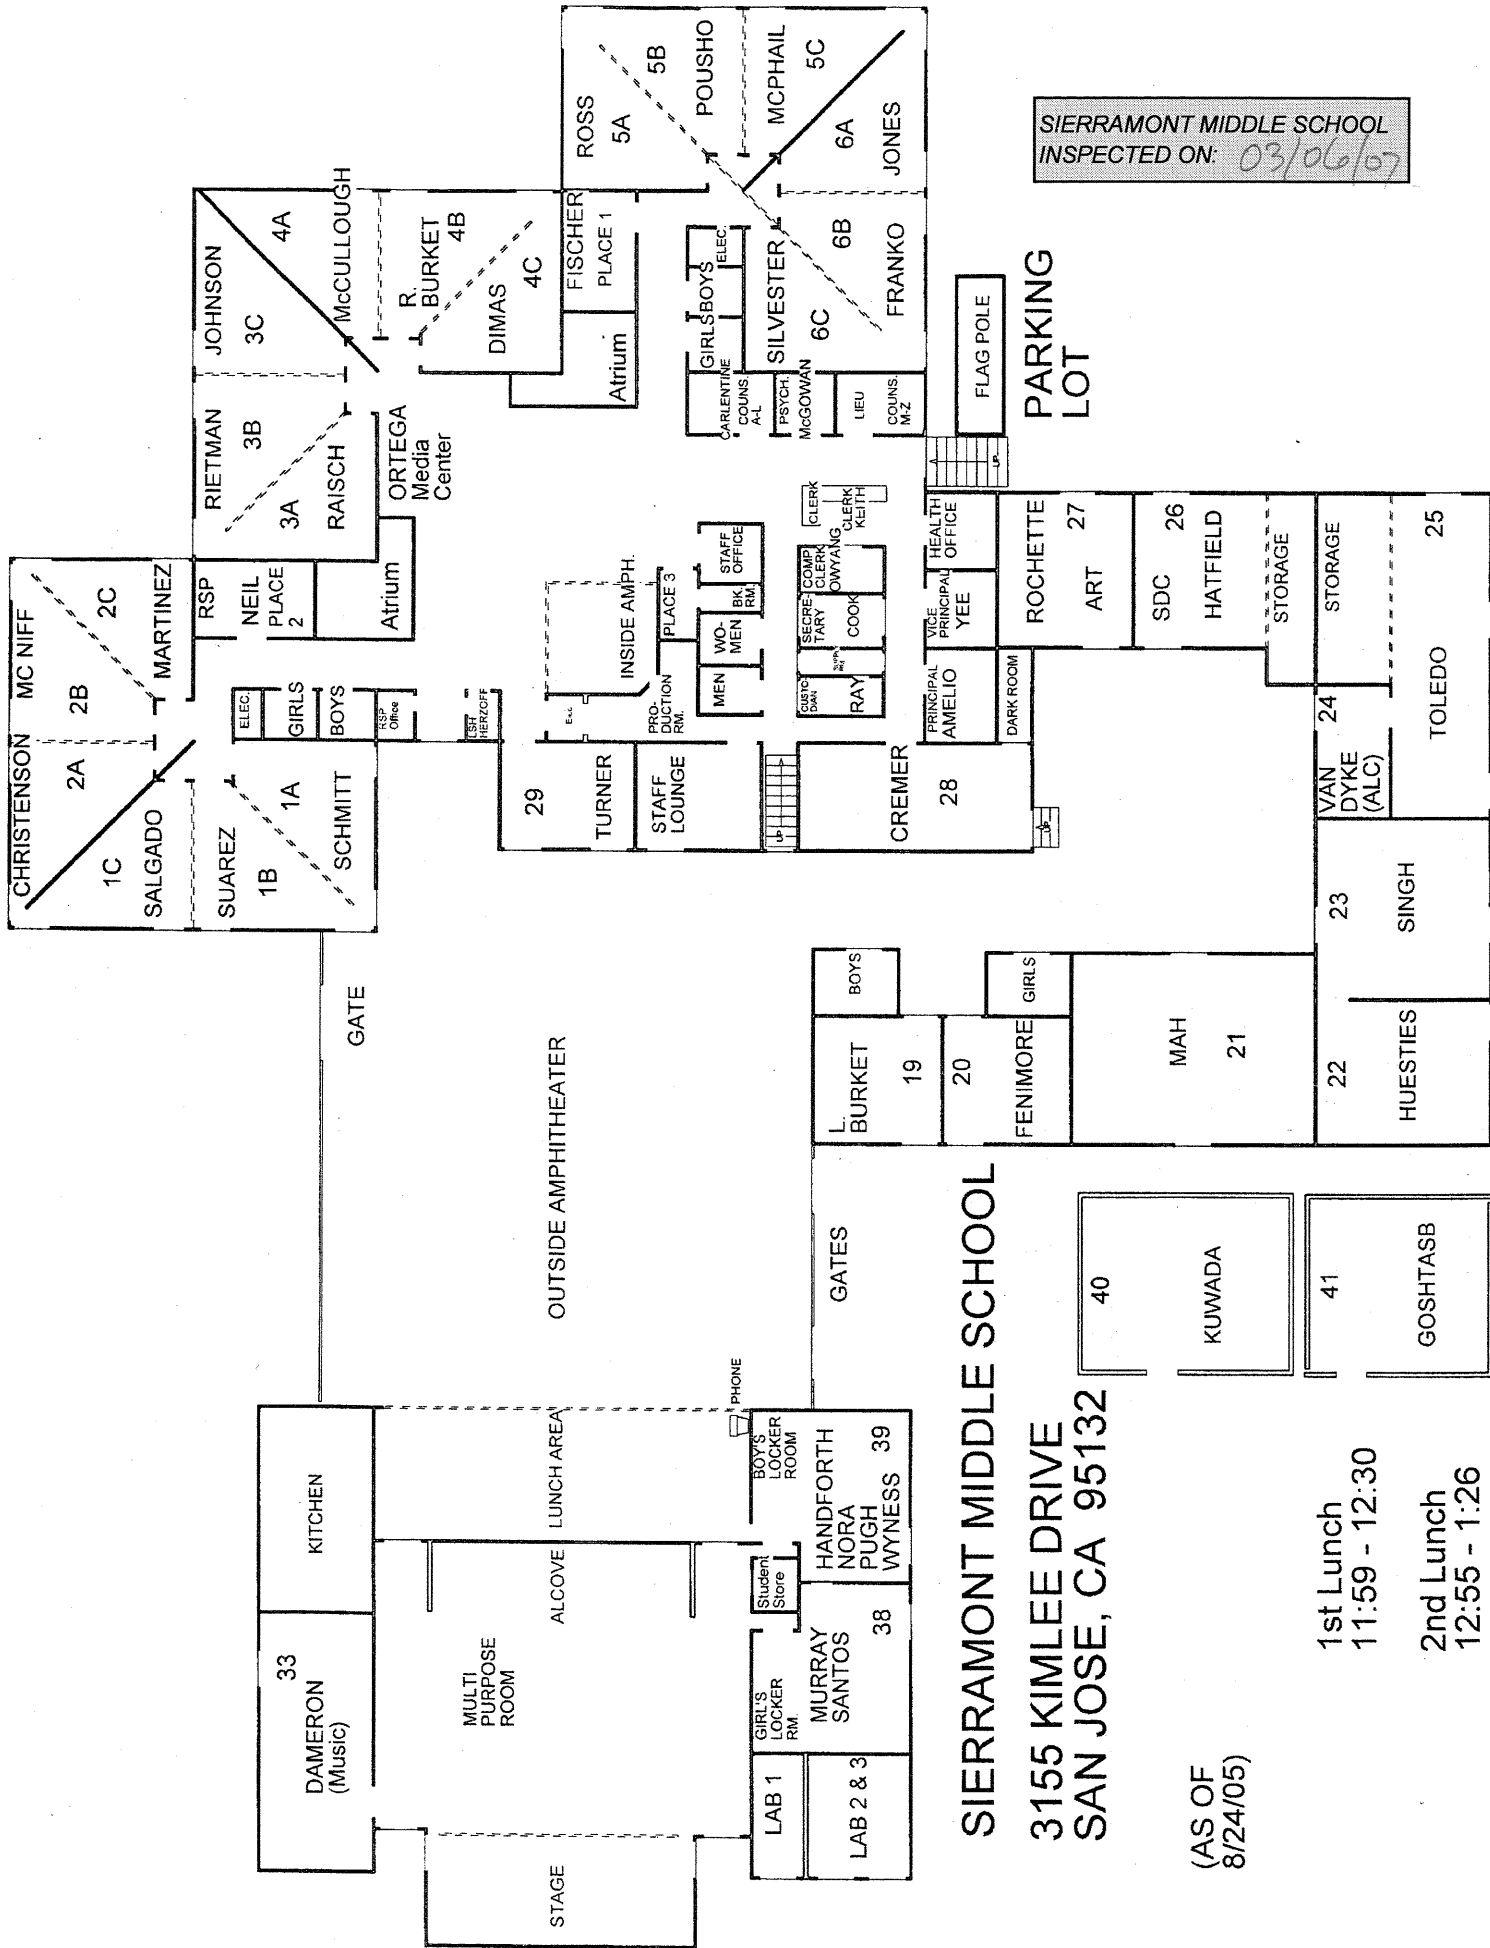

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 03/06/07


SIERRAMONT MIDDLE SCHOOL

3155 KIMLEE DRIVE
SAN JOSE, CA 95132

(AS OF
8/24/05)

1st Lunch
11:59 - 12:30

2nd Lunch
12:55 - 1:26

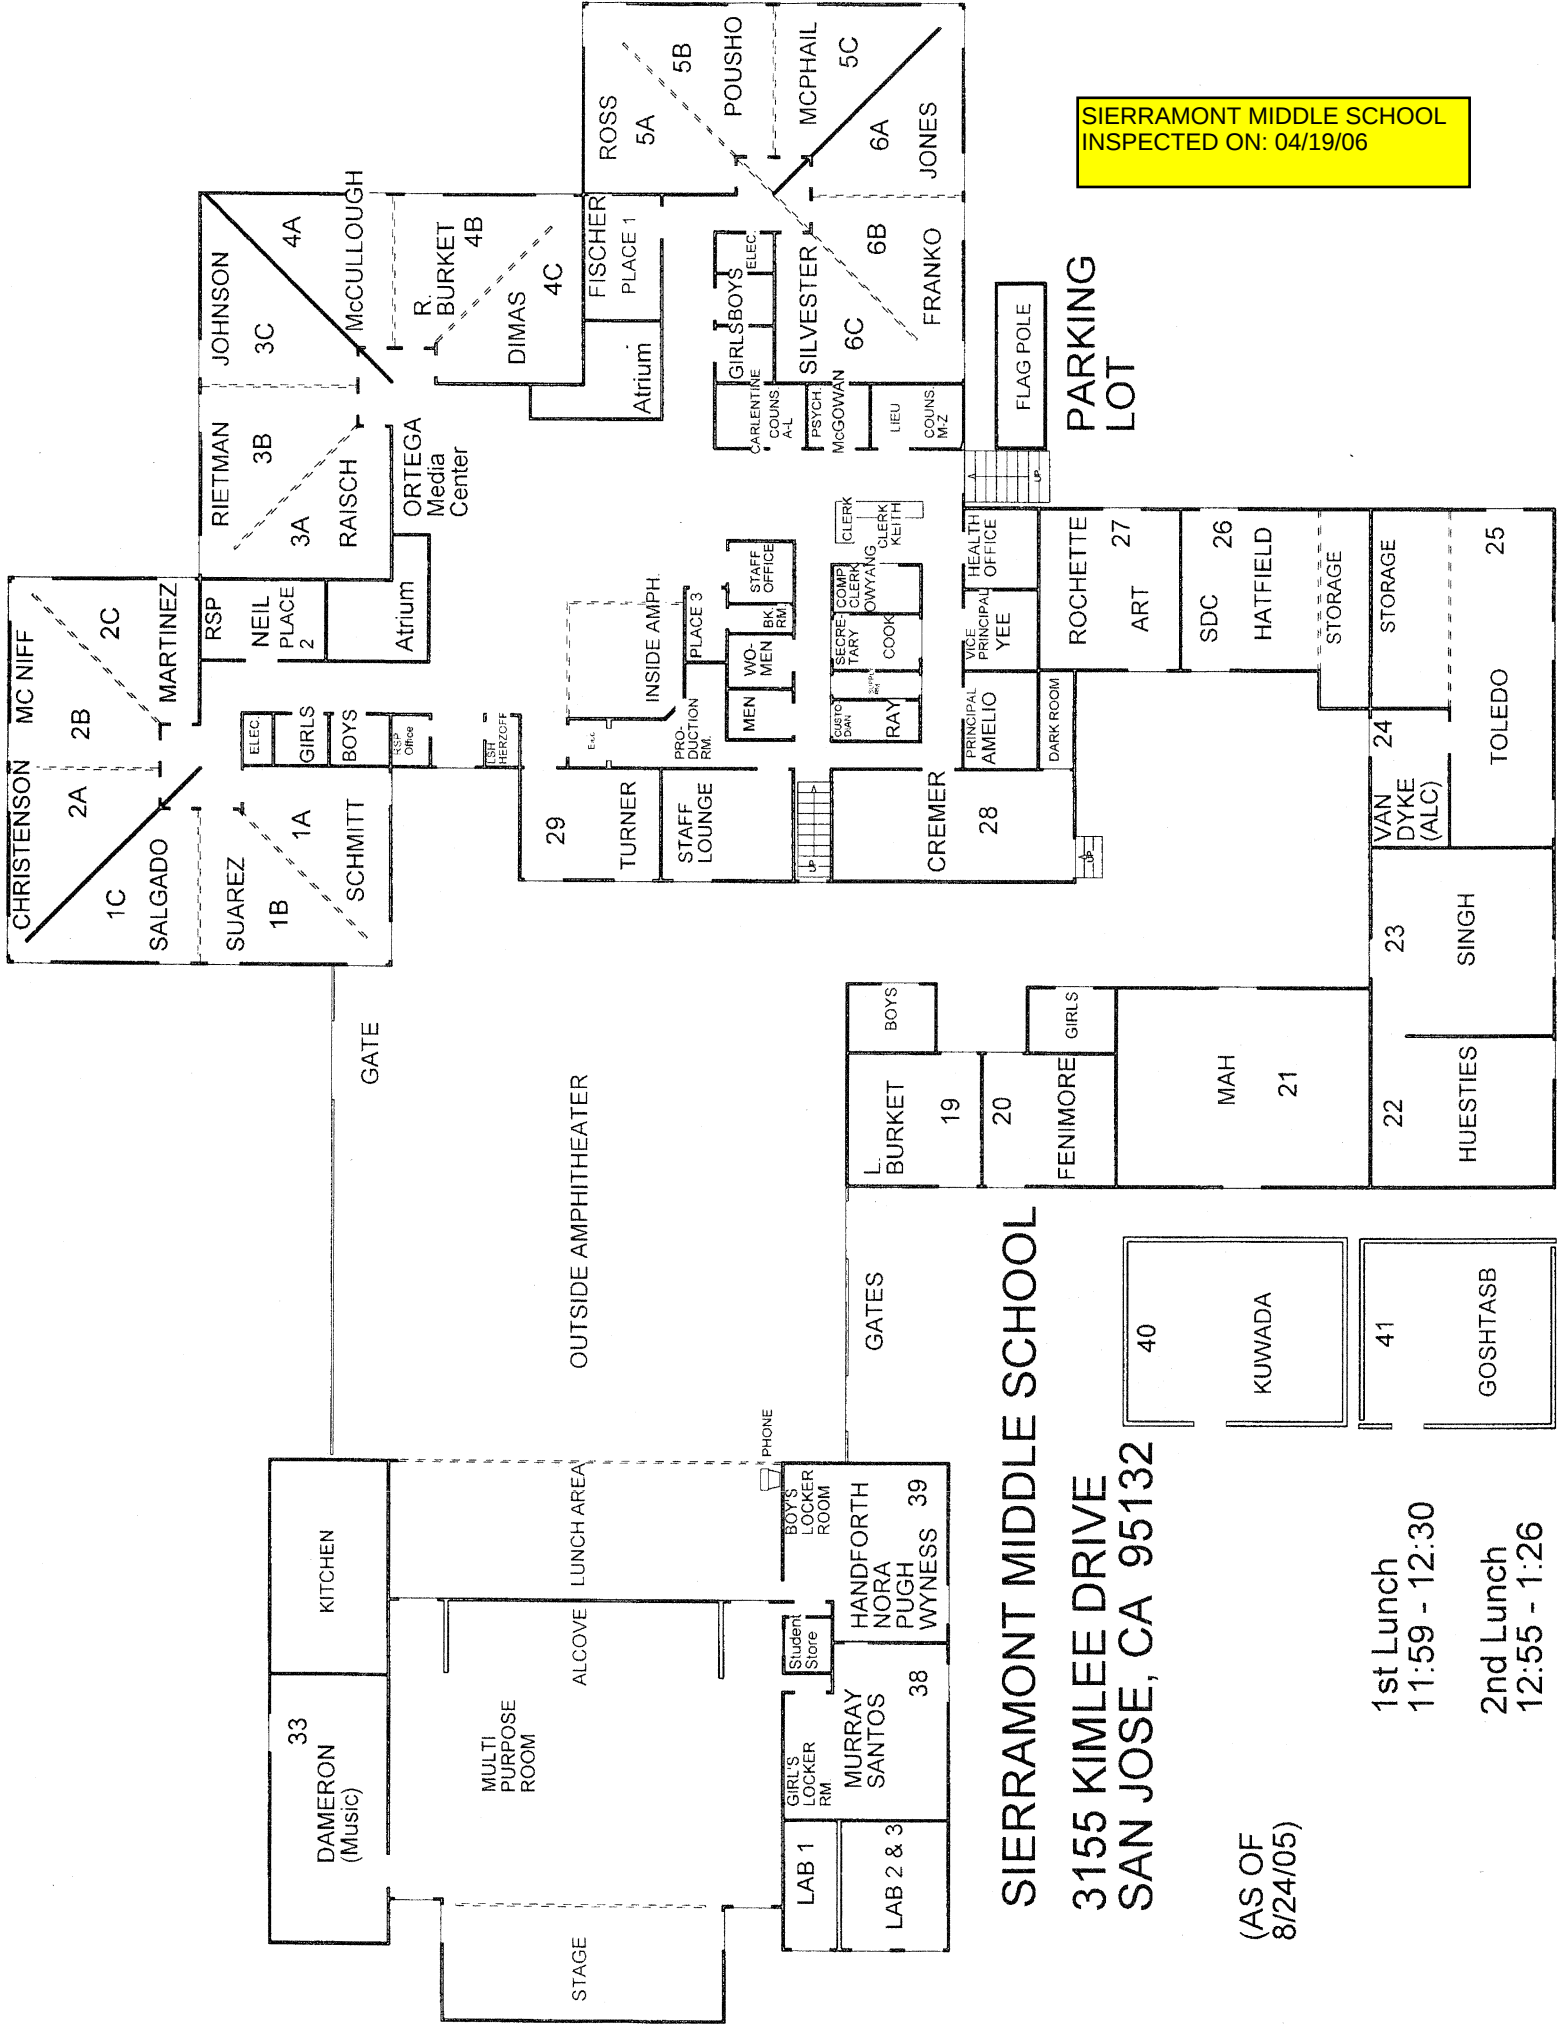

SIERRAMONT MIDDLE SCHOOL
INSPECTED ON: 04/19/06

SIERRAMONT MIDDLE SCHOOL
3155 KIMLEE DRIVE
SAN JOSE, CA 95132

(AS OF
8/24/05)

1st Lunch
11:59 - 12:30
2nd Lunch
12:55 - 1:26

