

SIX-MONTH SURVEILLANCE AHERA REPORT

**SUMMERDALE ELEMENTARY SCHOOL
1100 SUMMERDALE DRIVE
SAN JOSE, CA 95132**

**PREPARED FOR:
BERRYESSA UNION ELEMENTARY SCHOOL DISTRICT
981 RIDDER PARK DRIVE
SAN JOSE, CA 95131**

**INSPECTED ON:
SEPTEMBER 17, 2025**

HAZMAT DOC PROJECT #25-101

**PREPARED BY:
HAZMAT DOC
3080 OLCOTT STREET • SUITE D135
SANTA CLARA, CA 95054
Tel: 408.748.0055**

BERRYESSA UNION ELEMENTARY SCHOOL DISTRICT
SUMMERDALE ELEMENTARY SCHOOL

INSPECTED ON:
SEPTEMBER 17, 2025

INSPECTED BY:



Leland Kafeyan
Cal/OSHA Certified Site Surveillance Technician
Certification Number 06-4110

REPORTED BY:



Maheen B. Doctor
Cal/OSHA Certified Asbestos Consultant
Certification Number 95-1798

CONTENTS

PART - I

LEGEND AND GLOSSARY OF TERMS

PART – II

AHERA REPORT A – LIST OF BUILDINGS

PART – III

AHERA REPORT B – SURVEY REPORT

PART – IV

HOMOGENEOUS MATERIALS REPORT

PART – V

FRIABLE LOCATIONS REPORT

PART – VI

NON-FRIABLE LOCATIONS REPORT

PART – VII

RECOMMENDATIONS REPORT

PART – VIII

SAMPLES REPORT

PART – IX

DAMAGE REPORT

PART - X

SITE MAPS

LEGEND

THE FOLLOWING IS A LIST OF ABBREVIATIONS USED IN THIS REPORT:

Asbestos Sample Types

AC	=	ACTINOLITE
AM	=	AMOSITE
AN	=	ANTHOPHYLLITE
CH	=	CHRYBOTILE
CR	=	CROCIDOLITE
TR	=	TREMOLITE
ND	=	NONE DETECTED
NS	=	NO SAMPLE

Measurements

APPROX.	=	APPROXIMATELY
EA	=	EACH
I	=	INCHES
LF	=	LINEAR FEET
N	=	NUMBER
O.D.	=	OUTSIDE DIAMETER
SF	=	SQUARE FEET
TBD	=	TO BE DETERMINED

LIST OF BUILDINGS AT

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME BUILDING USED AS (#FLOORS) CONSTRUCTION		BUILDING AREA (APPROXIMATE)
CLASSROOMS 01 PORTABLE BUILDING		
Classroom (1) Wood and Metal Portable		960 SF
CLASSROOMS 02 PORTABLE BUILDING		
Classroom (1) Wood and Metal Portable		960 SF
CLASSROOMS 03 PORTABLE BUILDING		
Classroom (1) Wood and Metal Portable		960 SF
CLASSROOMS 04-07 PORTABLE BUILDING		
Classrooms (1) Wood and Metal Portables		3,840 SF
MAIN BUILDING		
Classrooms, Offices, Kitchen, Multi-Purpose Room, Library, Restrooms, Storages (1) Wood, Metal, Plaster, Gypsum Wallboard System, Concrete		29,700 SF
METAL STORAGE CONTAINERS		
Storage (1) Storage		640 SF
PLASTIC SHED STORAGE CONTAINER		
Storage (1) Hard Plastic		60 SF
Total Number Of Buildings : 7		(Approximate) Total Sq Ft. : 37,120
End Of Report, Total Of 1 Pages		

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

CLASSROOMS 01 PORTABLE BUILDING

CLASSROOMS 01 PORTABLE BUILDING

09/08/2005 BUILDING NOTES:

09/08/2005 Manufacturer's TAG Info: BY DESIGN MOBILE SYSTEM INC; DATE: 07/94; OSA# 61920; SERIAL# 3282-1, 3282-2. This Entry for informational and tracking purposes.

CLASSROOMS 01 PORTABLE BUILDING

PORTABLE 1

PORTABLE BUILDING

960 SF

09/08/2005 New 1994 Construction Relocatable Building per Manufacturer's Tag information.

03/05/2014 This Material is unchanged as of this date.

08/27/2014 This Material is unchanged as of this date.

03/17/2015 This Material is unchanged as of this date.

02/04/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212.NS NEW NO SAMPLE (NS)

SF=Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

CLASSROOMS 02 PORTABLE BUILDING

CLASSROOMS 02 PORTABLE BUILDING

09/08/2005 BUILDING NOTES:

09/08/2005 Manufacturer's TAG info: BY DESIGN MOBILE SYSTEM INC; DATE: 07/94; OSA# 61920; SERIAL# 3283-1, 3283-2. This entry for informational and tracking purposes.

CLASSROOMS 02 PORTABLE BUILDING

PORTABLE 2

PORTABLE BUILDING

960 SF

09/08/2005 New 1994 Construction relocatable building per Manufacturer's Tag information.

02/04/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212.NS	NEW	NO SAMPLE	(NS)
-----------	-----	-----------	--------

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

CLASSROOMS 03 PORTABLE BUILDING

CLASSROOMS 03 PORTABLE BUILDING

09/08/2005 BUILDING NOTES:

09/08/2005 Manufacturer's TAG Info:
BY AMERICAN MODULAR SYSTEM; DATE: 07/96; OSA# 65132; SERIAL# 96-R243-003A, 96-R243-003B.
This entry for informational and tracking purposes.

CLASSROOMS 03 PORTABLE BUILDING

PORTABLE 3

PORTABLE BUILDING

960 SF

09/08/2005 New 1996 Construction Relocatable Building per manufacturer's tag information.

02/04/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

05-212.NS	NEW	NO SAMPLE	(NS)
-----------	-----	-----------	--------

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

CLASSROOMS 04-07 PORTABLE BUILDING

CLASSROOMS 04-07 PORTABLE BUILDING

04/17/2006 BUILDING NOTES:

04/19/2006 Manufacturer's TAG Info:
BY AMERICAN MODULAR SYSTEM; DATE: 05/05; OSA# 01-107067; SERIAL#'S Portable 4 = 05-107-003A, 05-107-003B; Portable 5 = 05-107-006A, 05-107-006B; Portable 6 = 05-107-004A, 05-107-004B; Portable 7 = 05-107-005A, 05-107-005B.
This entry for informational and tracking purposes.

11/30/2011 Portable 5 is now Portable 7; Portable 6, now Portable 5; Portable 7, now Portable 6.

CLASSROOMS 04-07 PORTABLE BUILDING

PORTABLES 4-7

PORTABLE BUILDING

3,840 SF

09/08/2005 New 2005 Construction Relocatable Buildings per Manufacturer's Tag information.

02/08/2016 Sample 16-032-SA102 collected from Portable P7, Baseboard Off-White Mastic. Mastic/Adhesive for 4" Black Baseboard. Sample 16-032-SA103 collected from Portable P7, Carpet, Yellow Mastic. Mastic/Adhesive for 95% Gray Black Carpet and 5% Brown Carpet by Entry.

02/04/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

09/17/2025 This Material is unchanged as of this date.

16-032-SA103	ND	NONE DETECTED	(ND)
05-212.NS	NEW	NO SAMPLE	(NS)
16-032-SA102	ND	NONE DETECTED	(ND)

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME	
LOCATION	
MATERIAL TYPE	QTY (APPROXIMATE)
COMMENTS	

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

MAIN BUILDING

MAIN BUILDING

09/08/2005	BUILDING NOTES:
09/08/2005	Existing Gypsum Wallboard Systems Removed and Replaced with new in-kind in Path-of-Construction. Existing Plaster Systems Removed and Replaced with new in-kind in Path-of-Construction. New Flooring Finishes per information received from the BUESD. New Suspended Ceiling Tiles installed.
10/15/2008	New Ceramic Wall and Floor Tiles installed in Staff and Student Restrooms and on Drinking Fountain Walls per information received from BUESD.
11/30/2011	Following Classroom numbers have changed: B-1 now B-6; B-2 now B-5; B-3 now B-4 C-1 now C-7; C-2 now C-8; C-3 now C-9 D-1 now D-12; D-2 now D-11; D-3 now D-10 E-1 now E-13; E-2 now E-14; E-3 now E-15 F-1 now F-18; F-2 now F-17; F-3 now F-16.
09/18/2015	Following Classroom numbers have changed: B-4 is now B-1, B-5 is now B-2, B-6 is now B-3, C-7 is now C-1, C-8 is now C-2, C-9 is now C-3, C-10 is now D-1, C-11 is now D-2,, C-12 is now D-3, C-13 is now E-3, C-14 is now E-2, C-15 is now E-1, C-16 is now F-1, C-17 is now F-2, and C-18 is now F-3
03/29/2017	FIS POD D Renovation Project Finishes Replaced: Suspended Ceiling Tiles, Flooring, Grout/Mortar for 1'x 2' Gray Stone Ceramic Wall Tiles, Sinks with Thermal Undercoating, Vinyl Wall Cover, Pressed Wood Wall Panels, Wallboard System in path-of-construction. 2 Staff Restrooms (by Staff Lounge) and 2 Student Restrooms (Exterior Access): New Beige 1'x 2', New 6"x 6", and New Multi-Color 1'x 1' Wall Tiles installed. New Epoxy Flooring, and New Ceramic Wall Tiles installed.
08/18/2018	New Flooring Finishes installed Summer 2018 per information received from the BUESD. New Suspended Ceiling Tiles installed.
02/15/2023	New Green Epoxy Flooring installed in Exterior Restrooms (2 EA).

MAIN BUILDING

ALL ADMIN HALLWAYS, BOILER ROOM, KITCHEN, ELECTRICAL ROOM, MUSIC ROOM, STAGE, AND SDC ROOM

FIRE DOOR CORE INSULATION

525 SF

09/08/2005	Fire Door Core Insulation (25 EA Doors). This Material is in GOOD condition as of this date.
02/08/2016	Sample 16-032-SA043 collected from Main Building, Activity 69, Fire Door Core, White Insulation.

SF= Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
09/13/2016	Repairs Observed. Damages to Activity Room 67 (Interior), Lobby 1, and the Doorway between Hall 77 and Entry 16 Doors have been repaired during the Summer 2016 Modernization project. No other changes as of this date.		
02/04/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	Damage Observed. <5% Physical Damage - in the form of 1 EA Missing Screw White Core Insulation Exposed on Double Door to Main Entrance to Pod A. Material condition changed from GOOD to FAIR overall. Friability changed from Non-Friable to Friable. No other changes as of this date.		
08/17/2022	Additional Damage Observed. <5% Physical Damage in the form of 4 (EA) Small Screws Missing with White Core Insulation Exposed at Reading Room and Electrical Room Door. Double Door Gate House of Pod F has an Inside Cover Piece Missing with White Core Insulation Exposed. No other changes as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	Partial Repairs and Additional Damage Observed. The Damage to the Double Door Gate House of Pod F has been repaired. Additional Damage in the form of 2" Gouge with White Core Insulation Exposed due to the Chair Racks going in and out of the Chair Storage Room. Material remains in FAIR condition overall. No other changes as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

16-032-SA043	26%	CHRYSTILE	(CH)
05-212AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

ALL OFFICES, STORAGE ROOMS, LIBRARY, MULTI-PURPOSE ROOM, AND COURTYARD STORAGE CLOSETS (LOCATED OUTSIDE PODS A-F)

SMOOTH WALL MISCELLANEOUS

34,860 SF

09/08/2005 Gypsum Wallboard System Walls and Ceilings, (under Skim Coat, Vinyl Wall Coverings, Suspended Ceiling Tiles, and 1'x 1' Wall and Ceiling Tiles in some areas). This Material is in GOOD condition as of this date.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
04/16/2008	<10% Water Damage. Water Damage observed in Pods A, C, and D under 1'x1' Ceiling Tiles as of this date. Material is in FAIR condition overall. Material changed from Non-Friable to Friable. No other changes as of this date.		
03/10/2010	Additional Damage: <5% Physical Damage - in the form of approx. 1 SF of the Wall has been cut and removed in Electrical Room of Pod D. No other changes as of this date.		
02/08/2016	Sample 16-032-SA003 collected from Main Building, Classroom 38, Wall Joint Tape and Mud for Gypsum Board. Sample 16-032-SA004 collected from Main Building, Classroom 38, Wall Gypsum Board. Sample 16-032-SA013 collected from Main Building, Classroom 55, Wall Joint Tape and Mud. Sample 16-032-SA014 collected from Main Building, Classroom 55, Wall Gypsum Board. Sample 16-032-SA026 collected from Main Building, Toilet-59, Wall Joint Tape and Mud for Gypsum Board. Sample 16-032-SA027 collected from Main Building, Toilet-59, Ceiling Gypsum Board. Sample 16-032-SA035 collected from Main Building, Classroom 70, Wall Joint Tape and Mud for Gypsum Board. Sample 16-032-SA036 collected from Main Building, Classroom 70, Wall Gypsum Board. Sample 16-032-SA053 collected from Main Building, Girls Restroom 88, Upper Wall Joint Tape and Mud for Gypsum Board. Sample 16-032-SA054 collected from Girls Restroom 88, Upper Wall Gypsum Board. Sample 16-032-SA067 Main Building, Platform-93, Wall Joint Tape and Mud for Gypsum Board. Sample 16-032-SA068 Main Building, Platform-93, Wall Gypsum Board. Sample 16-032-SA083, Main Building, Janitor-4, Wall Joint Tape and Mud for Gypsum Board. Sample 16-032-SA084, Main Building, Janitor-4, Wall Gypsum Board. Sample 16-032-SA021 collected from Main Building, Activity 53, Ceiling Gypsum Board.		
03/17/2016	Additional Damage observed. 1 SF of Physical Damage in Multi-Purpose Room. No other changes as of this date.		
08/29/2017	Additional Damage Observed. Ceiling Tiles now have Water Damage. No other changes as of this date.		
02/04/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

SF= Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
16-032-SA003	ND	NONE DETECTED	(ND)
16-032-SA004	ND	NONE DETECTED	(ND)
16-032-SA003	ND	NONE DETECTED	(ND)
16-032-SA013	ND	NONE DETECTED	(ND)
16-032-SA013	ND	NONE DETECTED	(ND)
16-032-SA014	ND	NONE DETECTED	(ND)
16-032-SA026	ND	NONE DETECTED	(ND)
16-032-SA026	ND	NONE DETECTED	(ND)
16-032-SA036	ND	NONE DETECTED	(ND)
16-032-SA027	ND	NONE DETECTED	(ND)
16-032-SA035	ND	NONE DETECTED	(ND)
16-032-SA035	ND	NONE DETECTED	(ND)
16-032-SA053	ND	NONE DETECTED	(ND)
16-032-SA053	ND	NONE DETECTED	(ND)
16-032-SA054	ND	NONE DETECTED	(ND)
16-032-SA067	ND	NONE DETECTED	(ND)
16-032-SA067	ND	NONE DETECTED	(ND)
16-032-SA068	ND	NONE DETECTED	(ND)
16-032-SA083	ND	NONE DETECTED	(ND)
16-032-SA083	ND	NONE DETECTED	(ND)
16-032-SA084	ND	NONE DETECTED	(ND)
16-032-SA021	ND	NONE DETECTED	(ND)
05-212AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

ALL OFFICES, STORAGE ROOMS, LIBRARY, MULTI-PURPOSE ROOM, AND COURTYARD STORAGE CLOSETS
(LOCATED OUTSIDE PODS A-F)

SMOOTH WALL SURFACING

34,860 SF

- 08/24/2006 Skim Coat for Gypsum Wallboard System Walls and Ceilings, (under Skim Coat, Vinyl Wall Coverings, Suspended Ceiling Tiles, and 1'x 1' Wall and Ceiling Tiles in some areas). This Material is in GOOD condition as of this date.
- 04/16/2008 <10% Water Damage. Water Damage observed in Pods A, C, and D under 1'x1' Ceiling Tiles as of this date. Material is in FAIR condition overall. Material changed from Non-Friable to Friable. No other changes as of this date.
- 03/10/2010 Additional Damage: <5% Physical Damage - in the form of approx. 1 SF of the Wall has been cut and removed in Electrical Room of Pod D. No other changes as of this date.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

02/08/2016	Sample 16-032-SA002 collected from Main Building, Classroom 38, Wall Skim Coat and Paint for Gypsum Board. Sample 16-032-SA012 collected from Main Building, Classroom 55, Wall Skimcoat and Paint for Gypsum Board. Sample 16-032-SA025 collected from Main Building, Toilet-59, Ceiling Skimcoat and Paint for Gypsum Board. Sample 16-032-SA034 collected from Main Building Classroom 70, Wall Skimcoat and Paint for Gypsum Board. Sample 16-032-SA052 collected from Main Building, Girls Restroom-88, Upper Wall Skimcoat Skimcoat and Paint for Gypsum Board. Sample 16-032-SA060 collected from Main Building, Boys Restroom-89, Wall Old Skimcoat and Paint for Wood Panel. Sample 16-032-SA066 Main Building, Platform-93, Wall Skimcoat and Paint for Gypsum Board. Sample 16-032-SA082 Main Building, Janitor-4, Wall Skimcoat and Paint for Gypsum Board.		
03/17/2016	Additional Damage observed. 1 SF of Physical Damage in Multi-Purpose Room. No other changes as of this date.		
09/13/2016	Repairs Observed. Damages in Chair Storage Room have been repaired as of this date. Material remains in FAIR condition. No other changes as of this date.		
08/29/2017	Additional Damage Observed. Ceiling Tiles now have Water Damage. No other changes as of this date.		
02/04/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

16-032-SA002	ND	NONE DETECTED	(ND)
16-032-SA012	ND	NONE DETECTED	(ND)
16-032-SA025	ND	NONE DETECTED	(ND)
16-032-SA034	ND	NONE DETECTED	(ND)
16-032-SA052	ND	NONE DETECTED	(ND)
16-032-SA060	ND	NONE DETECTED	(ND)

SF= Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
16-032-SA082	ND	NONE DETECTED	(ND)
16-032-SA066	ND	NONE DETECTED	(ND)
06-223AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

ALL POD AREAS, PREP AREAS, MULTI-PURPOSE ROOM, STAGE, SDC ROOM, AND HALLWAYS TO MULTI-PURPOSE ROOM

CEILING TILE

7,650 SF

09/08/2005	1'x 1' Glued-on Ceiling Tiles (with Pitted Mark Pattern). This Material is in GOOD condition as of this date.
04/16/2008	Damage: <5% Physical Damage and <10% Water Damage due to 8 additional Tiles are Water Damage observed in Pod C and these Tiles are coming loose as of this date. Material condition changed from GOOD to FAIR overall. No other changes as of this date.
05/13/2009	Material Re-Assessed. Pod A has 2 Tiles that are becoming loose. <10% Water Damage due to Pod A has 3 Tiles with Water stains. Pod C has 7 Tiles Water stained. No other changes as of this date.
03/10/2010	Additional Damage observed in the form of E Pod has 1 Tile Water Damaged. Also, several Tiles are Physically Damaged in a Classroom in Multi-Purpose room. No other changes as of this date.
09/01/2010	Additional Damage observed. 6 SF Tiles missing on Hatch Door by Boiler Room exposing the Mastic/Adhesive. 2 Tiles Damaged in the Hallway to the Multi-Purpose Room by the Kitchen. 1 Tile is Missing in the Teachers Work Room in Pod D, exposing the Mastic/Adhesive. No other changes as of this date.
11/30/2011	Additional Damage - in the form of Multipurpose Room has 2 Tiles with holes. Pod C has an additional 2 Tiles with Water Damage. Pod A, previously had 3 Tiles with Water stains, now has 1 Tile only Water stained. No other changes as of this date.
10/10/2012	Additional Damage - in the form of Pod D has 4 Water Damaged Ceiling Tiles. No other changes as of this date.
03/17/2015	POD A & D each have 1 Ceiling Tile missing, and Brown Mastic/Adhesive is exposed. No other changes as of this date.
09/18/2015	Additional Damage observed, Hallway outside of Kitchen has 2 Tiles Physically Damaged. No other changes as of this date.
02/08/2016	Sample 16-032-SA19 collected from Main Building, Activity 53, 1'x1' Ceiling Tile. Sample 16-032-SA044 collected from Main Building, Activity 61, 1'x1' Ceiling Tile. Sample 16-032-SA080 collected from Main Building, Entry-82, 1'x1' Pitted Mark Ceiling Tile. Sample 16-032-SA092 collected from Main Building, Activity-29, 1'x1' Pitted Mark Ceiling Tile.
03/17/2016	Additional Damage observed. 1 Tile is missing in A Pod Work Room exposing Mastic/Adhesive. C Pod Work Room has 10 Tiles with Water Damage; E Pod Work Room has 1 Tile with Water Damage. F Pod Work Room has 1 Tile loose. No other changes as of this date.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
09/13/2016	Additional Damage observed. <10% Water Damage - in the form of 10 Tiles with Water Damage in the Multi-Purpose Room. No other changes as of this date.		
03/29/2017	Material Re-assessed. Water Damage in Multi-Purpose Room painted over. Additional Damage Observed. 7 Tiles loose and 7 Tiles have Water Stains in the Multi-Purpose Room. No other changes as of this date.		
08/29/2017	Additional Damage Observed. C-Pod now has 9 Tiles with Water Damage. Access Door has 1 Tile with Physical Damage. No other changes as of this date.		
08/08/2018	Additional Damage Observed. F-Pod now has 1Tile Missing on Hatch Door and 12 Tiles have Surface Damage. No other changes as of this date.		
08/14/2019	Additional Damage Observed. <5% Physical Damage in the form of 1 SF of Tiles with Stains in each one of the Activity Rooms of Pod A and Pod C. Material Condition remains in FAIR condition overall. No other changes as of this date.		
02/04/2020	Additional Damage Observed. 1 Tile Missing Mastic Exposed in Pod A. No other changes as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		
16-032-SA019	ND	NONE DETECTED	(ND)
16-032-SA080	ND	NONE DETECTED	(ND)
16-032-SA092	ND	NONE DETECTED	(ND)
05-212AAA	ASSUMED	NO SAMPLE	(NS)

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

MAIN BUILDING

ALL POD AREAS, PREP AREAS, MULTI-PURPOSE ROOM, STAGE, SDC ROOM, AND HALLWAYS TO MULTI-PURPOSE ROOM

CEILING TILE MASTIC

7,650 SF

09/08/2005	Mastic/Adhesive for 1'x 1' Glued-on Ceiling Tiles (with Pitted Mark Pattern). This Material is in GOOD condition as of this date.
04/16/2008	Damage: <5% Physical Damage and <10% Water Damage due to 8 additional Tiles are Water Damage observed in Pod C and these Tiles are coming loose as of this date. Material condition changed from GOOD to FAIR overall. Material changed from Non to Friable. No other changes as of this date.
05/13/2009	Material Re-Assessed. Pod A has 2 Tiles that are becoming loose. <10% Water Damage due to Pod A has 3 Tiles with Water stains. Pod C has 7 Tiles Water stained. No other changes as of this date.
03/10/2010	Additional Damage observed in the form of E Pod has 1 Tile Water Damaged. Also, several Tiles are Physically Damaged in a Classroom in Multi-Purpose room. No other changes as of this date.
09/01/2010	Additional Damage observed. 6 SF Tiles missing on Hatch Door by Boiler Room exposing the Mastic/Adhesive. 2 Tiles Damaged in the Hallway to the Multi-Purpose Room by the Kitchen. 1 Tile is Missing in the Teachers Work Room in Pod D, exposing the Mastic/Adhesive. No other changes as of this date.
11/30/2011	Additional Damage - in the form of Multipurpose Room has 2 Tiles with holes. Pod C has an additional 2 Tiles with Water Damage. Pod A, previously had 3 Tiles with Water stains, now has 1 Tile only Water stained. No other changes as of this date.
10/10/2012	Additional Damage - in the form of Pod D has 4 Water Damaged Ceiling Tiles. No other changes as of this date.
03/17/2015	POD A & D each have 1 Ceiling Tile missing, and Brown Mastic/Adhesive is exposed. No other changes as of this date.
09/18/2015	Additional Damage observed, Hallway outside of Kitchen has 2 Tiles Physically Damaged. No other changes as of this date.
02/08/2016	Sample 16-032-SA020 collected from Main Building, Activity 53, Brown Mastic for 1'x1' Ceiling Tile. Sample 16-032-SA045 collected from Main Building, Activity 61, 1'x1' Ceiling Tile Brown Mastic. Sample 16-032-SA081 collected from Main Building, Entry-82, 1'x1' Pitted Mark Ceiling Tile, Brown Mastic. Sample 16-032-SA093 collected from Main Building, Activity-29, 1'x1' Pitted Mark Ceiling Tile, Brown Mastic.
03/17/2016	Additional Damage observed. 1 Tile is missing in A Pod Work Room exposing Mastic/Adhesive. C Pod Work Room has 10 Tiles with Water Damage; E Pod Work Room has 1 Tile with Water Damage. F Pod Work Room has 1 Tile loose. No other changes as of this date.
09/13/2016	Additional Damage observed. <10% Water Damage - in the form of 10 Tiles with Water Damage in the Multi-Purpose Room. No other changes as of this date.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
03/29/2017	Material Re-assessed. Water Damage in Multi-Purpose Room painted over. Additional Damage Observed. 7 Tiles loose and 7 Tiles have Water Stains in the Multi-Purpose Room. No other changes as of this date.		
08/29/2017	Additional Damage Observed. C-Pod now has 9 Tiles with Water Damage. Access Door has 1 Tile with Physical Damage. No other changes as of this date.		
08/08/2018	Additional Damage Observed. F-Pod now has 1Tile Missing on Hatch Door and 12 Tiles have Surface Damage. No other changes as of this date.		
08/14/2019	Additional Damage Observed. <5% Physical Damage in the form of 1 SF of Tiles with Stains in each one of the Activity Rooms of Pod A and Pod C. Material Condition remains in FAIR condition overall. No other changes as of this date.		
02/04/2020	Additional Damage Observed. 1 Tile Missing Mastic Exposed in Pod A. No other changes as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

16-032-SA020	ND	NONE DETECTED	(ND)
16-032-SA045	ND	NONE DETECTED	(ND)
16-032-SA081	ND	NONE DETECTED	(ND)
16-032-SA093	ND	NONE DETECTED	(ND)
05-212AAA	ASSUMED	NO SAMPLE	(NS)

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

MAIN BUILDING

ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS

PRESSED WOOD WALL PANEL

22,000 SF

09/08/2005	4'x8' Pressed Wood Walls (with Vinyl Cover). This Material is in GOOD condition as of this date.
02/04/2020	This Material is unchanged as of this date.
08/28/2020	Damage Observed. <5% Physical Damage in the form of 2 LF of Broken Wall Panel in Prep Areare of D-Pod. Material condition changed from GOOD to FAIR overall. Friability updated from Non-Friable to Friable. No other changes as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MAIN BUILDING

ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS

PRESSED WOOD WALL PANEL MASTIC

22,000 SF

09/08/2005	Mastic/Adhesive for 4'x8' Pressed Wood Walls (with Vinyl Cover). This Material is in GOOD condition as of this date.
02/04/2020	This Material is unchanged as of this date.
08/28/2020	Damage Observed. <5% Physical Damage in the form of 2 LF of Broken Wall Panel in Prep Areare of D-Pod. Material condition changed from GOOD to FAIR overall. Friability updated from Non-Friable to Friable. No other changes as of this date.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
02/10/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		
05-212AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS

VINYL WALL COVER MASTIC

22,000 SF

09/08/2005	Mastic/Adhesive for Vinyl Wall Covering on 4'x 8' Pressed Wood Wall Panels. This Material is in GOOD condition as of this date.
02/08/2016	Sample 16-032-SA006 collected from Main Building, Classroom 38, Wall Vinyl Wall Covered Mastic and Fiberboard. Sample 16-032-SA016 collected from Main Building, Classroom 55, Wall Vinyl Wall Covered Yellow Mastic and Fiberboard. Sample 16-032-SA038 collected from Main Building, Classroom 70, Wall Vinyl Wall Covered, Fiberboard and Mastic only. Sample 16-032-SA070 collected from Main Building, SDC-96, Wall Vinyl Wall Covered Adhesive and Compound only.
02/04/2020	This Material is unchanged as of this date.
08/28/2020	Damage Observed. <5% Physical Damage in the form of 2 LF of Broken Wall Panel in Prep Areare of D-Pod. Material condition changed from GOOD to FAIR overall. Friability updated from Non-Friable to Friable. No other changes as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

16-032-SA006	ND	NONE DETECTED	(ND)
16-032-SA006	ND	NONE DETECTED	(ND)
16-032-SA016	ND	NONE DETECTED	(ND)
16-032-SA016	ND	NONE DETECTED	(ND)
16-032-SA038	ND	NONE DETECTED	(ND)
16-032-SA070	ND	NONE DETECTED	(ND)
16-032-SA070	ND	NONE DETECTED	(ND)
05-212AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

COURTYARDS (LOCATED OUTSIDE PODS A-F)

SINK UNDERCOATING

30 SF

03/10/2010 Beige Thermal Undercoating on Sink. (6 EA Sinks). (No cabinets present). This Material is in GOOD condition as of this date. (Original entry updated on 10/10/12.)

09/01/2010 This Material is unchanged as of this date. Some sinks are in cabinets.

10/10/2012 Undercoating is Beige. Original entry updated. No other changes as of this date.

02/04/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		
10-052AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

EXTERIOR WALLS

ROUGH WALL

21,750 SF

09/08/2005	Stucco Walls. This Material is in good condition as of this date.		
02/04/2020	This Material is unchanged as of this date.		
08/28/2020	Damage Observed. <5% Physical Damage in the form of 1 Inch Hole in Wall near Rear Entry into D-2. Material condition changed from GOOD to FAIR overall. Friability updated from Non-Friable to Friable. No other changes as of this date.		
02/10/2021	Additional Damage Observed. 3 LF of Cracks near Entry to Kitchen. No other changes as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

MAIN BUILDING

EXTERIOR WALLS

ROUGH WALL SURFACING

21,750 SF

09/08/2005	Skim Coat for Stucco Walls. This Material is in good condition as of this date.		
02/04/2020	This Material is unchanged as of this date.		
08/28/2020	Damage Observed. <5% Physical Damage in the form of 1 Inch Hole in Wall near Rear Entry into D-2. Material condition changed from GOOD to FAIR overall. Friability updated from Non-Friable to Friable. No other changes as of this date.		
02/10/2021	Additional Damage Observed. 3 LF of Cracks near Entry to Kitchen. No other changes as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

05-212AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MAIN BUILDING

LIBRARY OFFICE

CEMENTITIOUS WALL PANEL

16 SF

03/10/2010	Brown Cementitious Chalkboard. (1 EA). This Material is in GOOD condition as of this date.		
02/04/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		
10-052AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

LIBRARY OFFICE

CEMENTITIOUS WALL PANEL MASTIC

16 SF

03/10/2010	Mastic/Adhesive for Brown Cementitious Chalkboard. (1 EA). This Material is in GOOD condition as of this date.		
02/04/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

10-052AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

MAIN BUILDING

LOUNGE, HALLWAY, OFFICES, LOBBY, STAGE, CLASSROOMS

VINYL WALL COVER MASTIC

4,000 SF

09/01/2010 Mastic/Adhesive for Vinyl Wall Cover (over Sheetrock Walls). This Material is in GOOD condition as of this date.

02/04/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 Damage Observed. <5% Physical Damage - in the form of 1 SF Peeling with Light Brown Mastic Exposed in Kitchen and Multipurpose Room. Material condition changed from GOOD to FAIR overall. Friability changed from Non-Friable to Friable. No other changes as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

10-174AAA	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

MAIN BUILDING

MAIN ELECTRICAL PANEL ROOM, AND CONCEALED LOCATIONS

PIPE FITTING INSULATION

2 LF

11/05/2007	Thermal System Insulation on Pipe Fittings. (2 EA Fittings Type). Additional Fittings may be located in the Planum, Attic, and other inaccessible area/spaces. Damage: <50% Physical Damage - due to 1 fitting being in POOR condition. This Material is in FAIR condition as of this date.		
04/16/2008	Damaged fitting has been sealed and wrapped with duct tape as a temporary measure. No other changes as of this date.		
02/04/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

07-043AAA

ASSUMED

NO SAMPLE

(NS)

MAIN BUILDING

MULTI-PURPOSE ROOM, STAGE, HALLWAYS, SDC ROOM, MUSIC ROOM, KITCHEN, PE CLOSET, RSP ROOM, REC. ROOM, AND BOILER ROOM

SMOOTH WALL SURFACING

7,320 SF

09/08/2005	Skim Coat/Texture on Concrete Walls. This Material is in good condition as of this date.		
------------	--	--	--

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

COMMENTS

QTY (APPROXIMATE)

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
02/08/2016	Sample 16-032-SA051 collected from Main Building, Girls Restroom-88, Wall Skimcoat and Paint for Concrete. Sample 16-032-SA061 collected from Main Building, Girls Restroom, Exterior Wall Skimcoat and Paint for Concrete. Sample 16-032-SA065 collected from Main Building, Platform-93, Wall Skimcoat and Paint for Concrete.		
02/04/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		

16-032-SA051	ND	NONE DETECTED	(ND)
16-032-SA065	ND	NONE DETECTED	(ND)
16-032-SA061	ND	NONE DETECTED	(ND)
05-212AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

STAGE

VINYL WALL COVER

300 SF

05/13/2009	Vinyl Wall Cover on Accordion Type Collapsible Partition. This Material is in GOOD condition as of this date.
03/29/2017	Damage Observed. <5% Physical Damage - in the form of Vinyl Cover becoming Frayed and Torn at the Bottom. Damages Re-Assessed. Additional 2 Tiles are Water Damaged outside Classroom 9. No other changes as of this date.
02/04/2020	This Material is unchanged as of this date.

SF=Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		
08/16/2023	This Material is unchanged as of this date.		
02/14/2024	This Material is unchanged as of this date.		
08/14/2024	This Material is unchanged as of this date.		
02/27/2025	This Material is unchanged as of this date.		
09/17/2025	This Material is unchanged as of this date.		
09-098AAA	ASSUMED	NO SAMPLE	(NS)

MAIN BUILDING

STAGE

VINYL WALL COVER MASTIC

300 SF

05/13/2009	Mastic/Adhesive for Vinyl Wall Cover on Accordion Type Collapsible Partition. This Material is in GOOD condition as of this date.		
03/29/2017	Damage Observed. <5% Physical Damage - in the form of Vinyl Cover becoming Frayed and Torn at the Bottom. Damages Re-Assessed. Additional 2 Tiles are Water Damaged outside Classroom 9. No other changes as of this date.		
02/04/2020	This Material is unchanged as of this date.		
08/28/2020	This Material is unchanged as of this date.		
02/10/2021	This Material is unchanged as of this date.		
08/11/2021	This Material is unchanged as of this date.		
02/18/2022	This Material is unchanged as of this date.		
08/17/2022	This Material is unchanged as of this date.		
02/15/2023	This Material is unchanged as of this date.		

SF=Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

09-098AAA ASSUMED NO SAMPLE (NS)

MAIN BUILDING

TEACHERS WORK AREA IN EACH POD, TEACHER LOUNGE, NURSE ROOM, KINDERGARTEN PRODUCTION ROOM, AND SPEECH ROOM

SINK UNDERCOATING

84 SF

10/15/2008 Thermal Undercoating on Sink. (21 EA Sink). This Material is in GOOD condition as of this date.

02/08/2016 Sample 16-032-SA024 collected from Main Building, Activity 53, Stainless Metal Sink Black Undercoating.
Sample 16-032-SA032 collected from Main Building, Atrium 57, Stainless Metal Sink Gray Undercoating.

02/04/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

02/10/2021 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

08-241AAA ASSUMED NO SAMPLE (NS)

16-032-SA024 ND NONE DETECTED (ND)

SF= Sq. Ft, I=Inches, LF=Linear Ft., N=Number, EA=Each

HazMat Doc. All Rights Reserved.

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
16-032-SA032	ND	NONE DETECTED	(ND)

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS CODE
------------	------------------	---------------	---------------

METAL STORAGE CONTAINERS

METAL STORAGE CONTAINERS

05/13/2009 BUILDING NOTES:

05/13/2009 Metal Storage Containers. (2 EA Containers).

METAL STORAGE CONTAINERS

METAL STORAGE CONTAINERS (2)

STORAGE CONTAINER

640 SF

03/17/2016 Metal Storage Containers. 2 EA, approximately 320 SF EA.

02/04/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

16-074.NS	ASSUMED	NO SAMPLE	(NS)
-----------	---------	-----------	--------

SURVEY REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

QTY (APPROXIMATE)

COMMENTS

SAMPLE NO.

ASBESTOS CONTENT

ASBESTOS NAME

ASBESTOS CODE

PLASTIC SHED STORAGE CONTAINER

PLASTIC SHED STORAGE CONTAINER

PLASTIC STORAGE CONTAINER (LOCATED NEXT TO 2 METAL STORAGE CONTAINERS)

STORAGE CONTAINER

60 SF

03/10/2010 Apparent New Plastic Storage Container identified by the AHERA Accredited inspector. This Material is in GOOD condition as of this date.

02/04/2020 This Material is unchanged as of this date.

08/28/2020 This Material is unchanged as of this date.

08/11/2021 This Material is unchanged as of this date.

02/18/2022 This Material is unchanged as of this date.

08/17/2022 This Material is unchanged as of this date.

02/15/2023 This Material is unchanged as of this date.

08/16/2023 This Material is unchanged as of this date.

02/14/2024 This Material is unchanged as of this date.

08/14/2024 This Material is unchanged as of this date.

02/27/2025 This Material is unchanged as of this date.

10-052.NS

NEW

NO SAMPLE

(NS)

End Of Report, Total Of 28 Pages

HOMOGENEOUS MATERIALS IN SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

MATERIAL CATEGORY

LOCATION

MATERIAL TYPE

CLASSROOMS 01 PORTABLE BUILDING

MISCELLANEOUS MATERIAL

PORTABLE 1

PORTABLE BUILDING

CLASSROOMS 02 PORTABLE BUILDING

MISCELLANEOUS MATERIAL

PORTABLE 2

PORTABLE BUILDING

CLASSROOMS 03 PORTABLE BUILDING

MISCELLANEOUS MATERIAL

PORTABLE 3

PORTABLE BUILDING

CLASSROOMS 04-07 PORTABLE BUILDING

MISCELLANEOUS MATERIAL

PORTABLES 4-7

PORTABLE BUILDING

MAIN BUILDING

MISCELLANEOUS MATERIAL

ALL ADMIN HALLWAYS, BOILER ROOM, KITCHEN, ELECTRICAL ROOM, MUSIC ROOM, STAGE, AND SDC ROOM

FIRE DOOR CORE INSULATION

ALL OFFICES, STORAGE ROOMS, LIBRARY, MULTI-PURPOSE ROOM, AND COURTYARD STORAGE CLOSETS (LOCATED OUTSIDE PODS A-F)

SMOOTH WALL
MISCELLANEOUS

ALL POD AREAS, PREP AREAS, MULTI-PURPOSE ROOM, STAGE, SDC ROOM, AND HALLWAYS TO MULTI-PURPOSE ROOM

CEILING TILE

ALL POD AREAS, PREP AREAS, MULTI-PURPOSE ROOM, STAGE, SDC ROOM, AND HALLWAYS TO MULTI-PURPOSE ROOM

CEILING TILE MASTIC

ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS

PRESSED WOOD WALL PANEL

ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS

PRESSED WOOD WALL PANEL
MASTIC

ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS
COURTYARDS (LOCATED OUTSIDE PODS A-F)

VINYL WALL COVER MASTIC

LIBRARY OFFICE

SINK UNDERCOATING

LIBRARY OFFICE

CEMENTITIOUS WALL PANEL

CEMENTITIOUS WALL PANEL

MASTIC

LOUNGE, HALLWAY, OFFICES, LOBBY, STAGE, CLASSROOMS

VINYL WALL COVER MASTIC

STAGE

VINYL WALL COVER

STAGE

VINYL WALL COVER MASTIC

TEACHERS WORK AREA IN EACH POD, TEACHER LOUNGE, NURSE ROOM, KINDERGARTEN PRODUCTION ROOM, AND SPEECH ROOM

SINK UNDERCOATING

HOMOGENEOUS MATERIALS IN
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

MATERIAL CATEGORY

LOCATION

MATERIAL TYPE

SURFACING MATERIAL

ALL OFFICES, STORAGE ROOMS, LIBRARY, MULTI-PURPOSE ROOM, AND
COURTYARD STORAGE CLOSETS (LOCATED OUTSIDE PODS A-F)

SMOOTH WALL SURFACING

EXTERIOR WALLS

ROUGH WALL

EXTERIOR WALLS

ROUGH WALL SURFACING

MULTI-PURPOSE ROOM, STAGE, HALLWAYS, SDC ROOM, MUSIC ROOM,
KITCHEN, PE CLOSET, RSP ROOM, REC. ROOM, AND BOILER ROOM

SMOOTH WALL SURFACING

THERMAL SYSTEM INSULATION

MAIN ELECTRICAL PANEL ROOM, AND CONCEALED LOCATIONS

PIPE FITTING INSULATION

METAL STORAGE CONTAINERS

MISCELLANEOUS MATERIAL

METAL STORAGE CONTAINERS (2)

STORAGE CONTAINER

PLASTIC SHED STORAGE CONTAINER

MISCELLANEOUS MATERIAL

PLASTIC STORAGE CONTAINER (LOCATED NEXT TO 2 METAL STORAGE
CONTAINERS)

STORAGE CONTAINER

End Of Report, Total Of 2 Pages

FRIABLE LOCATIONS IN SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME			
LOCATION		QTY	ASBESTOS
MATERIAL TYPE		(APPROXIMATE)	CONTENT
MAIN BUILDING			
ALL ADMIN HALLWAYS, BOILER ROOM, KITCHEN, ELECTRICAL ROOM, MUSIC ROOM, STAGE, AND SDC ROOM			
FIRE DOOR CORE INSULATION		525 SF	Greater Than 1%
ALL OFFICES, STORAGE ROOMS, LIBRARY, MULTI-PURPOSE ROOM, AND COURTYARD STORAGE CLOSETS (LOCATED OUTSIDE PODS A-F)			
SMOOTH WALL MISCELLANEOUS		34,860 SF	Non Detected
ALL OFFICES, STORAGE ROOMS, LIBRARY, MULTI-PURPOSE ROOM, AND COURTYARD STORAGE CLOSETS (LOCATED OUTSIDE PODS A-F)			
SMOOTH WALL SURFACING		34,860 SF	Non Detected
ALL POD AREAS, PREP AREAS, MULTI-PURPOSE ROOM, STAGE, SDC ROOM, AND HALLWAYS TO MULTI-PURPOSE ROOM			
CEILING TILE		7,650 SF	Non Detected
ALL POD AREAS, PREP AREAS, MULTI-PURPOSE ROOM, STAGE, SDC ROOM, AND HALLWAYS TO MULTI-PURPOSE ROOM			
CEILING TILE MASTIC		7,650 SF	Non Detected
ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS			
PRESSED WOOD WALL PANEL		22,000 SF	Assumed
EXTERIOR WALLS			
ROUGH WALL		21,750 SF	Assumed
EXTERIOR WALLS			
ROUGH WALL SURFACING		21,750 SF	Assumed
LOUNGE, HALLWAY, OFFICES, LOBBY, STAGE, CLASSROOMS			
VINYL WALL COVER MASTIC		4,000 SF	Assumed
MAIN ELECTRICAL PANEL ROOM, AND CONCEALED LOCATIONS			
PIPE FITTING INSULATION		2 LF	Assumed
STAGE			
VINYL WALL COVER		300 SF	Assumed
STAGE			
VINYL WALL COVER MASTIC		300 SF	Assumed
End Of Report, Total Of 1 Pages			

Non- Friable Locations In SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME			
LOCATION		QTY	ASBESTOS
MATERIAL TYPE		(APPROXIMATE)	CONTENT
MAIN BUILDING			
ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS			
PRESSED WOOD WALL PANEL MASTIC	22,000 SF		Assumed
ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS			
VINYL WALL COVER MASTIC	22,000 SF		Non Detected
COURTYARDS (LOCATED OUTSIDE PODS A-F)			
SINK UNDERCOATING	30 SF		Assumed
LIBRARY OFFICE			
CEMENTITIOUS WALL PANEL	16 SF		Greater Than 1%
LIBRARY OFFICE			
CEMENTITIOUS WALL PANEL MASTIC	16 SF		Assumed
MULTI-PURPOSE ROOM, STAGE, HALLWAYS, SDC ROOM, MUSIC ROOM, KITCHEN, PE CLOSET, RSP ROOM, REC. ROOM, AND BOILER ROOM			
SMOOTH WALL SURFACING	7,320 SF		Non Detected
TEACHERS WORK AREA IN EACH POD, TEACHER LOUNGE, NURSE ROOM, KINDERGARTEN PRODUCTION ROOM, AND SPEECH ROOM			
SINK UNDERCOATING	84 SF		Non Detected
End Of Report, Total Of 1 Pages			

RECOMMENDATIONS FOR
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

CLASSROOMS 01 PORTABLE BUILDING

PORTABLE 1

PORTABLE BUILDING

960 SF

- (a) This is a replacement/new material.
- (b) The district should obtain documentation from the manufacturer/installer that no asbestos has been used in the manufacture or installation of this building material.
- (c) This documentation is to be maintained with the district's AHERA records.

CLASSROOMS 02 PORTABLE BUILDING

PORTABLE 2

PORTABLE BUILDING

960 SF

- (a) This is a replacement/new material.
- (b) The district should obtain documentation from the manufacturer/installer that no asbestos has been used in the manufacture or installation of this building material.
- (c) This documentation is to be maintained with the district's AHERA records.

CLASSROOMS 03 PORTABLE BUILDING

PORTABLE 3

PORTABLE BUILDING

960 SF

- (a) This is a replacement/new material.
- (b) The district should obtain documentation from the manufacturer/installer that no asbestos has been used in the manufacture or installation of this building material.
- (c) This documentation is to be maintained with the district's AHERA records.

RECOMMENDATIONS FOR
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

CLASSROOMS 04-07 PORTABLE BUILDING

PORTABLES 4-7

PORTABLE BUILDING

3,840 SF

- (a) This is a replacement/new material.
- (b) The district should obtain documentation from the manufacturer/installer that no asbestos has been used in the manufacture or installation of this building material.
- (c) This documentation is to be maintained with the district's AHERA records.

MAIN BUILDING

ALL ADMIN HALLWAYS, BOILER ROOM, KITCHEN, ELECTRICAL ROOM, MUSIC ROOM, STAGE, AND SDC ROOM

FIRE DOOR CORE INSULATION

525 SF

- (a) No abatement is necessary.
- (b) Maintain the material in an intact and undamaged condition.
- (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
- (d) Include this material in the long term surveillance and re-inspection program
- (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material. Removal must be designed and performed by accredited personnel only.

**ALL OFFICES, STORAGE ROOMS, LIBRARY, MULTI-PURPOSE ROOM, AND COURTYARD STORAGE CLOSETS
(LOCATED OUTSIDE PODS A-F)**

SMOOTH WALL MISCELLANEOUS

34,860 SF

- (a) No abatement is necessary.
- (b) Maintain the material in an intact and undamaged condition.
- (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
- (d) Include this material in the long term surveillance and re-inspection program
- (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material. Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

ALL OFFICES, STORAGE ROOMS, LIBRARY, MULTI-PURPOSE ROOM, AND COURTYARD STORAGE CLOSETS
(LOCATED OUTSIDE PODS A-F)

SMOOTH WALL SURFACING 34,860 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

ALL POD AREAS, PREP AREAS, MULTI-PURPOSE ROOM, STAGE, SDC ROOM, AND HALLWAYS TO
MULTI-PURPOSE ROOM

CEILING TILE 7,650 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

ALL POD AREAS, PREP AREAS, MULTI-PURPOSE ROOM, STAGE, SDC ROOM, AND HALLWAYS TO
MULTI-PURPOSE ROOM

CEILING TILE MASTIC 7,650 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS

PRESSED WOOD WALL PANEL 22,000 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS

PRESSED WOOD WALL PANEL MASTIC 22,000 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS

VINYL WALL COVER MASTIC 22,000 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

COURTYARDS (LOCATED OUTSIDE PODS A-F)

SINK UNDERCOATING 30 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

EXTERIOR WALLS

ROUGH WALL 21,750 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

EXTERIOR WALLS

ROUGH WALL SURFACING

21,750 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

LIBRARY OFFICE

CEMENTITIOUS WALL PANEL

16 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

LIBRARY OFFICE

CEMENTITIOUS WALL PANEL MASTIC

16 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

LOUNGE, HALLWAY, OFFICES, LOBBY, STAGE, CLASSROOMS

VINYL WALL COVER MASTIC

4,000 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

MAIN ELECTRICAL PANEL ROOM, AND CONCEALED LOCATIONS

PIPE FITTING INSULATION

2 LF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

MULTI-PURPOSE ROOM, STAGE, HALLWAYS, SDC ROOM, MUSIC ROOM, KITCHEN, PE CLOSET, RSP ROOM, REC. ROOM, AND BOILER ROOM

SMOOTH WALL SURFACING

7,320 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

STAGE

VINYL WALL COVER

300 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

STAGE

VINYL WALL COVER MASTIC

300 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

TEACHERS WORK AREA IN EACH POD, TEACHER LOUNGE, NURSE ROOM, KINDERGARTEN PRODUCTION ROOM, AND SPEECH ROOM

SINK UNDERCOATING

84 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

METAL STORAGE CONTAINERS

METAL STORAGE CONTAINERS (2)

STORAGE CONTAINER

640 SF

- (a) No abatement is necessary.
 - (b) Maintain the material in an intact and undamaged condition.
 - (c) Include this material in the Operations and Maintenance (O & M) program until it has been replaced with a material that does not contain Asbestos.
 - (d) Include this material in the long term surveillance and re-inspection program
 - (e) Remove the material if it becomes damaged or repairs and maintenance work may impact this material.
- Removal must be designed and performed by accredited personnel only.

RECOMMENDATIONS FOR
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

RECOMMENDATION

QTY

(APPROXIMATE)

PLASTIC SHED STORAGE CONTAINER

PLASTIC STORAGE CONTAINER (LOCATED NEXT TO 2 METAL STORAGE CONTAINERS)

STORAGE CONTAINER

60 SF

- (a) This is a replacement/new material.
 - (b) The District should obtain documentation from the manufacturer/installer that no asbestos has been used in the manufacture or installation of this building material.
 - (c) This documentation is to be maintained with the District's AHERA records.
-

End Of Report, Total Of 8 Pages

SAMPLES REPORT FOR
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO.	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
COMMENTS					

CLASSROOMS 01 PORTABLE BUILDING

CLASSROOMS 01 PORTABLE BUILDING

PORTABLE 1

PORTABLE BUILDING

05-212.NS

9/8/2005

Negative

NEW MATERIAL

NO SAMPLE

NS

New 1994 Construction Relocatable Building per Manufacturer's Tag information.

SAMPLES REPORT FOR
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO.	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
COMMENTS					

CLASSROOMS 02 PORTABLE BUILDING

CLASSROOMS 02 PORTABLE BUILDING

PORTABLE 2

PORTABLE BUILDING

05-212.NS

9/8/2005

Negative

NEW MATERIAL

NO SAMPLE

NS

New 1994 Construction Relocatable Building per Manufacturer's Tag information.

SAMPLES REPORT FOR
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO.	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
COMMENTS					

CLASSROOMS 03 PORTABLE BUILDING

CLASSROOMS 03 PORTABLE BUILDING

PORTABLE 3

PORTABLE BUILDING

05-212.NS

9/8/2005

Negative

NEW MATERIAL

NO SAMPLE

NS

New 1996 Construction Relocatable Building per Manufacturer's Tag information.

SAMPLES REPORT FOR
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE No.	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
COMMENTS					

CLASSROOMS 04-07 PORTABLE BUILDING

CLASSROOMS 04-07 PORTABLE BUILDING

PORTABLES 4-7

PORTABLE BUILDING

05-212.NS	9/8/2005	Negative	NEW MATERIAL	NO SAMPLE	NS
------------------	----------	----------	--------------	-----------	----

New 2005 Construction Relocatable Buildings per Manufacturer's Tag information.

16-032-SA102	2/8/2016	Negative	ND	NONE DETECTED	ND
---------------------	----------	----------	----	---------------	----

P7 - 4" Black Baseboard Off-White Mastic

16-032-SA103	2/8/2016	Negative	ND	NONE DETECTED	ND
---------------------	----------	----------	----	---------------	----

P7 - Gray-Black and Brown Carpets-Yellow Mastic.

SAMPLES REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME
LOCATION
MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

MAIN BUILDING

MAIN BUILDING

ALL ADMIN HALLWAYS, BOILER ROOM, KITCHEN, ELECTRICAL ROOM, MUSIC ROOM, STAGE, AND SDC ROOM
 FIRE DOOR CORE INSULATION

<u>05-212AAA</u>	9/8/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

<u>16-032-SA043</u>	2/8/2016	Positive	26%	CHRYSTILE	CH
----------------------------	----------	----------	-----	-----------	----

Main Building, Activity 69, Fire Door Core White Insulation.

MAIN BUILDING

ALL OFFICES, STORAGE ROOMS, LIBRARY, MULTI-PURPOSE ROOM, AND COURTYARD STORAGE CLOSETS (LOCATED OUTSIDE PODS A-F)
 SMOOTH WALL MISCELLANEOUS

<u>05-212AAA</u>	9/8/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

<u>16-032-SA003</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Classroom 38, Wall Mud.

<u>16-032-SA003</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Classroom 38, Wall Joint Tape.

<u>16-032-SA004</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Classroom 38, Wall Gypsum Board.

<u>16-032-SA013</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Classroom 55, Wall Mud.

<u>16-032-SA013</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Classroom 55, Wall Joint Tape.

<u>16-032-SA014</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Classroom 55, Wall Gypsum Board.

<u>16-032-SA021</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Activity 53, Ceiling Gypsum Board.

<u>16-032-SA026</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Toilet 59, Wall Mud.

SAMPLES REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME
LOCATION
MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
<u>16-032-SA026</u> Main Building, Toilet 59, Joint Tape.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA027</u> Main Building, Toilet 59, Ceiling Gypsum Board.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA035</u> Main Building, Classroom 70, Wall Mud.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA035</u> Main Building, Classroom 70, Joint Tape.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA036</u> Main Building, Classroom 70, Wall Gypsum Board.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA053</u> Main Building, Girls Restroom, Upper Wall Mud.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA053</u> Main Building, Girls Restroom, Upper Wall Joint Tape.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA054</u> Main Building, Girls Restroom, Upper Wall Gypsum Board.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA067</u> Main Building, Platform-93, Wall Mud.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA067</u> Main Building, Platform-93, Joint Tape.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA068</u> Main Building, Platform-93, Wall Gypsum Board.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA083</u> Main Building, Janitor-4, Wall Mud.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA083</u> Main Building, Janitor-4, Wall Joint Tape.	2/8/2016	Negative	ND	NONE DETECTED	ND
<u>16-032-SA084</u> Main Building, Janitor-4, Wall Gypsum Board.	2/8/2016	Negative	ND	NONE DETECTED	ND

SAMPLES REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME
LOCATION
MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

MAIN BUILDING

ALL OFFICES, STORAGE ROOMS, LIBRARY, MULTI-PURPOSE ROOM, AND COURTYARD STORAGE CLOSETS (LOCATED OUTSIDE PODS A-F)

SMOOTH WALL SURFACING

<u>06-223AAA</u>	8/24/2006	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

<u>16-032-SA002</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Classroom 38, Wall Skimcoat and Paint for Gypsum Board.

<u>16-032-SA012</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Classroom 55, Wall Skimcoat and Paint for Gypsum Board.

<u>16-032-SA025</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Toilet-59, Ceiling Skimcoat and Paint for Gypsum Board.

<u>16-032-SA034</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Classroom 70, Wall Skimcoat and Paint for Gypsum Board.

<u>16-032-SA052</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Girls Restroom-88, Upper Wall, Skimcoat and Paint for Gypsum Board.

<u>16-032-SA060</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Boys Restroom-89, Wall Old Skimcoat and Paint for Wood Panel.

<u>16-032-SA066</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Platform-93, Wall Skimcoat and Paint for Gypsum Board.

<u>16-032-SA082</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Janitor-4, Wall Skimcoat and Paint for Gypsum Board.

MAIN BUILDING

ALL POD AREAS, PREP AREAS, MULTI-PURPOSE ROOM, STAGE, SDC ROOM, AND HALLWAYS TO MULTI-PURPOSE ROOM
 CEILING TILE

<u>05-212AAA</u>	9/8/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

<u>16-032-SA019</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Activity 53, 1'x1' Ceiling Tile.

<u>16-032-SA080</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Entry 82, 1'x1' Pitted Mark Ceiling Tile.

SAMPLES REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME
LOCATION
MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

<u>16-032-SA092</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Activity-29, 1'x1' Pitted Mark Ceiling Tile.

MAIN BUILDING

ALL POD AREAS, PREP AREAS, MULTI-PURPOSE ROOM, STAGE, SDC ROOM, AND HALLWAYS TO MULTI-PURPOSE ROOM
 CEILING TILE MASTIC

<u>05-212AAA</u>	9/8/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

<u>16-032-SA020</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Activity 53, Brown Mastic.

<u>16-032-SA045</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Activity 61, Brown Mastic.

<u>16-032-SA081</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Entry 82, Brown Mastic.

<u>16-032-SA093</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Activity-29, Brown Mastic.

MAIN BUILDING

ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS
 PRESSED WOOD WALL PANEL

<u>05-212AAA</u>	9/8/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

MAIN BUILDING

ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS
 PRESSED WOOD WALL PANEL MASTIC

<u>05-212AAA</u>	9/8/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

MAIN BUILDING

ALL PODS, PREP AREAS, SDC ROOM, STAGE AND ALL CLASSROOMS
 VINYL WALL COVER MASTIC

<u>05-212AAA</u>	9/8/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

<u>16-032-SA006</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Classroom 38, Mastic.

SAMPLES REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

16-032-SA006

2/8/2016

Negative

ND

NONE DETECTED

ND

Main Building, Classroom 38, Fiberboard.

16-032-SA016

2/8/2016

Negative

ND

NONE DETECTED

ND

Main Building, Classroom 55, Yellow Mastic.

16-032-SA016

2/8/2016

Negative

ND

NONE DETECTED

ND

Main Building, Classroom 55, Fiberboard.

16-032-SA038

2/8/2016

Negative

ND

NONE DETECTED

ND

Main Building, Classroom 70, Wall Vinyl Wall Covered, Fiberboard and Mastic only.

16-032-SA070

2/8/2016

Negative

ND

NONE DETECTED

ND

Main Building, SDC-96, Wall Viny Wall Covered Adhesive.

16-032-SA070

2/8/2016

Negative

ND

NONE DETECTED

ND

Main Building, SDC-96, Wall Vinyl Wall Covered Compound only.

MAIN BUILDING

COURTYARDS (LOCATED OUTSIDE PODS A-F)

SINK UNDERCOATING

10-052AAA

3/10/2010

Positive

ASSUMED

NO SAMPLE

NS

MAIN BUILDING

EXTERIOR WALLS

ROUGH WALL

05-212AAA

9/8/2005

Positive

ASSUMED

NO SAMPLE

NS

MAIN BUILDING

EXTERIOR WALLS

ROUGH WALL SURFACING

05-212AAA

9/8/2005

Positive

ASSUMED

NO SAMPLE

NS

MAIN BUILDING

LIBRARY OFFICE

CEMENTITIOUS WALL PANEL

10-052AAA

3/10/2010

Positive

ASSUMED

NO SAMPLE

NS

SAMPLES REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

MAIN BUILDING

LIBRARY OFFICE

CEMENTITIOUS WALL PANEL MASTIC

<u>10-052AAA</u>	3/10/2010	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MAIN BUILDING

LOUNGE, HALLWAY, OFFICES, LOBBY, STAGE, CLASSROOMS

VINYL WALL COVER MASTIC

<u>10-174AAA</u>	9/1/2010	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

MAIN BUILDING

MAIN ELECTRICAL PANEL ROOM, AND CONCEALED LOCATIONS

PIPE FITTING INSULATION

<u>07-043AAA</u>	11/5/2007	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MAIN BUILDING

MULTI-PURPOSE ROOM, STAGE, HALLWAYS, SDC ROOM, MUSIC ROOM, KITCHEN, PE CLOSET, RSP ROOM, REC. ROOM, AND BOILER ROOM

SMOOTH WALL SURFACING

<u>05-212AAA</u>	9/8/2005	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	----------	----------	---------	-----------	----

<u>16-032-SA051</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Girls Restroom-88, Wall Skimcoat and Paint for Concrete.

<u>16-032-SA061</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Girls Restroom-88, Exterior Wall Skimcoat and Paint for Concrete.

<u>16-032-SA065</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Platform-93, Wall Skimcoat and Paint for Concrete.

MAIN BUILDING

STAGE

VINYL WALL COVER

<u>09-098AAA</u>	5/13/2009	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

SAMPLES REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO. COMMENTS	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
------------------------	------	--------	---------------------	------------------	------------------

MAIN BUILDING

STAGE

VINYL WALL COVER MASTIC

<u>09-098AAA</u>	5/13/2009	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

MAIN BUILDING

TEACHERS WORK AREA IN EACH POD, TEACHER LOUNGE, NURSE ROOM, KINDERGARTEN PRODUCTION ROOM, AND SPEECH ROOM

SINK UNDERCOATING

<u>08-241AAA</u>	10/15/2008	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	------------	----------	---------	-----------	----

<u>16-032-SA024</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Activity 53, Stainless Metal Sink Black Undercoating.

<u>16-032-SA032</u>	2/8/2016	Negative	ND	NONE DETECTED	ND
----------------------------	----------	----------	----	---------------	----

Main Building, Atrium 57, Stainless Metal Sink Gray Undercoating.

SAMPLES REPORT FOR
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO.	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
COMMENTS					

METAL STORAGE CONTAINERS

METAL STORAGE CONTAINERS

METAL STORAGE CONTAINERS (2)

STORAGE CONTAINER

<u>16-074.NS</u>	3/17/2016	Positive	ASSUMED	NO SAMPLE	NS
-------------------------	-----------	----------	---------	-----------	----

SAMPLES REPORT FOR
SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME

LOCATION

MATERIAL TYPE

SAMPLE NO.	DATE	RESULT	ASBESTOS CONTENT	ASBESTOS NAME	ASBESTOS TYPE
COMMENTS					

PLASTIC SHED STORAGE CONTAINER

PLASTIC SHED STORAGE CONTAINER

PLASTIC STORAGE CONTAINER (LOCATED NEXT TO 2 METAL STORAGE CONTAINERS)

STORAGE CONTAINER

10-052.NS

3/10/2010

Negative

NEW MATERIAL

NO SAMPLE

NS

Plastic Storage Container.

End Of Report, Total Of 13 Pages

DAMAGE REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
RISK ASSESMENT CATEGORY	COMMENTS			

MAIN BUILDING

MAIN BUILDING

ALL ADMIN HALLWAYS, BOILER ROOM, KITCHEN, ELECTRICAL ROOM, MUSIC ROOM, STAGE, AND SDC ROOM

FIRE DOOR CORE INSULATION

525 SF

P: Less Than 5%

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

09/08/2005	Fire Door Core Insulation (25 EA Doors). This Material is in GOOD condition as of this date.
02/08/2016	Sample 16-032-SA043 collected from Main Building, Activity 69, Fire Door Core, White Insulation.
09/13/2016	Repairs Observed. Damages to Activity Room 67 (Interior), Lobby 1, and the Doorway between Hall 77 and Entry 16 Doors have been repaired during the Summer 2016 Modernization project. No other changes as of this date.
02/04/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	Damage Observed. <5% Physical Damage - in the form of 1 EA Missing Screw White Core Insulation Exposed on Double Door to Main Entrance to Pod A. Material condition changed from GOOD to FAIR overall. Friability changed from Non-Friable to Friable. No other changes as of this date.
08/17/2022	Additional Damage Observed. <5% Physical Damage in the form of 4 (EA) Small Screws Missing with White Core Insulation Exposed at Reading Room and Electrical Room Door. Double Door Gate House of Pod F has an Inside Cover Piece Missing with White Core Insulation Exposed. No other changes as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	Partial Repairs and Additional Damage Observed. The Damage to the Double Door Gate House of Pod F has been repaired. Additional Damage in the form of 2" Gouge with White Core Insulation Exposed due to the Chair Racks going in and out of the Chair Storage Room. Material remains in FAIR condition overall. No other changes as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESSMENT CATEGORY	COMMENTS	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
---------------	----------	---------------	--------------------------	----------	----------------------	---

MAIN BUILDING

ALL OFFICES, STORAGE ROOMS, LIBRARY, MULTI-PURPOSE ROOM, AND COURTYARD STORAGE CLOSETS
(LOCATED OUTSIDE PODS A-F)

SMOOTH WALL MISCELLANEOUS

34,860 SF

P: Less Than 5%

W: <10% Stains or Flaking

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

09/08/2005	Gypsum Wallboard System Walls and Ceilings, (under Skim Coat, Vinyl Wall Coverings, Suspended Ceiling Tiles, and 1'x 1' Wall and Ceiling Tiles in some areas). This Material is in GOOD condition as of this date.
04/16/2008	<10% Water Damage. Water Damage observed in Pods A, C, and D under 1'x1' Ceiling Tiles as of this date. Material is in FAIR condition overall. Material changed from Non-Friable to Friable. No other changes as of this date.
03/10/2010	Additional Damage: <5% Physical Damage - in the form of approx. 1 SF of the Wall has been cut and removed in Electrical Room of Pod D. No other changes as of this date.
02/08/2016	Sample 16-032-SA003 collected from Main Building, Classroom 38, Wall Joint Tape and Mud for Gypsum Board. Sample 16-032-SA004 collected from Main Building, Classroom 38, Wall Gypsum Board. Sample 16-032-SA013 collected from Main Building, Classroom 55, Wall Joint Tape and Mud. Sample 16-032-SA014 collected from Main Building, Classroom 55, Wall Gypsum Board. Sample 16-032-SA026 collected from Main Building, Toilet-59, Wall Joint Tape and Mud for Gypsum Board. Sample 16-032-SA027 collected from Main Building, Toilet-59, Ceiling Gypsum Board. Sample 16-032-SA035 collected from Main Building, Classroom 70, Wall Joint Tape and Mud for Gypsum Board. Sample 16-032-SA036 collected from Main Building, Classroom 70, Wall Gypsum Board. Sample 16-032-SA053 collected from Main Building.
03/17/2016	Additional Damage observed. 1 SF of Physical Damage in Multi-Purpose Room. No other changes as of this date.
08/29/2017	Additional Damage Observed. Ceiling Tiles now have Water Damage. No other changes as of this date.
02/04/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESSMENT CATEGORY	COMMENTS	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
---------------	----------	---------------	--------------------------	----------	----------------------	---

MAIN BUILDING

ALL OFFICES, STORAGE ROOMS, LIBRARY, MULTI-PURPOSE ROOM, AND COURTYARD STORAGE CLOSETS
(LOCATED OUTSIDE PODS A-F)

SMOOTH WALL SURFACING

34,860 SF

P: Less Than 5%

W: <10% Stains or Flaking

DAMAGED FRIABLE SURFACING ACM

08/24/2006	Skim Coat for Gypsum Wallboard System Walls and Ceilings, (under Skim Coat, Vinyl Wall Coverings, Suspended Ceiling Tiles, and 1'x 1' Wall and Ceiling Tiles in some areas). This Material is in GOOD condition as of this date.
04/16/2008	<10% Water Damage. Water Damage observed in Pods A, C, and D under 1'x1' Ceiling Tiles as of this date. Material is in FAIR condition overall. Material changed from Non-Friable to Friable. No other changes as of this date.
03/10/2010	Additional Damage: <5% Physical Damage - in the form of approx. 1 SF of the Wall has been cut and removed in Electrical Room of Pod D. No other changes as of this date.
02/08/2016	Sample 16-032-SA002 collected from Main Building, Classroom 38, Wall Skim Coat and Paint for Gypsum Board. Sample 16-032-SA012 collected from Main Building, Classroom 55, Wall Skimcoat and Paint for Gypsum Board. Sample 16-032-SA025 collected from Main Building, Toilet-59, Ceiling Skimcoat and Paint for Gypsum Board. Sample 16-032-SA034 collected from Main Building Classroom 70, Wall Skimcoat and Paint for Gypsum Board. Sample 16-032-SA052 collected from Main Building, Girls Restroom-88, Upper Wall Skimcoat Skimcoat and Paint for Gypsum Board. Sample 16-032-SA060 collected from Main Building, Boys Restroom-89, Wall Old Skimcoat and Paint for Wood Panel. Sample 16-032-SA066 Main Building, Platform-93 Wall Skimcoat and Paint for Gypsum Board. Sample 16-032-SA082 Main Building Janitor-4
03/17/2016	Additional Damage observed. 1 SF of Physical Damage in Multi-Purpose Room. No other changes as of this date.
09/13/2016	Repairs Observed. Damages in Chair Storage Room have been repaired as of this date. Material remains in FAIR condition. No other changes as of this date.
08/29/2017	Additional Damage Observed. Ceiling Tiles now have Water Damage. No other changes as of this date.
02/04/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESSMENT CATEGORY	COMMENTS	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
---------------	----------	---------------	--------------------------	----------	----------------------	---

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

MAIN BUILDING

ALL POD AREAS, PREP AREAS, MULTI-PURPOSE ROOM, STAGE, SDC ROOM, AND HALLWAYS TO MULTI-PURPOSE ROOM

CEILING TILE

7,650 SF

P: Less Than 5%

W: <10% Stains or Flaking

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

09/08/2005 1'x 1' Glued-on Ceiling Tiles (with Pitted Mark Pattern). This Material is in GOOD condition as of this date.

04/16/2008 Damage: <5% Physical Damage and <10% Water Damage due to 8 additional Tiles are Water Damage observed in Pod C and these Tiles are coming loose as of this date. Material condition changed from GOOD to FAIR overall. No other changes as of this date.

05/13/2009 Material Re-Assessed. Pod A has 2 Tiles that are becoming loose. <10% Water Damage due to Pod A has 3 Tiles with Water stains. Pod C has 7 Tiles Water stained. No other changes as of this date.

03/10/2010 Additional Damage observed in the form of E Pod has 1 Tile Water Damaged. Also, several Tiles are Physically Damaged in a Classroom in Multi-Purpose room. No other changes as of this date.

09/01/2010 Additional Damage observed. 6 SF Tiles missing on Hatch Door by Boiler Room exposing the Mastic/Adhesive. 2 Tiles Damaged in the Hallway to the Multi-Purpose Room by the Kitchen. 1 Tile is Missing in the Teachers Work Room in Pod D, exposing the Mastic/Adhesive. No other changes as of this date.

11/30/2011 Additional Damage - in the form of Multipurpose Room has 2 Tiles with holes. Pod C has an additional 2 Tiles with Water Damage. Pod A, previously had 3 Tiles with Water stains, now has 1 Tile only Water stained. No other changes as of this date.

10/10/2012 Additional Damage - in the form of Pod D has 4 Water Damaged Ceiling Tiles. No other changes as of this date.

03/17/2015 POD A & D each have 1 Ceiling Tile missing, and Brown Mastic/Adhesive is exposed. No other changes as of this date.

09/18/2015 Additional Damage observed, Hallway outside of Kitchen has 2 Tiles Physically Damaged. No other changes as of this date.

02/08/2016 Sample 16-032-SA19 collected from Main Building, Activity 53, 1'x1' Ceiling Tile. Sample 16-032-SA044 collected from Main Building, Activity 61, 1'x1' Ceiling Tile. Sample 16-032-SA080 collected from Main Building, Entry-82, 1'x1' Pitted Mark Ceiling Tile. Sample 16-032-SA092 collected from Main Building, Activity-29, 1'x1' Pitted Mark Ceiling Tile.

03/17/2016 Additional Damage observed. 1 Tile is missing in A Pod Work Room exposing Mastic/Adhesive. C Pod Work Room has 10 Tiles with Water Damage; E Pod Work Room has 1 Tile with Water Damage. F Pod Work Room has 1 Tile loose. No other changes as of this date.

09/13/2016 Additional Damage observed. <10% Water Damage - in the form of 10 Tiles with Water Damage in the Multi-Purpose Room. No other changes as of this date.

DAMAGE REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESMENT CATEGORY	COMMENTS	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
03/29/2017				Material Re-assessed. Water Damage in Multi-Purpose Room painted over. Additional Damage Observed. 7 Tiles loose and 7 Tiles have Water Stains in the Multi-Purpose Room. No other changes as of this date.		
08/29/2017				Additional Damage Observed. C-Pod now has 9 Tiles with Water Damage. Access Door has 1 Tile with Physical Damage. No other changes as of this date.		
08/08/2018				Additional Damage Observed. F-Pod now has 1Tile Missing on Hatch Door and 12 Tiles have Surface Damage. No other changes as of this date.		
08/14/2019				Additional Damage Observed. <5% Physical Damage in the form of 1 SF of Tiles with Stains in each one of the Activity Rooms of Pod A and Pod C. Material Condition remains in FAIR condition overall. No other changes as of this date.		
02/04/2020				Additional Damage Observed. 1 Tile Missing Mastic Exposed in Pod A. No other changes as of this date.		
08/28/2020				This Material is unchanged as of this date.		
02/10/2021				This Material is unchanged as of this date.		
08/11/2021				This Material is unchanged as of this date.		
02/18/2022				This Material is unchanged as of this date.		
08/17/2022				This Material is unchanged as of this date.		
02/15/2023				This Material is unchanged as of this date.		
08/16/2023				This Material is unchanged as of this date.		
02/14/2024				This Material is unchanged as of this date.		
08/14/2024				This Material is unchanged as of this date.		
02/27/2025				This Material is unchanged as of this date.		
09/17/2025				This Material is unchanged as of this date.		

MAIN BUILDING

ALL POD AREAS, PREP AREAS, MULTI-PURPOSE ROOM, STAGE, SDC ROOM, AND HALLWAYS TO MULTI-PURPOSE ROOM

CEILING TILE MASTIC

7,650 SF

P: Less Than 5%

W: <10% Stains or Flaking

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

09/08/2005	Mastic/Adhesive for 1'x 1' Glued-on Ceiling Tiles (with Pitted Mark Pattern). This Material is in GOOD condition as of this date.
04/16/2008	Damage: <5% Physical Damage and <10% Water Damage due to 8 additional Tiles are Water Damage observed in Pod C and these Tiles are coming loose as of this date. Material condition changed from GOOD to FAIR overall. Material changed from Non to Friable. No other changes as of this date.
05/13/2009	Material Re-Assessed. Pod A has 2 Tiles that are becoming loose. <10% Water Damage due to Pod A has 3 Tiles with Water stains. Pod C has 7 Tiles Water stained. No other changes as of this date.

DAMAGE REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESMENT CATEGORY	COMMENTS	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
03/10/2010				Additional Damage observed in the form of E Pod has 1 Tile Water Damaged. Also, several Tiles are Physically Damaged in a Classroom in Multi-Purpose room. No other changes as of this date.		
09/01/2010				Additional Damage observed. 6 SF Tiles missing on Hatch Door by Boiler Room exposing the Mastic/Adhesive. 2 Tiles Damaged in the Hallway to the Multi-Purpose Room by the Kitchen. 1 Tile is Missing in the Teachers Work Room in Pod D, exposing the Mastic/Adhesive. No other changes as of this date.		
11/30/2011				Additional Damage - in the form of Multipurpose Room has 2 Tiles with holes. Pod C has an additional 2 Tiles with Water Damage. Pod A, previously had 3 Tiles with Water stains, now has 1 Tile only Water stained. No other changes as of this date.		
10/10/2012				Additional Damage - in the form of Pod D has 4 Water Damaged Ceiling Tiles. No other changes as of this date.		
03/17/2015				POD A & D each have 1 Ceiling Tile missing, and Brown Mastic/Adhesive is exposed. No other changes as of this date.		
09/18/2015				Additional Damage observed, Hallway outside of Kitchen has 2 Tiles Physically Damaged. No other changes as of this date.		
02/08/2016				Sample 16-032-SA020 collected from Main Building, Activity 53, Brown Mastic for 1'x1' Ceiling Tile. Sample 16-032-SA045 collected from Main Building, Activity 61, 1'x1' Ceiling Tile Brown Mastic. Sample 16-032-SA081 collected from Main Building, Entry-82, 1'x1' Pitted Mark Ceiling Tile, Brown Mastic. Sample 16-032-SA093 collected from Main Building, Activity-29, 1'x1' Pitted Mark Ceiling Tile, Brown Mastic.		
03/17/2016				Additional Damage observed. 1 Tile is missing in A Pod Work Room exposing Mastic/Adhesive. C Pod Work Room has 10 Tiles with Water Damage; E Pod Work Room has 1 Tile with Water Damage. F Pod Work Room has 1 Tile loose. No other changes as of this date.		
09/13/2016				Additional Damage observed. <10% Water Damage - in the form of 10 Tiles with Water Damage in the Multi-Purpose Room. No other changes as of this date.		
03/29/2017				Material Re-assessed. Water Damage in Multi-Purpose Room painted over. Additional Damage Observed. 7 Tiles loose and 7 Tiles have Water Stains in the Multi-Purpose Room. No other changes as of this date.		
08/29/2017				Additional Damage Observed. C-Pod now has 9 Tiles with Water Damage. Access Door has 1 Tile with Physical Damage. No other changes as of this date.		
08/08/2018				Additional Damage Observed. F-Pod now has 1Tile Missing on Hatch Door and 12 Tiles have Surface Damage. No other changes as of this date.		
08/14/2019				Additional Damage Observed. <5% Physical Damage in the form of 1 SF of Tiles with Stains in each one of the Activity Rooms of Pod A and Pod C. Material Condition remains in FAIR condition overall. No other changes as of this date.		
02/04/2020				Additional Damage Observed. 1 Tile Missing Mastic Exposed in Pod A. No other changes as of this date.		
08/28/2020				This Material is unchanged as of this date.		
02/10/2021				This Material is unchanged as of this date.		
08/11/2021				This Material is unchanged as of this date.		
02/18/2022				This Material is unchanged as of this date.		
08/17/2022				This Material is unchanged as of this date.		

DAMAGE REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME		QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
LOCATION	MATERIAL TYPE		
RISK ASSESMENT CATEGORY			
COMMENTS			

02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

MAIN BUILDING

EXTERIOR WALLS

ROUGH WALL

21,750 SF

P: Less Than 5%

W: No Evidence

DAMAGED FRIABLE SURFACING ACM

09/08/2005	Stucco Walls. This Material is in good condition as of this date.
02/04/2020	This Material is unchanged as of this date.
08/28/2020	Damage Observed. <5% Physical Damage in the form of 1 Inch Hole in Wall near Rear Entry into D-2. Material condition changed from GOOD to FAIR overall. Friability updated from Non-Friable to Friable. No other changes as of this date.
02/10/2021	Additional Damage Observed. 3 LF of Cracks near Entry to Kitchen. No other changes as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
RISK ASSESSMENT CATEGORY	COMMENTS			

MAIN BUILDING

EXTERIOR WALLS

ROUGH WALL SURFACING

21,750 SF

P: Less Than 5%

W: No Evidence

DAMAGED FRIABLE SURFACING ACM

09/08/2005	Skim Coat for Stucco Walls. This Material is in good condition as of this date.
02/04/2020	This Material is unchanged as of this date.
08/28/2020	Damage Observed. <5% Physical Damage in the form of 1 Inch Hole in Wall near Rear Entry into D-2. Material condition changed from GOOD to FAIR overall. Friability updated from Non-Friable to Friable. No other changes as of this date.
02/10/2021	Additional Damage Observed. 3 LF of Cracks near Entry to Kitchen. No other changes as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

MAIN BUILDING

LIBRARY OFFICE

CEMENTITIOUS WALL PANEL

16 SF

P: Less Than 5%

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

03/10/2010	Brown Cementitious Chalkboard. (1 EA). This Material is in GOOD condition as of this date.
02/04/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESMENT CATEGORY	COMMENTS	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
---------------	----------	---------------	-------------------------	----------	----------------------	---

08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

MAIN BUILDING

LOUNGE, HALLWAY, OFFICES, LOBBY, STAGE, CLASSROOMS

VINYL WALL COVER MASTIC

4,000 SF

P: Less Than 5%

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

09/01/2010	Mastic/Adhesive for Vinyl Wall Cover (over Sheetrock Walls). This Material is in GOOD condition as of this date.
02/04/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	Damage Observed. <5% Physical Damage - in the form of 1 SF Peeling with Light Brown Mastic Exposed in Kitchen and Multipurpose Room. Material condition changed from GOOD to FAIR overall. Friability changed from Non-Friable to Friable. No other changes as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESMENT CATEGORY	COMMENTS	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
---------------	----------	---------------	-------------------------	----------	----------------------	---

MAIN BUILDING

MAIN ELECTRICAL PANEL ROOM, AND CONCEALED LOCATIONS

PIPE FITTING INSULATION

2 LF

P: Less Than 50% No Debris

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

11/05/2007	Thermal System Insulation on Pipe Fittings. (2 EA Fittings Type). Additional Fittings may be located in the Planum, Attic, and other inaccessible area/spaces. Damage: <50% Physical Damage - due to 1 fitting being in POOR condition. This Material is in FAIR condition as of this date.
04/16/2008	Damaged fitting has been sealed and wrapped with duct tape as a temporary measure. No other changes as of this date.
02/04/2020	This Material is unchanged as of this date.
08/28/2020	This Material is unchanged as of this date.
02/10/2021	This Material is unchanged as of this date.
08/11/2021	This Material is unchanged as of this date.
02/18/2022	This Material is unchanged as of this date.
08/17/2022	This Material is unchanged as of this date.
02/15/2023	This Material is unchanged as of this date.
08/16/2023	This Material is unchanged as of this date.
02/14/2024	This Material is unchanged as of this date.
08/14/2024	This Material is unchanged as of this date.
02/27/2025	This Material is unchanged as of this date.
09/17/2025	This Material is unchanged as of this date.

MAIN BUILDING

STAGE

VINYL WALL COVER

300 SF

P: Less Than 5%

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

05/13/2009	Vinyl Wall Cover on Accordion Type Collapsible Partition. This Material is in GOOD condition as of this date.
03/29/2017	Damage Observed. <5% Physical Damage - in the form of Vinyl Cover becoming Frayed and Torn at the Bottom. Damages Re-Assessed. Additional 2 Tiles are Water Damaged outside Classroom 9. No other changes as of this date.
02/04/2020	This Material is unchanged as of this date.

DAMAGE REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME	LOCATION	MATERIAL TYPE	RISK ASSESMENT CATEGORY	COMMENTS	QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:) WATER DAMAGE (W:)
---------------	----------	---------------	-------------------------	----------	----------------------	---

08/28/2020	This Material is unchanged as of this date.				
02/10/2021	This Material is unchanged as of this date.				
08/11/2021	This Material is unchanged as of this date.				
02/18/2022	This Material is unchanged as of this date.				
08/17/2022	This Material is unchanged as of this date.				
02/15/2023	This Material is unchanged as of this date.				
08/16/2023	This Material is unchanged as of this date.				
02/14/2024	This Material is unchanged as of this date.				
08/14/2024	This Material is unchanged as of this date.				
02/27/2025	This Material is unchanged as of this date.				
09/17/2025	This Material is unchanged as of this date.				

MAIN BUILDING

STAGE

VINYL WALL COVER MASTIC

300 SF

P: Less Than 5%

W: No Evidence

DAMAGED OR SIGNIFICANTLY DAMAGED FRIABLE MISCELLANEOUS ACM

05/13/2009	Mastic/Adhesive for Vinyl Wall Cover on Accordion Type Collapsible Partition. This Material is in GOOD condition as of this date.				
03/29/2017	Damage Observed. <5% Physical Damage - in the form of Vinyl Cover becoming Frayed and Torn at the Bottom. Damages Re-Assessed. Additional 2 Tiles are Water Damaged outside Classroom 9. No other changes as of this date.				
02/04/2020	This Material is unchanged as of this date.				
08/28/2020	This Material is unchanged as of this date.				
02/10/2021	This Material is unchanged as of this date.				
08/11/2021	This Material is unchanged as of this date.				
02/18/2022	This Material is unchanged as of this date.				
08/17/2022	This Material is unchanged as of this date.				
02/15/2023	This Material is unchanged as of this date.				
08/16/2023	This Material is unchanged as of this date.				
02/14/2024	This Material is unchanged as of this date.				
08/14/2024	This Material is unchanged as of this date.				

DAMAGE REPORT FOR

SUMMERDALE ELEMENTARY SCHOOL

BUILDING NAME				
LOCATION				
MATERIAL TYPE			QTY (APPROXIMATE)	PHYSICAL DAMAGE (P:)
RISK ASSESMENT CATEGORY				WATER DAMAGE (W:)
COMMENTS				

02/27/2025 This Material is unchanged as of this date.

09/17/2025 This Material is unchanged as of this date.

End Of Report, Total Of 12 Pages

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsley Drive

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 5-2-1-9

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2 Portable 1

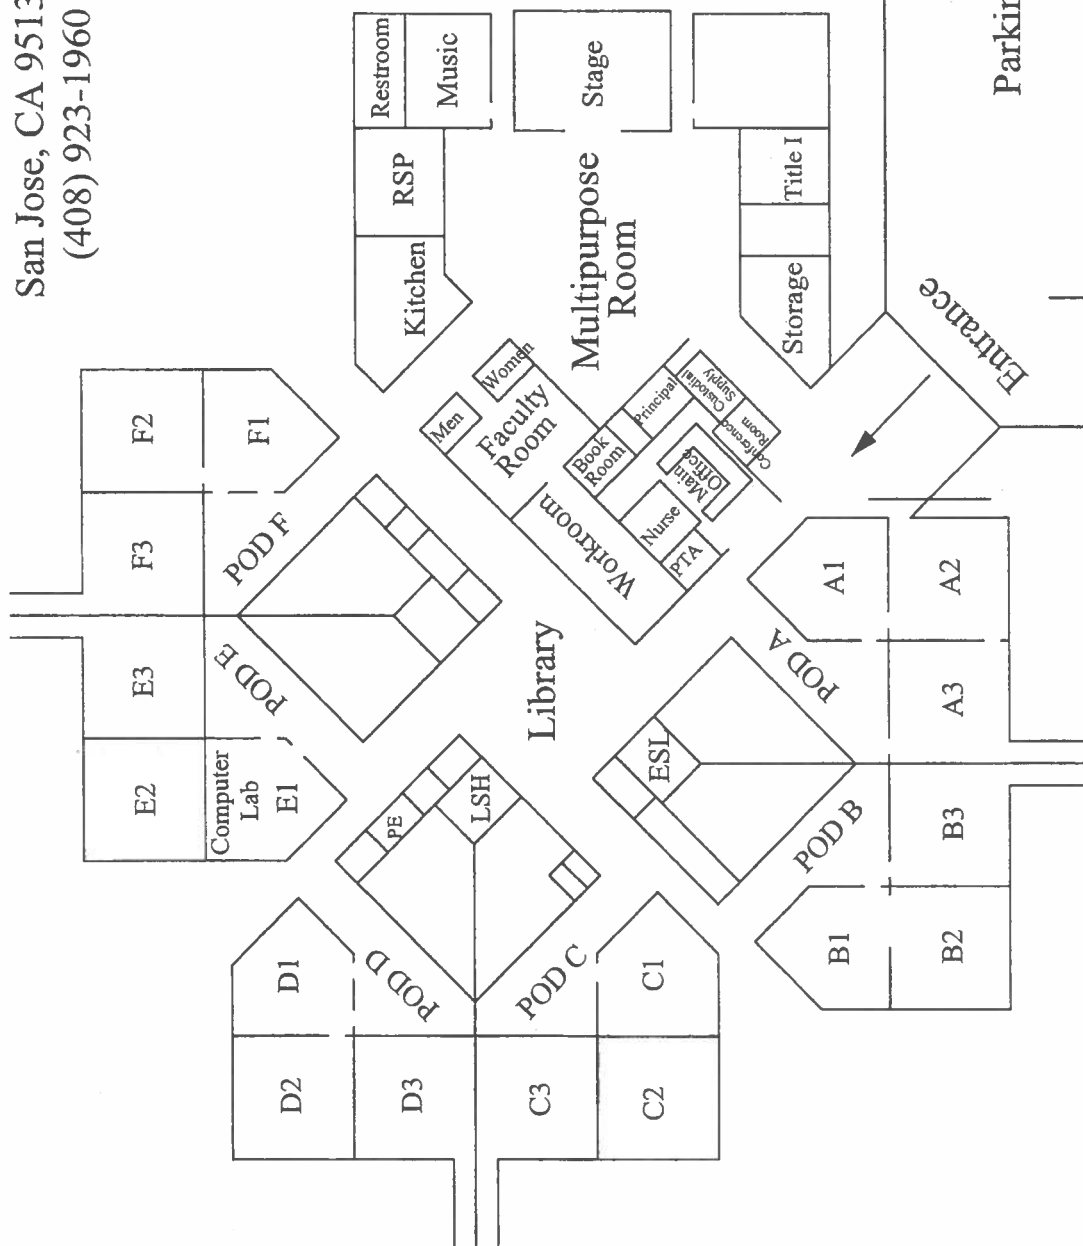

Summerdale Drive

25-076

Summerdale Elementary School
1100 Summerdale Drive
San Jose, CA 95132
(408) 923-1960


Helmsey Drive

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 5-2-12

Portable 7
Portable 6
Portable 5
Portable 4

Portable 3

Portable 2 Portable 1

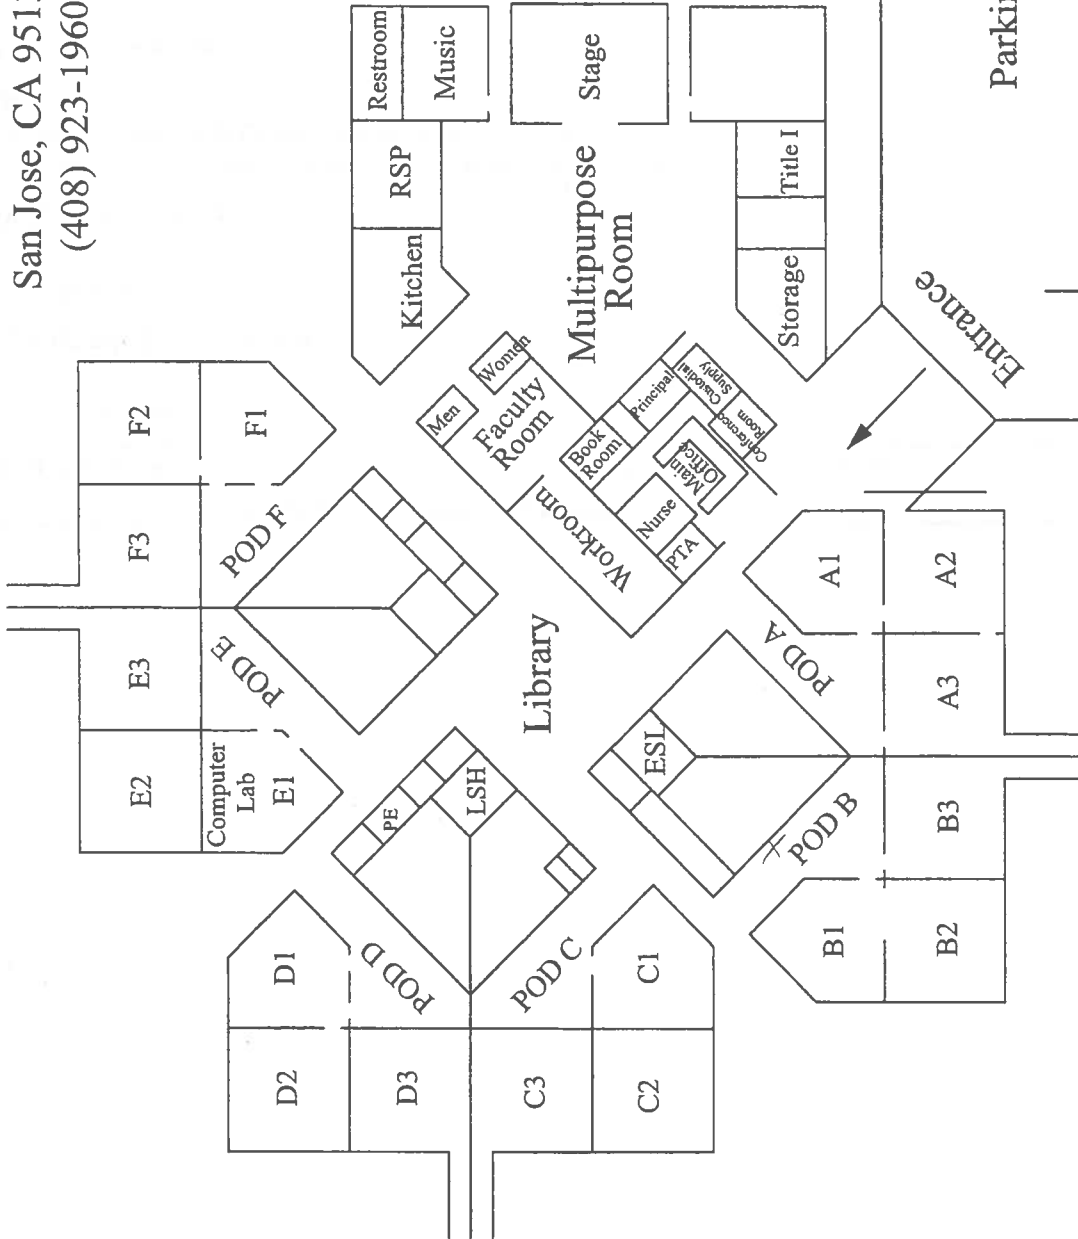

Parking Lot

Summerdale Drive

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsley Drive

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 42-41-8

Portable 7
Portable 6
Portable 5
Portable 4

Portable 3

Portable 2	Portable 1
------------	------------

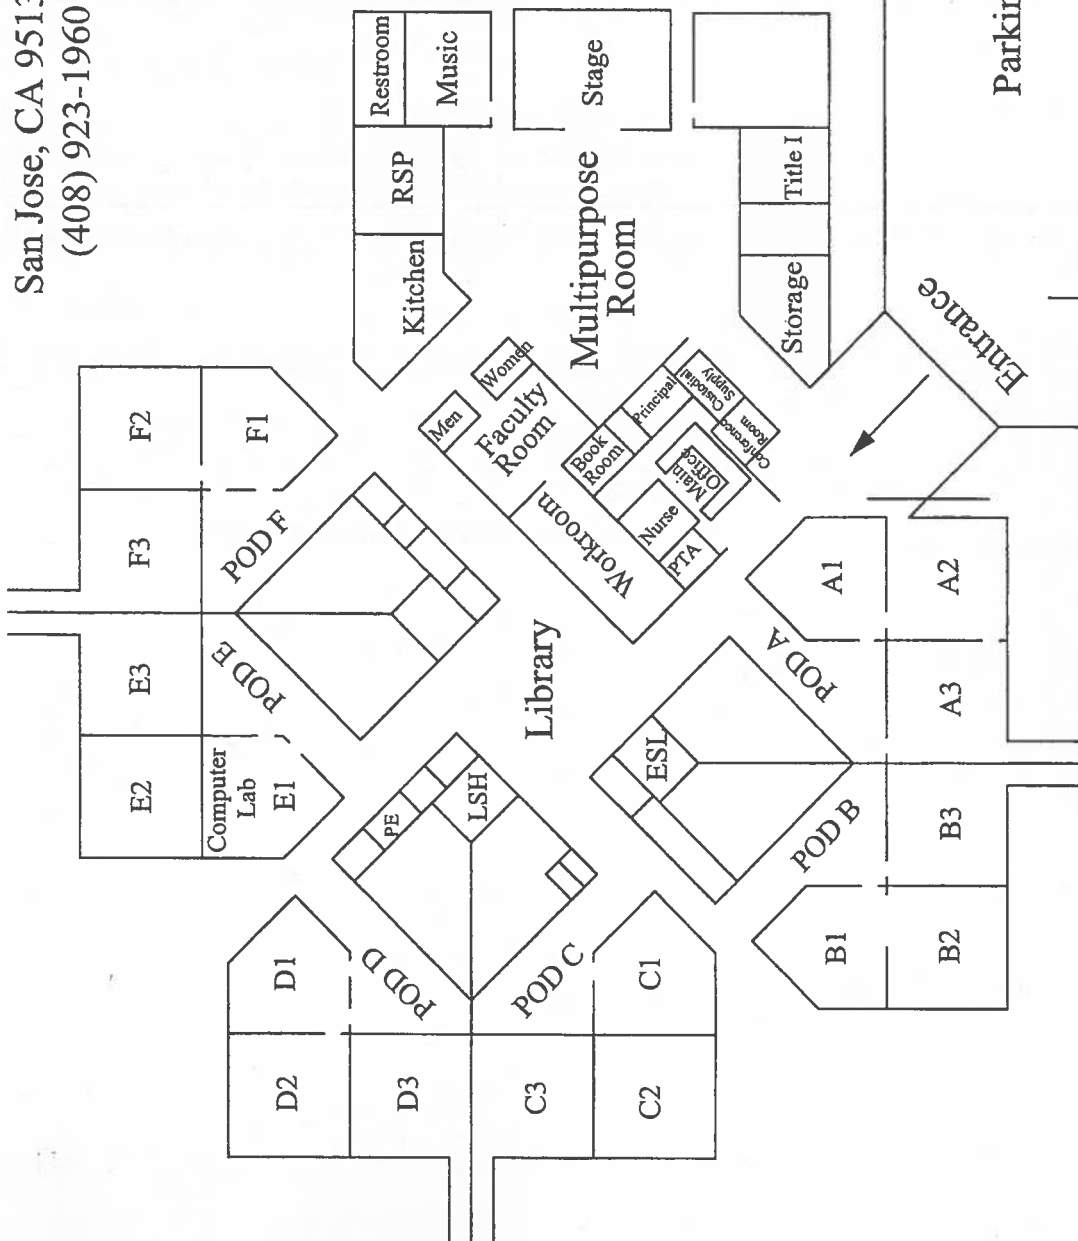

Parking Lot

Summerdale Drive

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsey Drive

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 2-14-24

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

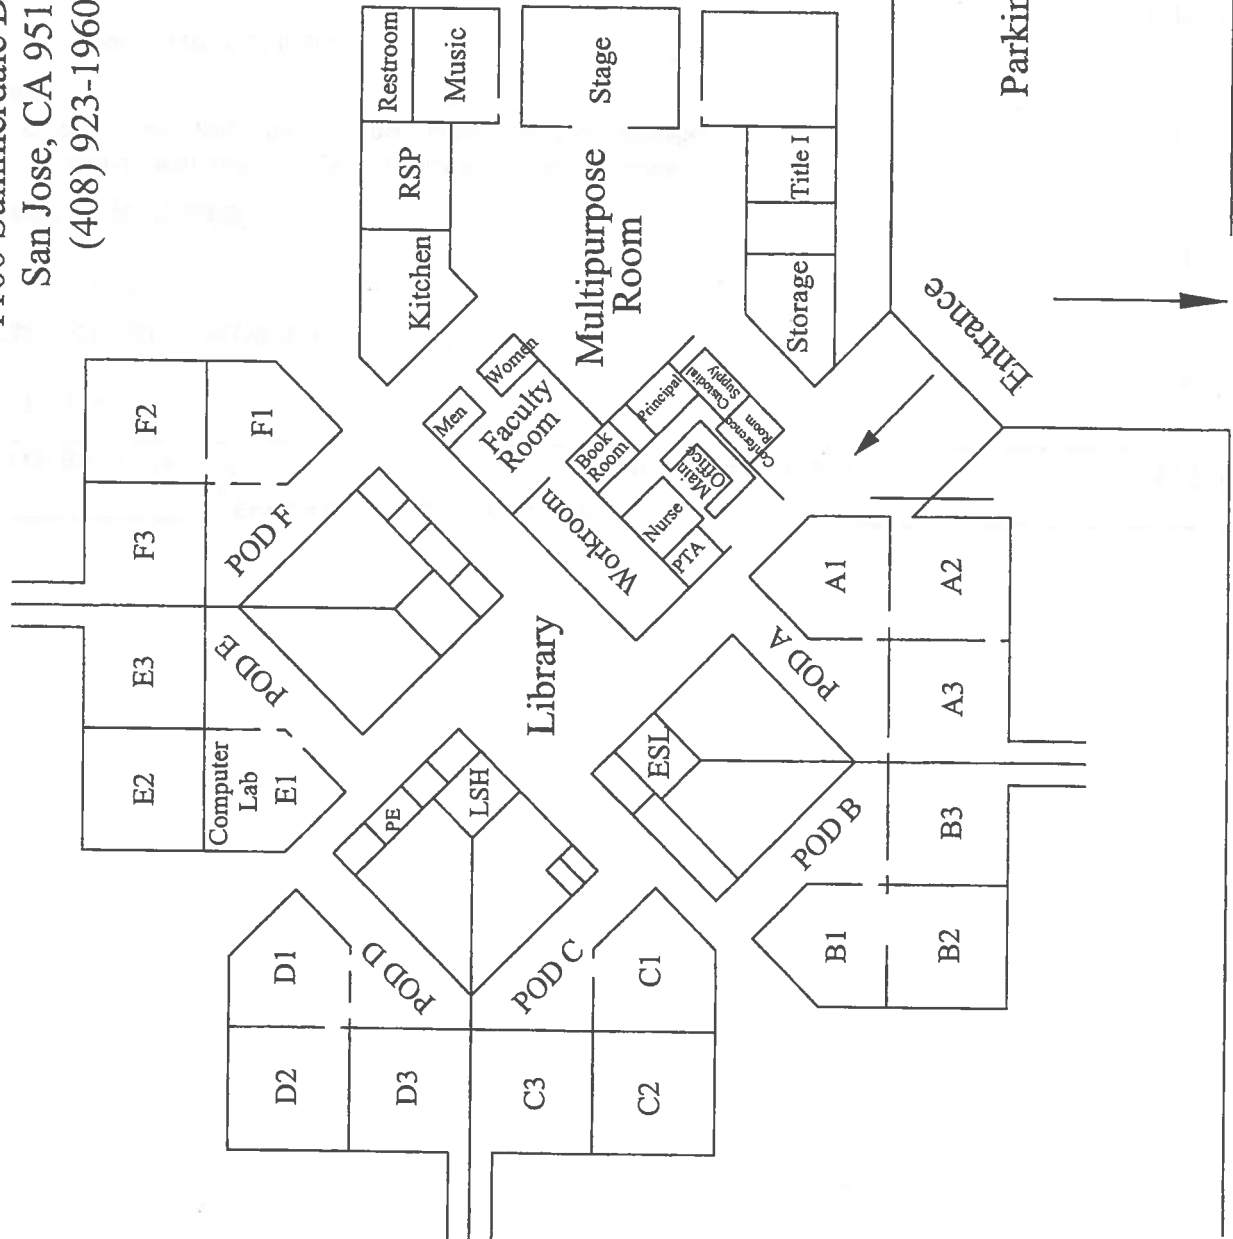

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsley Drive

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 08-16-2023

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2 Portable 1

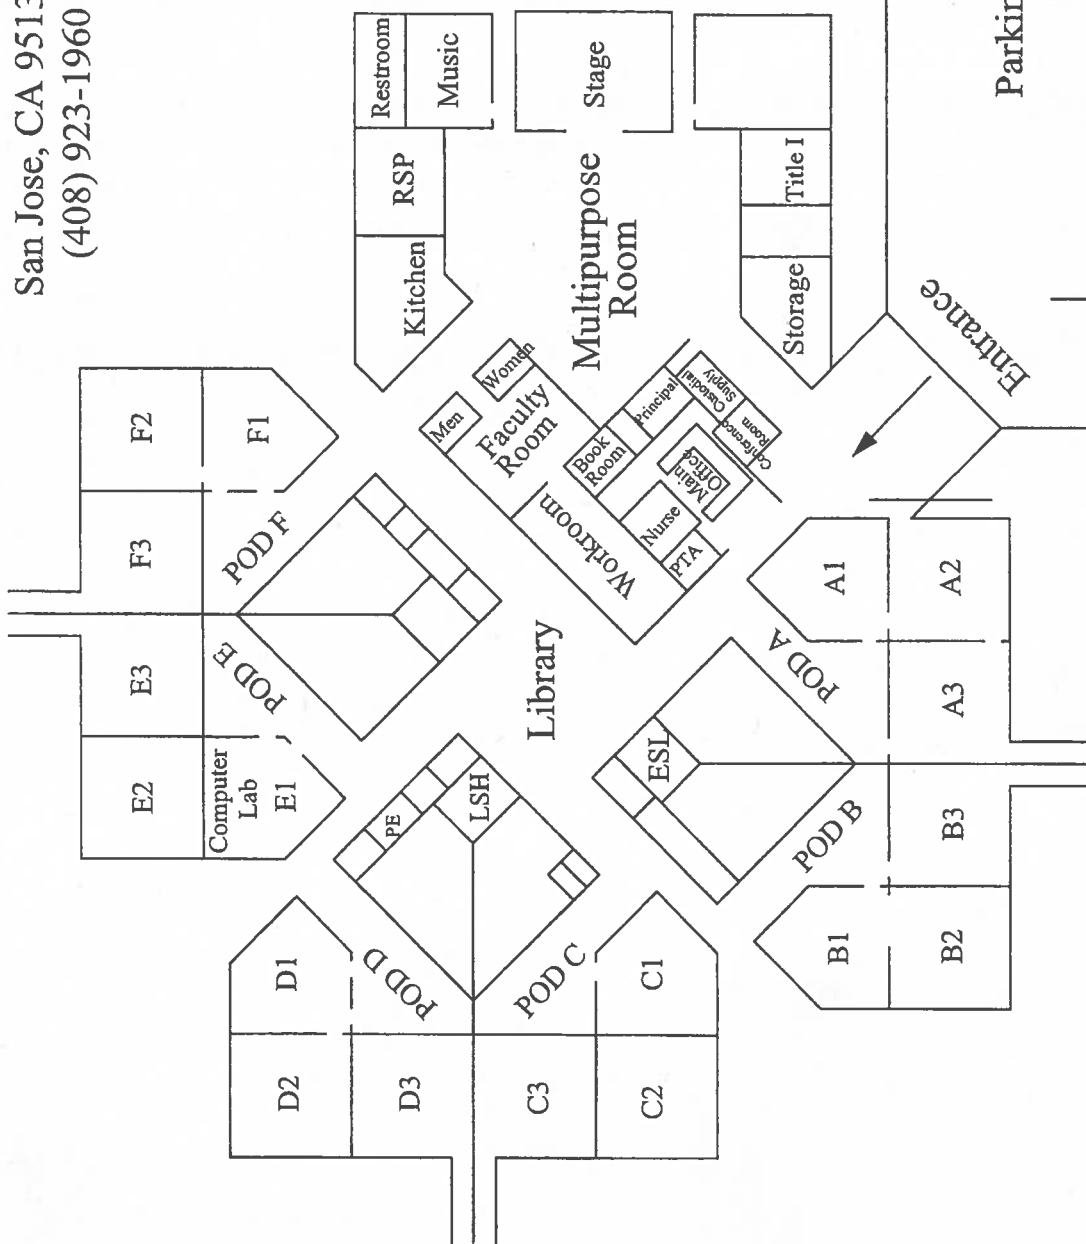

Parking Lot

Summerdale Drive

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmley Drive

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 5/13/23

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

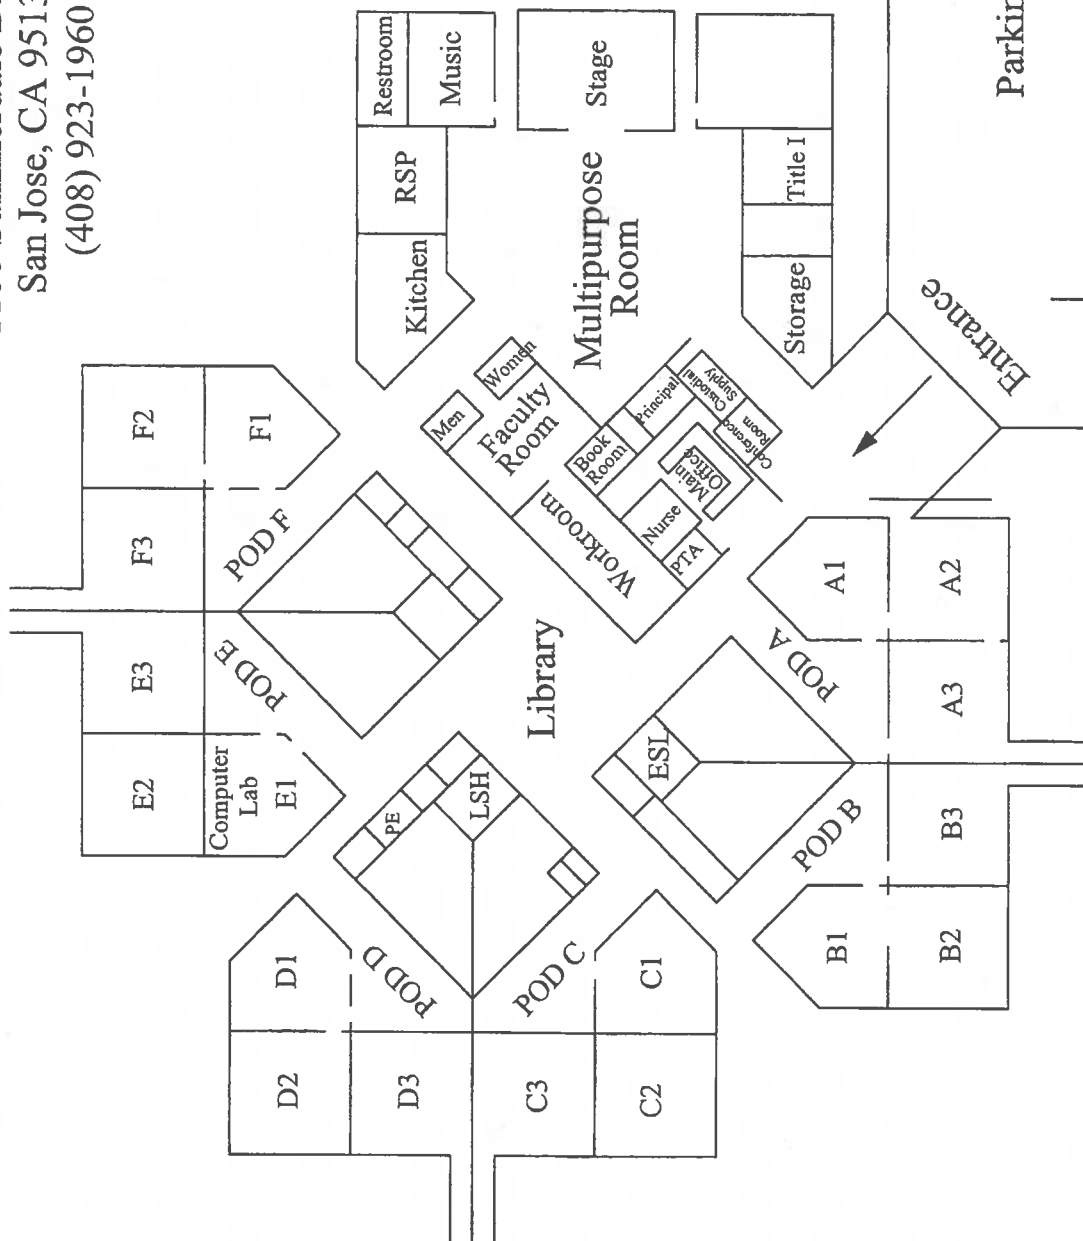

Parking Lot

Summerdale Drive

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsley Drive

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 02-18-2022

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

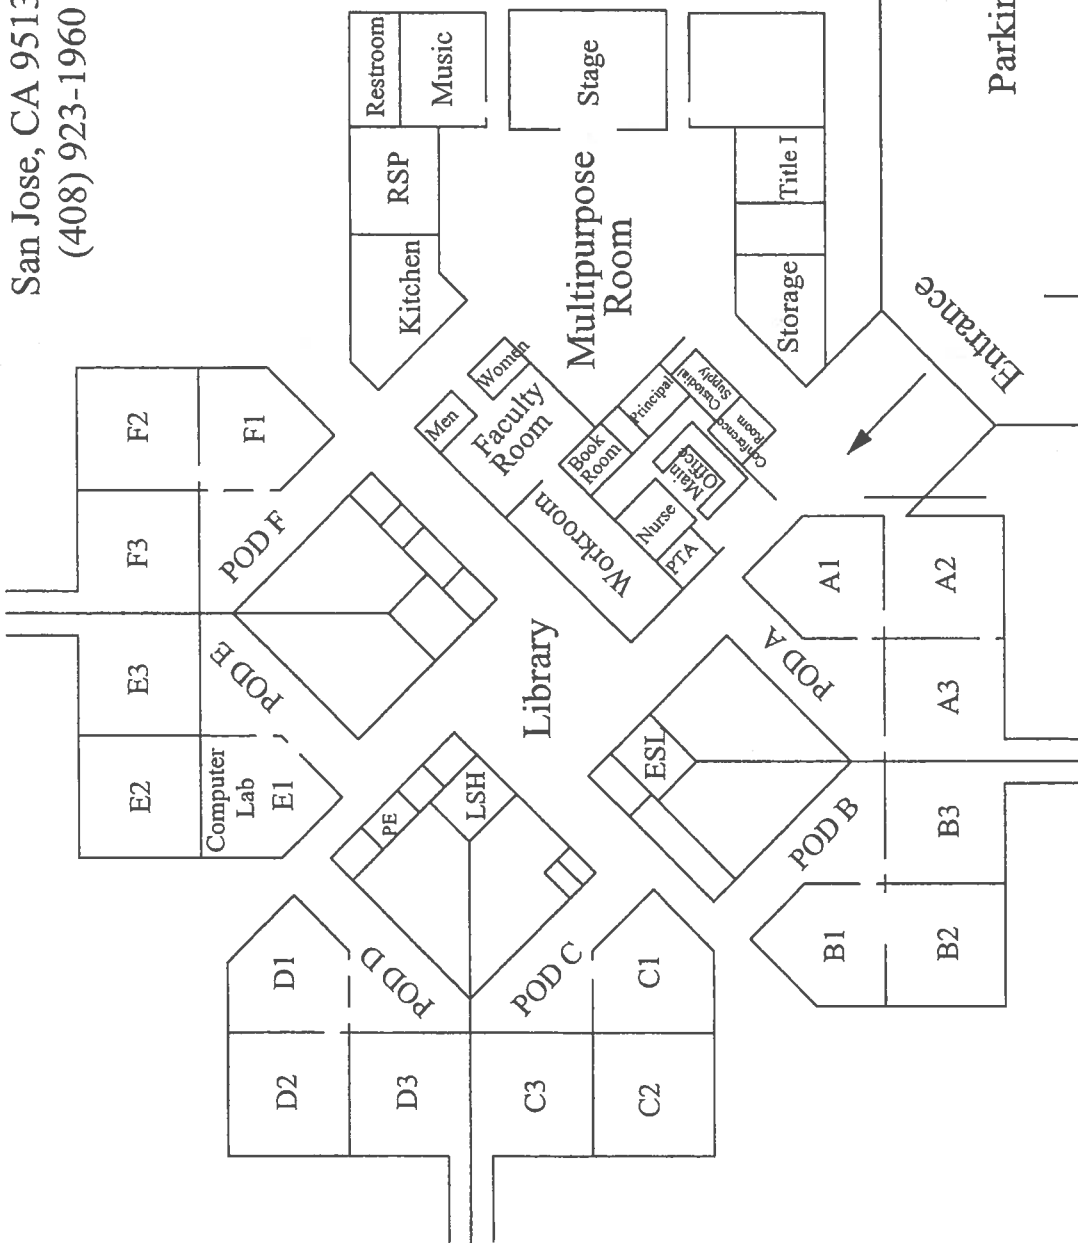

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960

Helmsey Drive

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 12/11/18

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

Restroom
 Music
 RSP
 Kitchen
 Stage
 Multipurpose Room
 Storage
 Title I

F2
 F3
 E3
 E2
 F1
 POD F
 POD E
 Computer Lab
 E1

Men
 Women
 Faculty Room
 Book Room
 Principal
 Nurse
 PTA
 Main Office
 Cafeteria
 Room Supply

Library

D1
 D2
 D3
 C3
 C2
 C1
 POD D
 POD C
 PE
 LSH

A1
 A2
 A3
 B1
 B2
 B3
 POD A
 POD B
 ESL

Parking Lot

Entrance

Summerdale Drive

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmley Drive

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 12/01/21

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

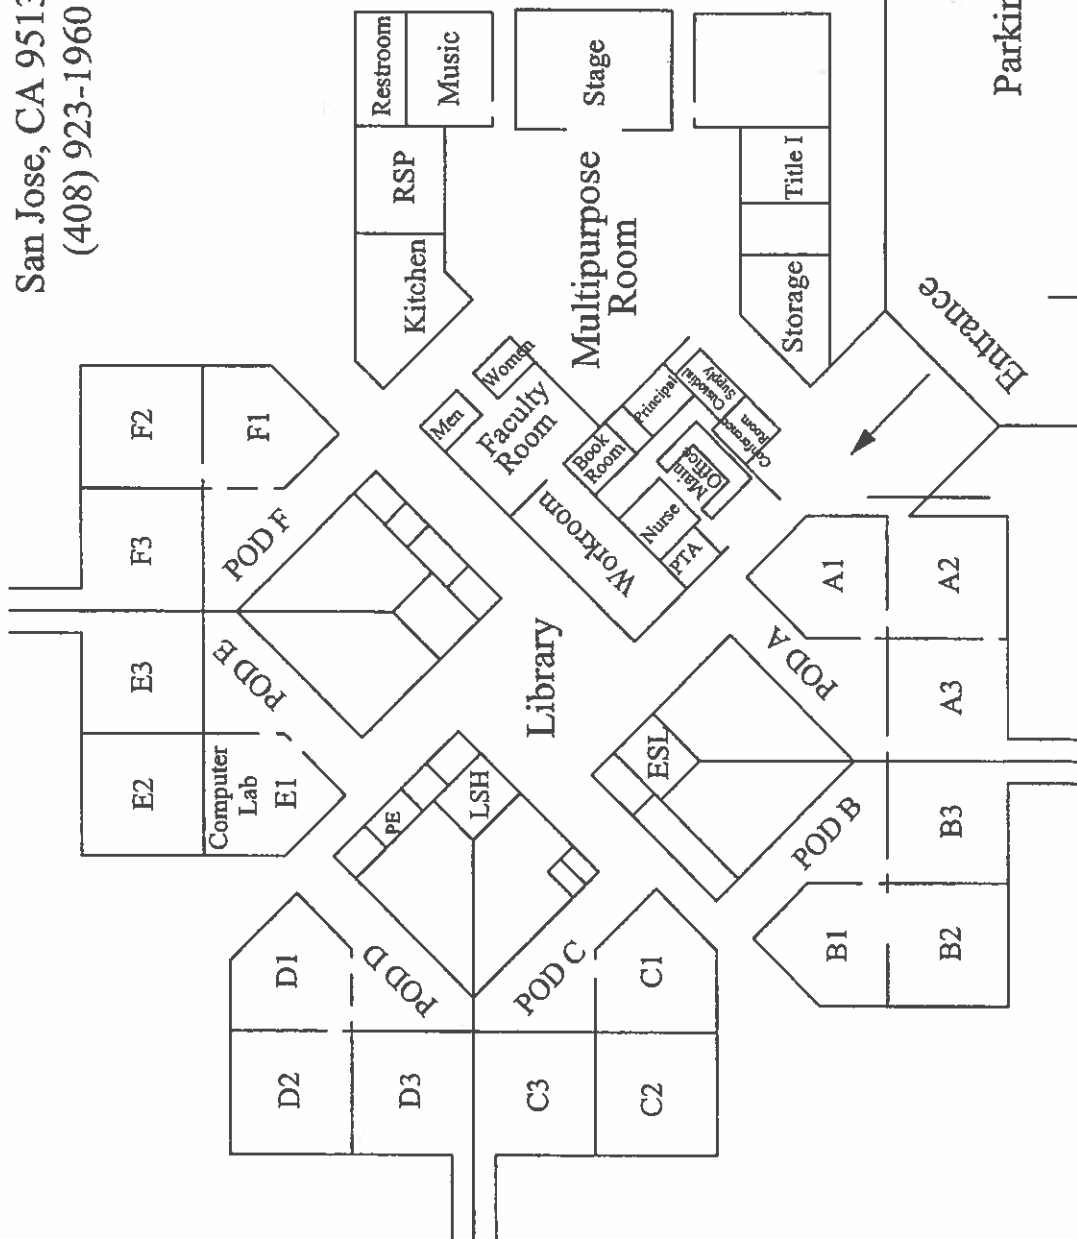

Parking Lot

Entrance

Summerdale Drive

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmley Drive

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 02/28/88

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2 Portable 1

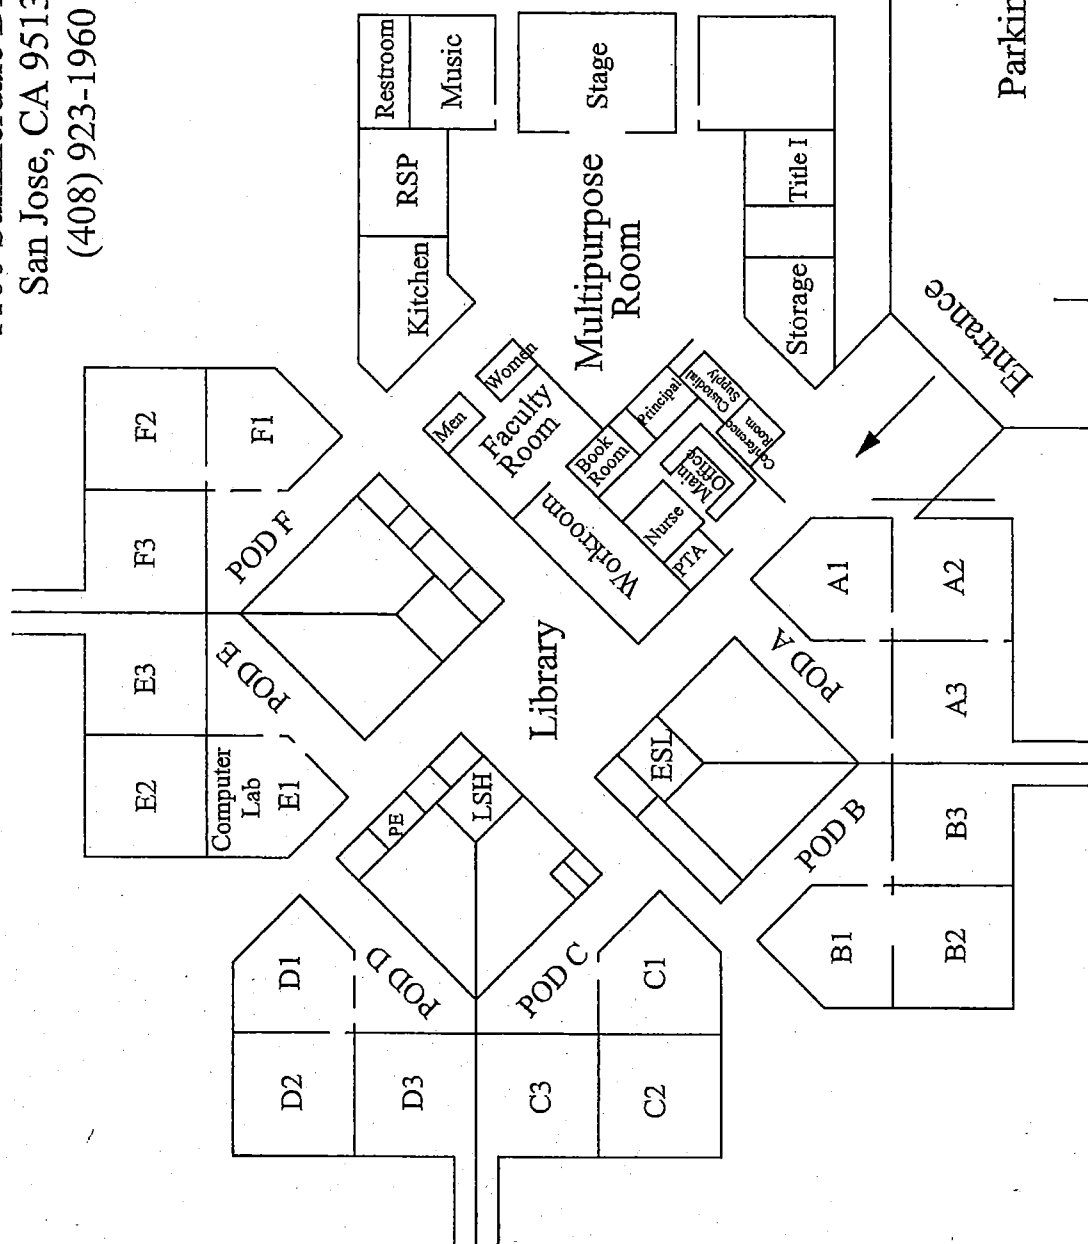

Parking Lot

Summerdale Drive

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960

Helmsey Drive


SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 0202-4-20

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

miss lib

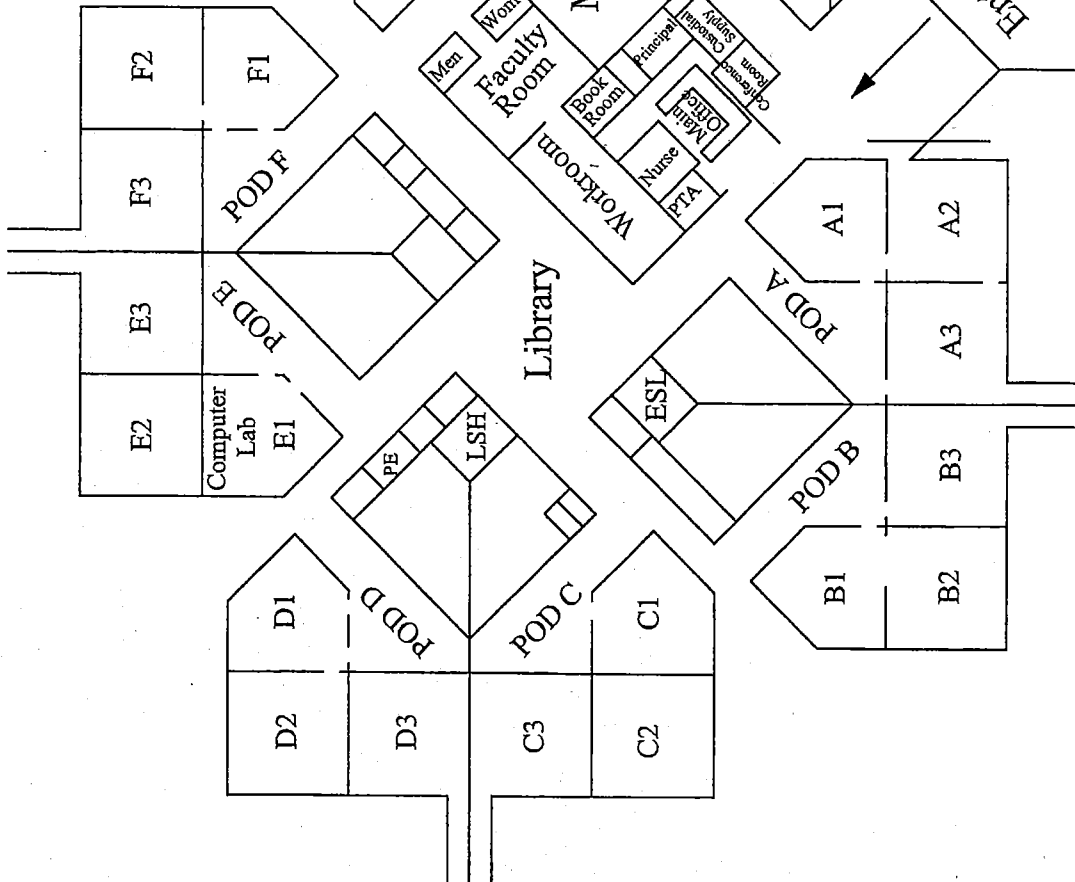

Summerdale Drive

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsley Drive

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 6-14-8

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

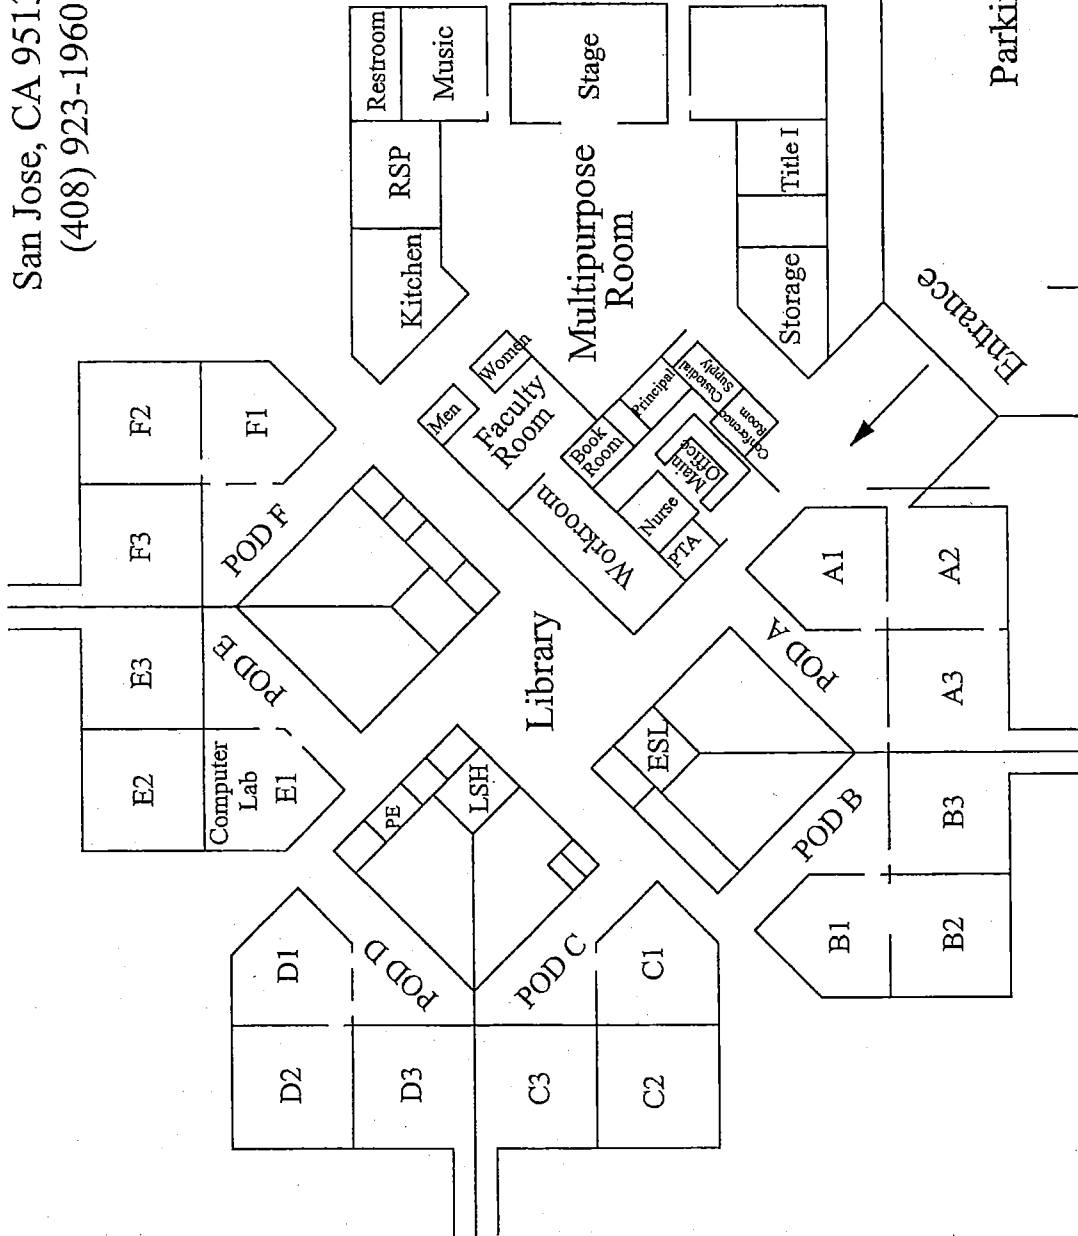

Parking Lot

Summerdale Drive

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsley Drive

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 6/02-90-2019

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

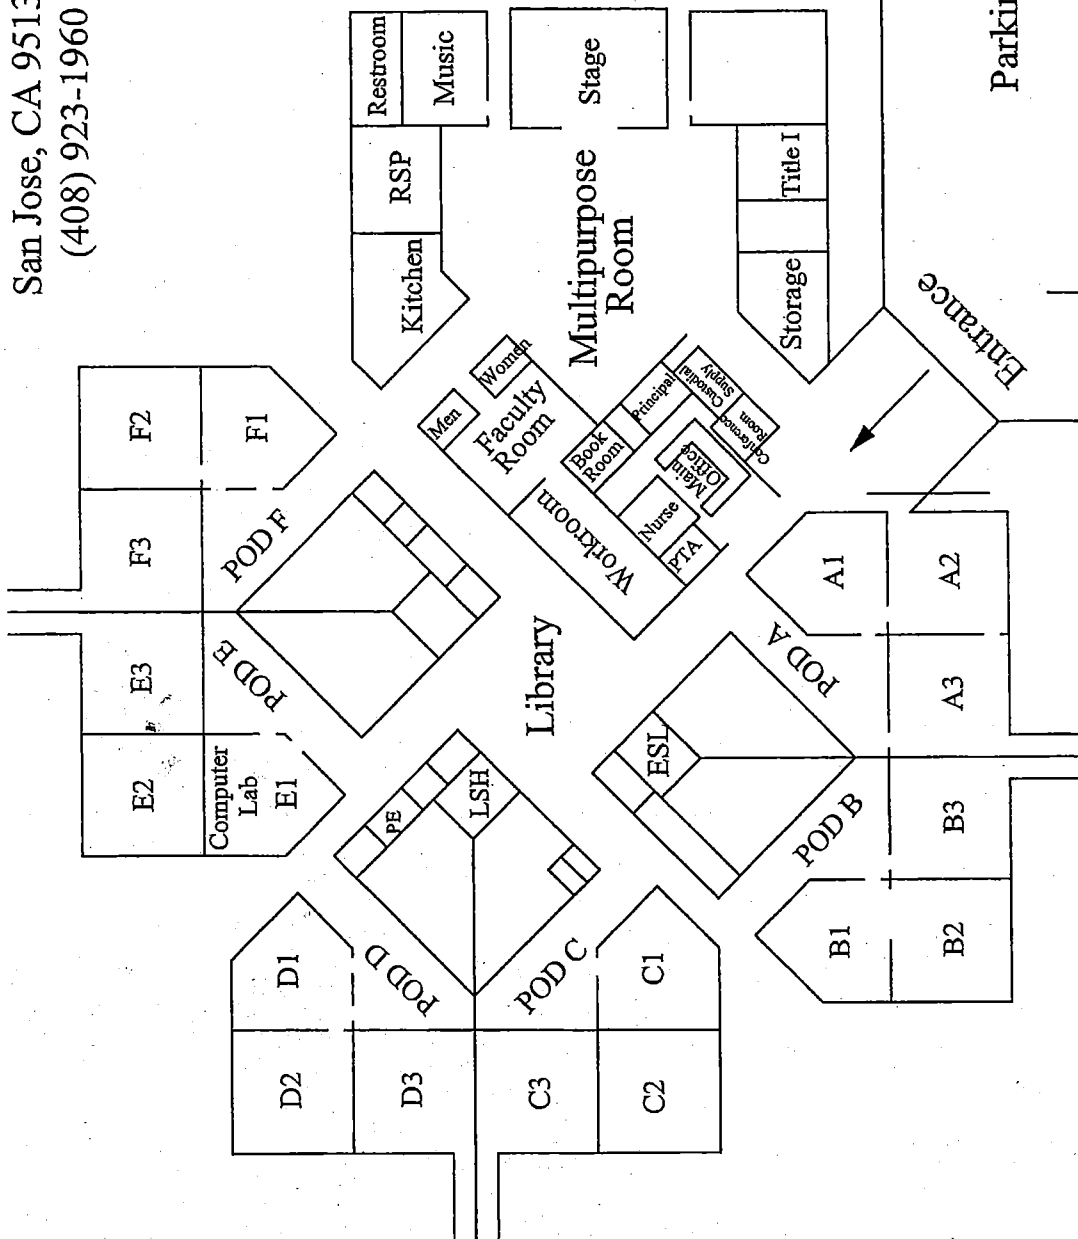

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsley Drive

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 8/9/18

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

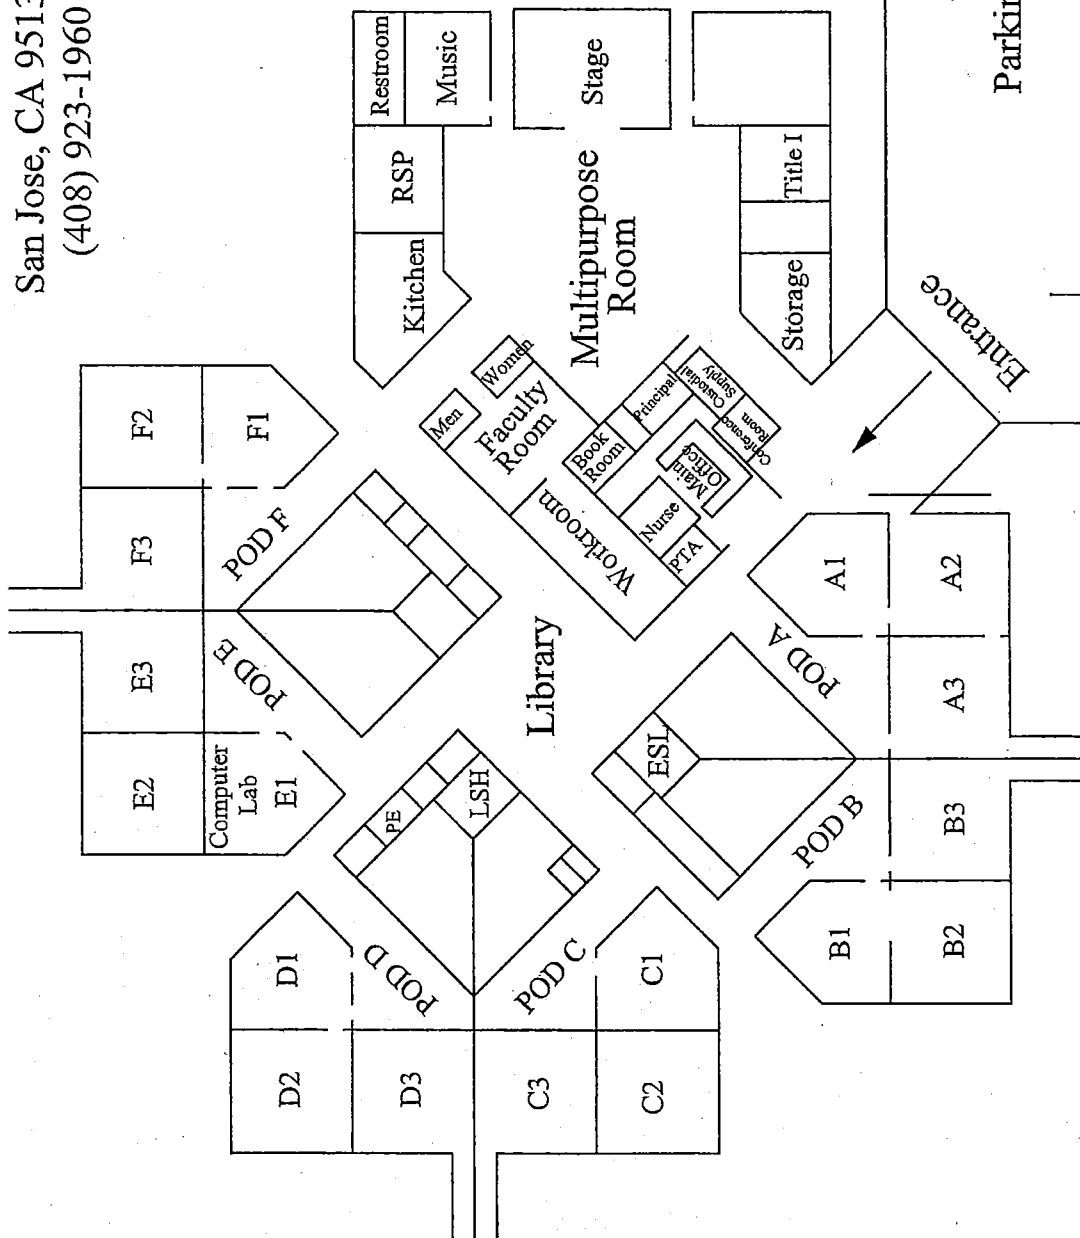

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsley Drive

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 2/14/18

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2 Portable 1

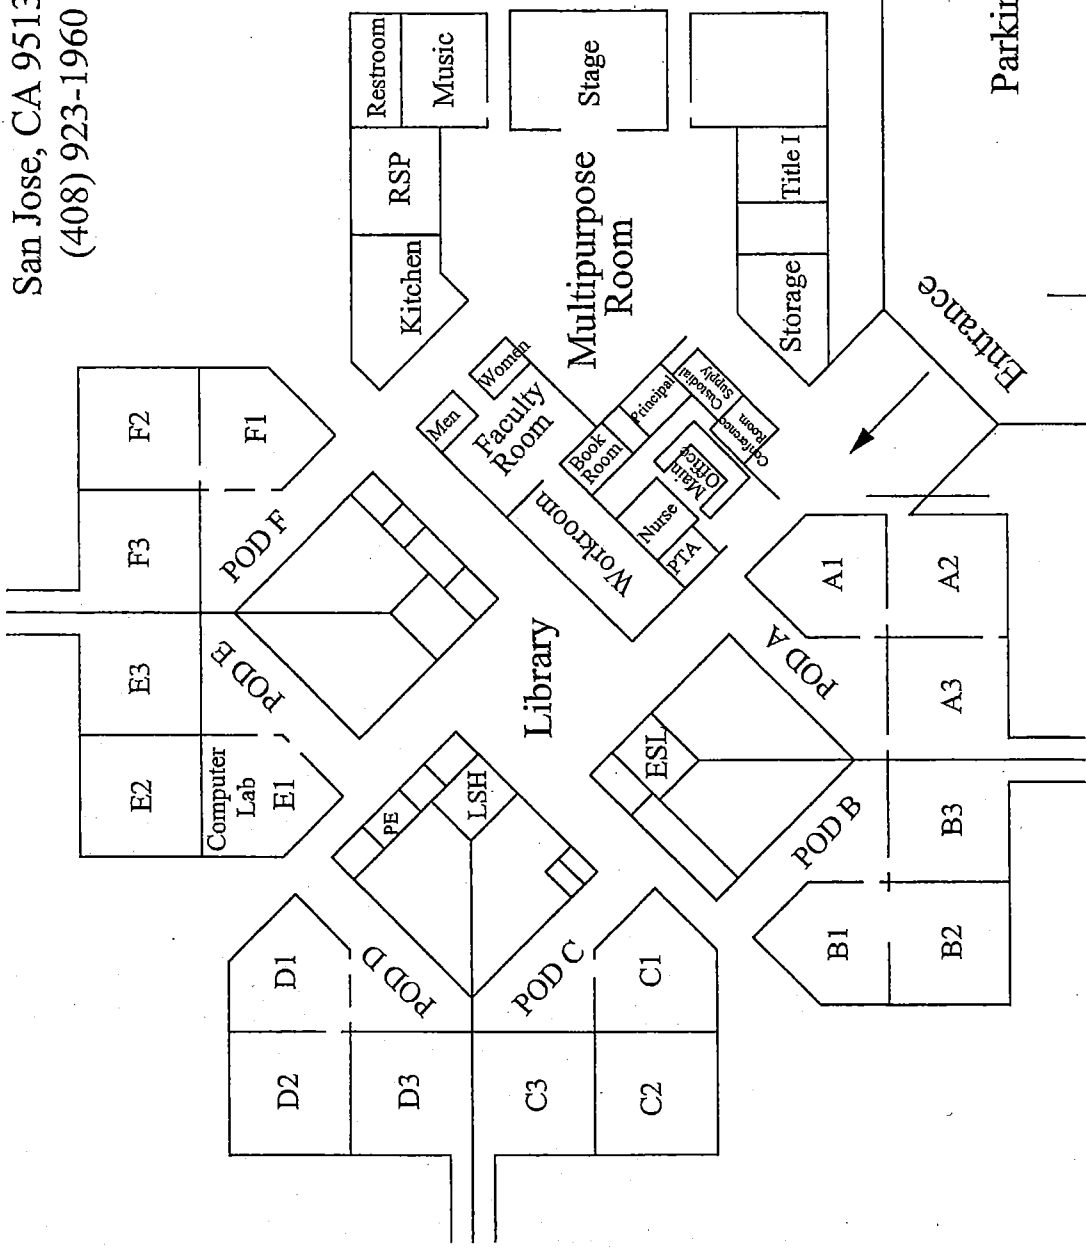

Parking Lot

Summerdale Drive

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsley Drive

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 8/22/17

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2 Portable 1

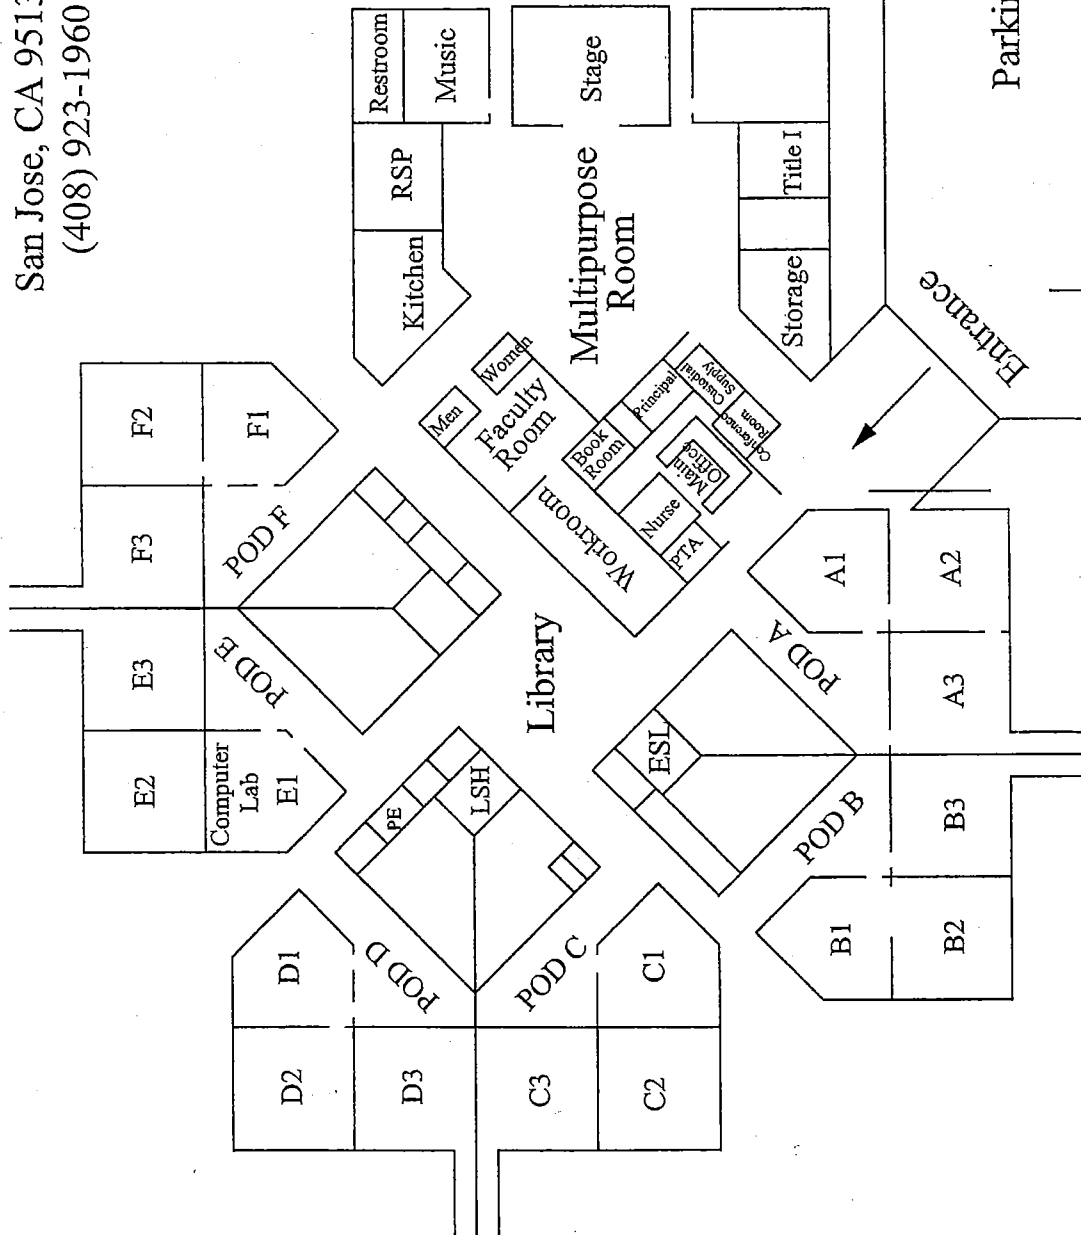

Parking Lot

Summerdale Drive

Entrance

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsley Drive

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 3/29/17

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2 Portable 1

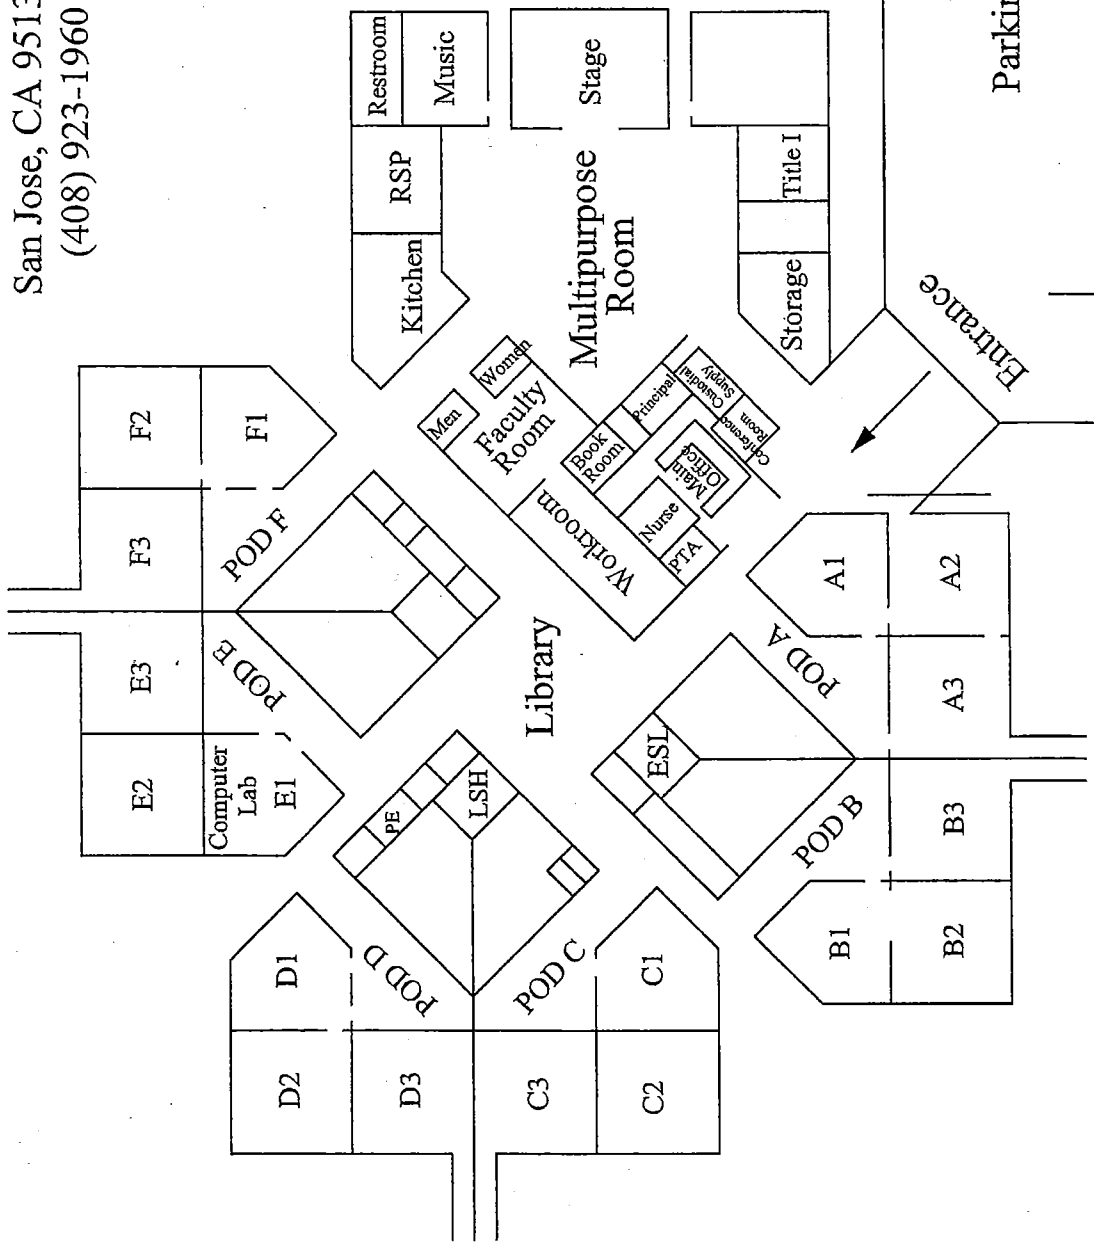

Parking Lot

Summerdale Drive

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsley Drive
 Summerdale Drive

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 9-13-16

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

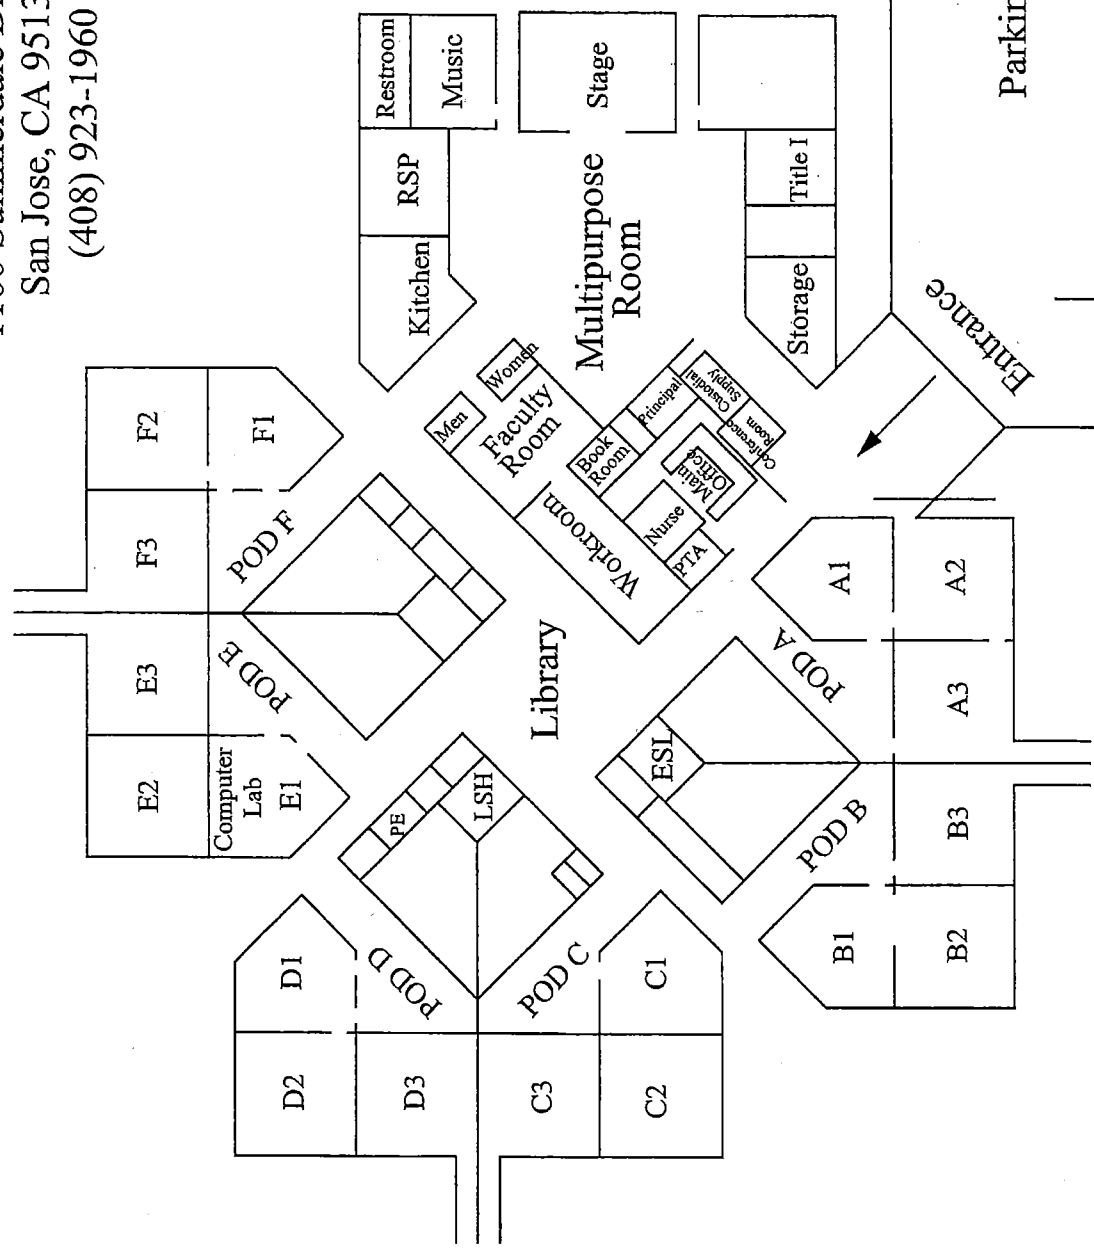

Summerdale Drive

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmsley Drive

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 3-17-16

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

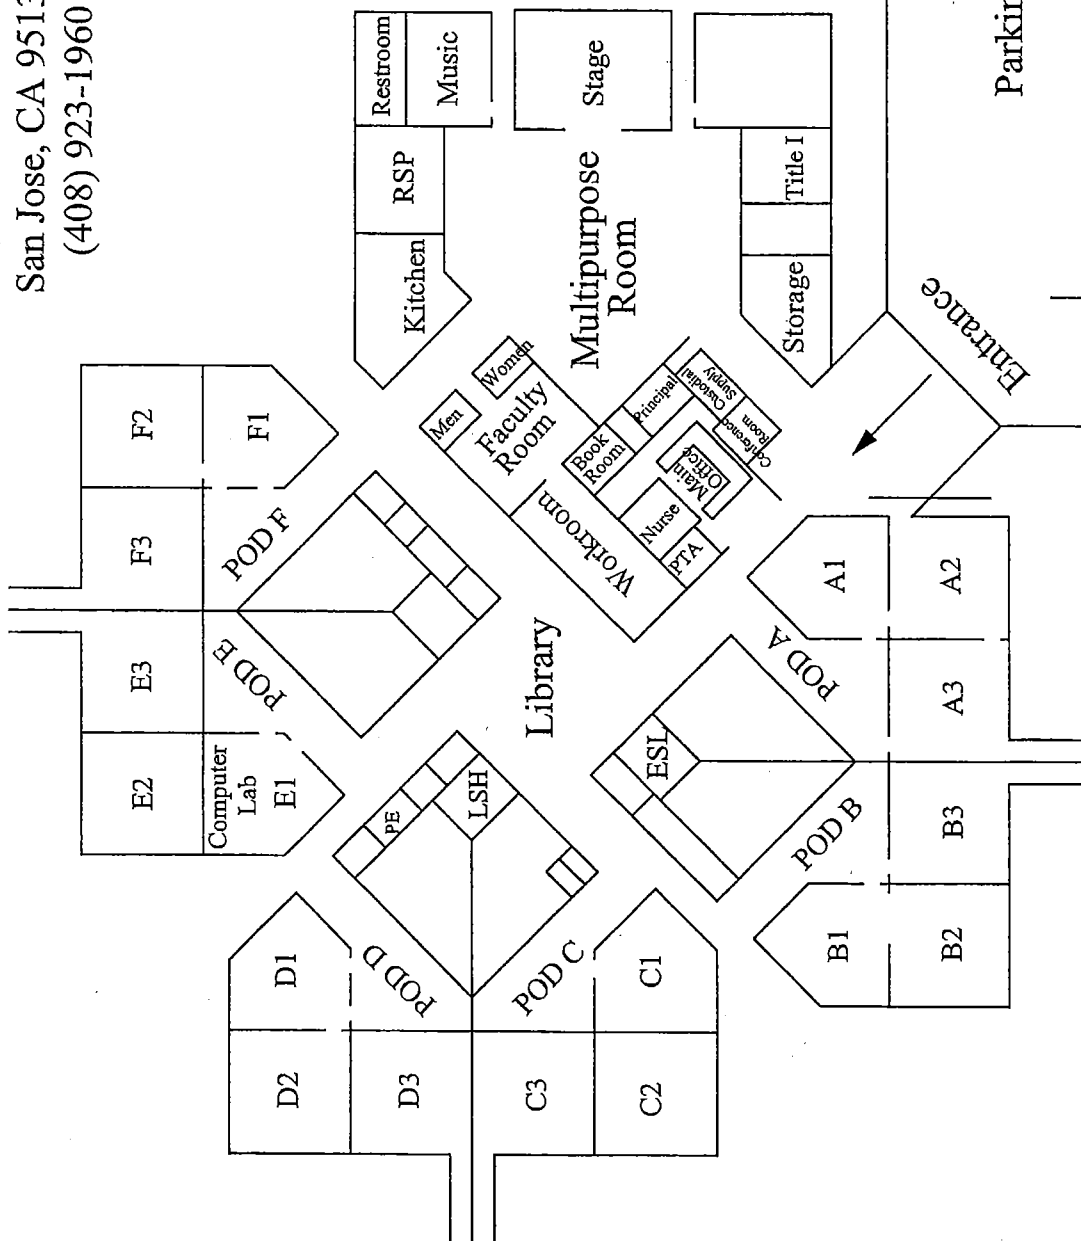

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmley Drive

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 8/18/18

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

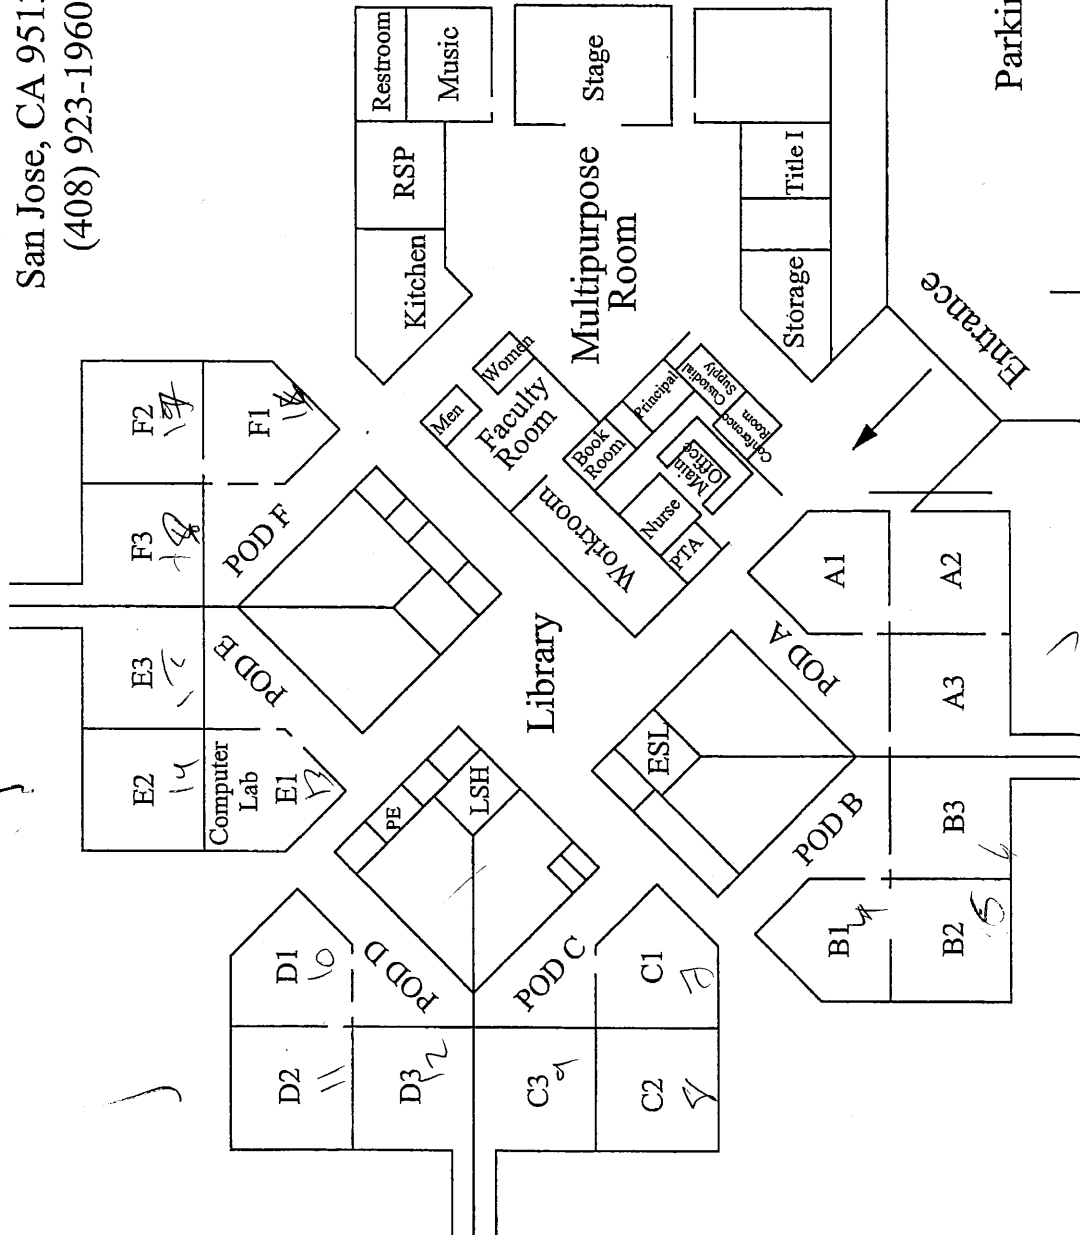

Summerdale Elementary School
 1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960


Helmley Drive


SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 03-17-2015

Portable 7
 Portable 6
 Portable 5
 Portable 4

Portable 3

Portable 2
 Portable 1

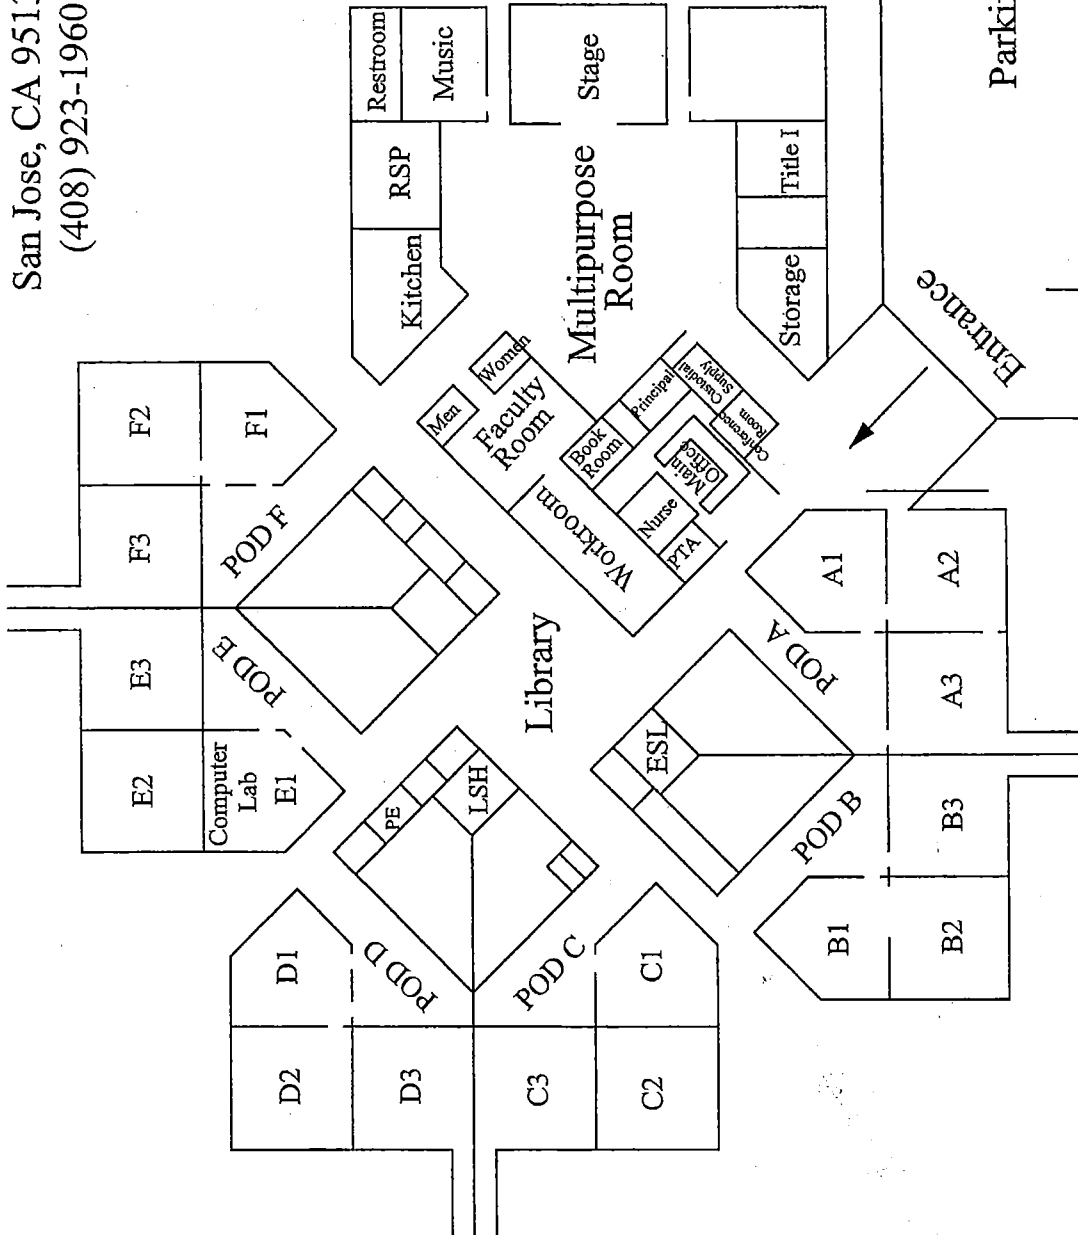



Summerdale Elementary School

1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960
 (408) 937-4923 (fax)

Patty McDonald, Principal

Tran

P-6

King

P-5


Labrador

P-4

P-3


Hopes

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 08-27-2014

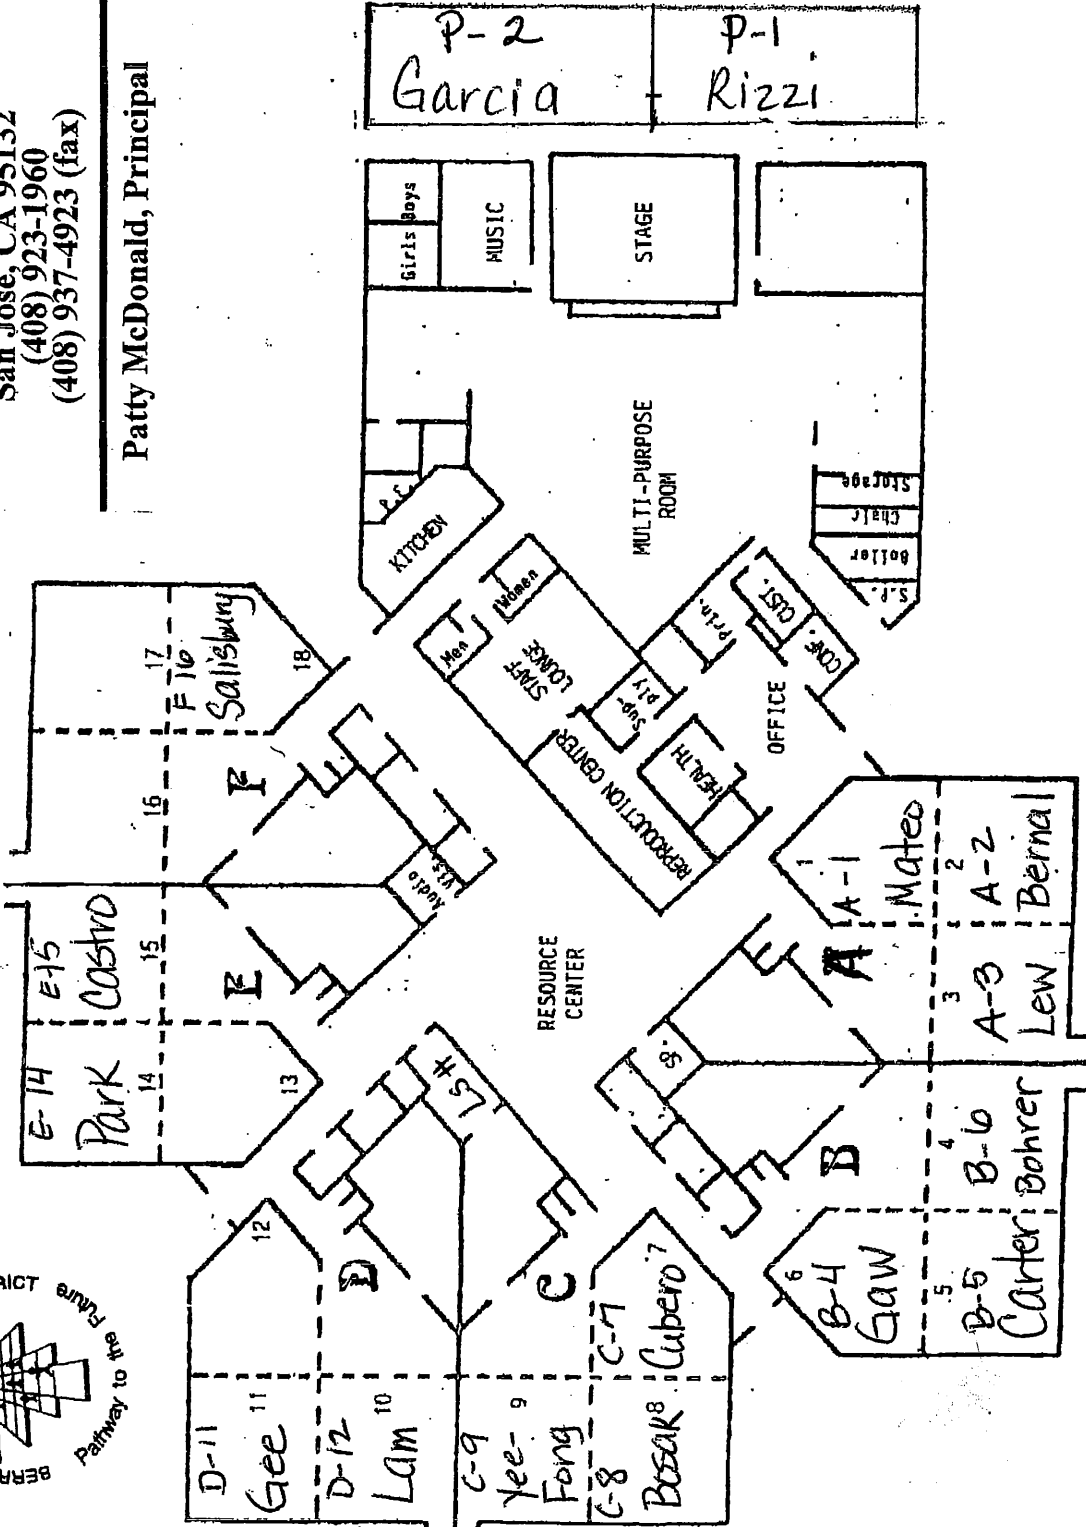

P-2
 Garcia

P-1
 Rizzi



Summerdale Elementary School

1100 Summerdale Drive
San Jose, CA 95132
(408) 923-1960
(408) 937-4923 (fax)

Patty McDonald, Principal

Tran

P-6

King

P-5


Labrador


P-4

P-3

Hopes

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 3-5-14

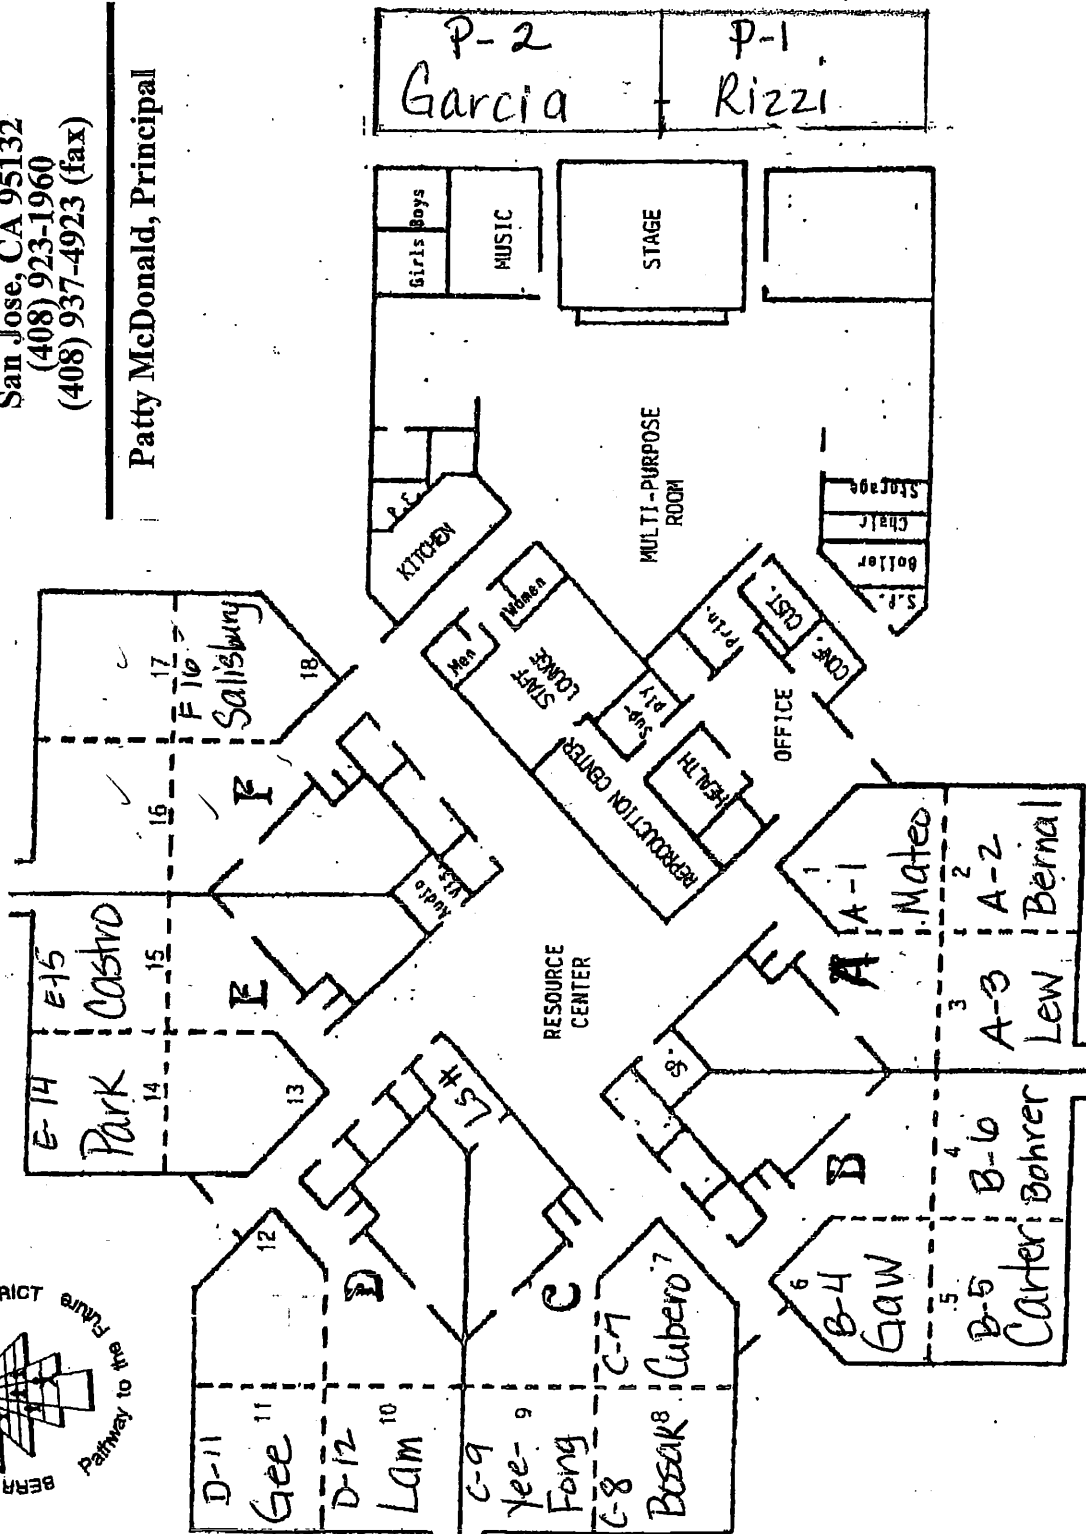



Summerdale Elementary School

1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960
 (408) 937-4923 (fax)

Patty McDonald, Principal

Tran

P-6

King

P-5


Labrador

P-4

P-3


Hopes

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 09-25-2013

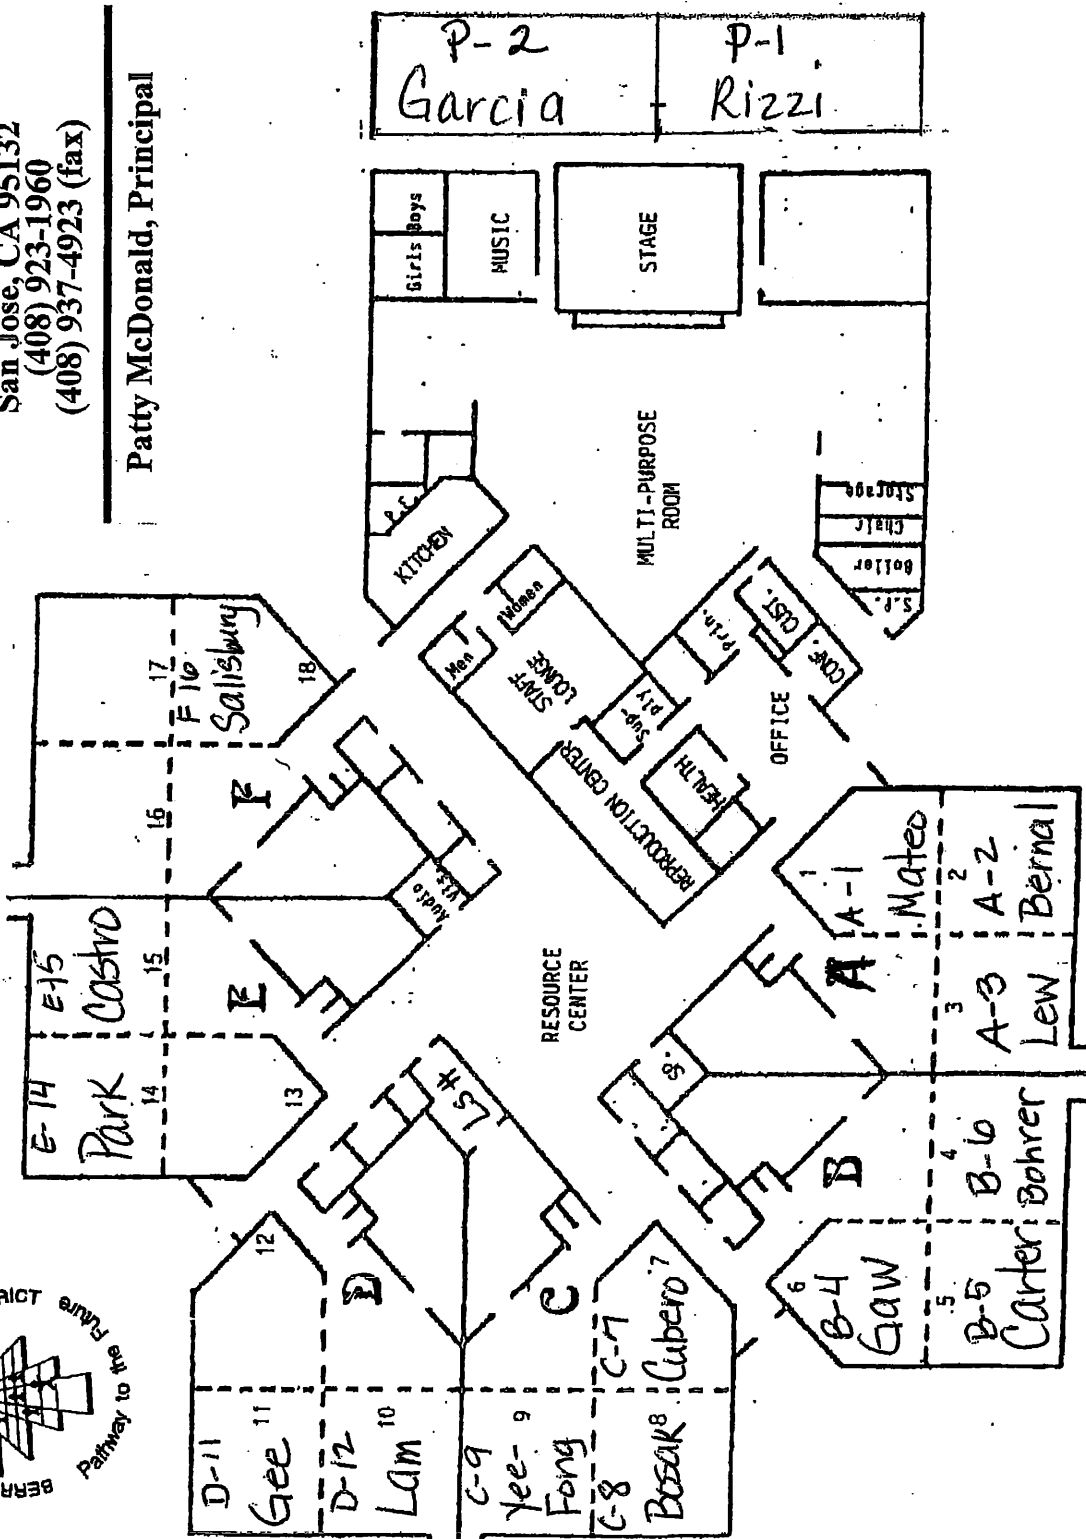

P-2
 Garcia

P-1
 Rizzi



Summerdale Elementary School

1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960
 (408) 937-4923 (fax)

Patty McDonald, Principal

Tran

P-6

King

P-5


Labrador


P-4

P-3

Hopes

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 04-03-13

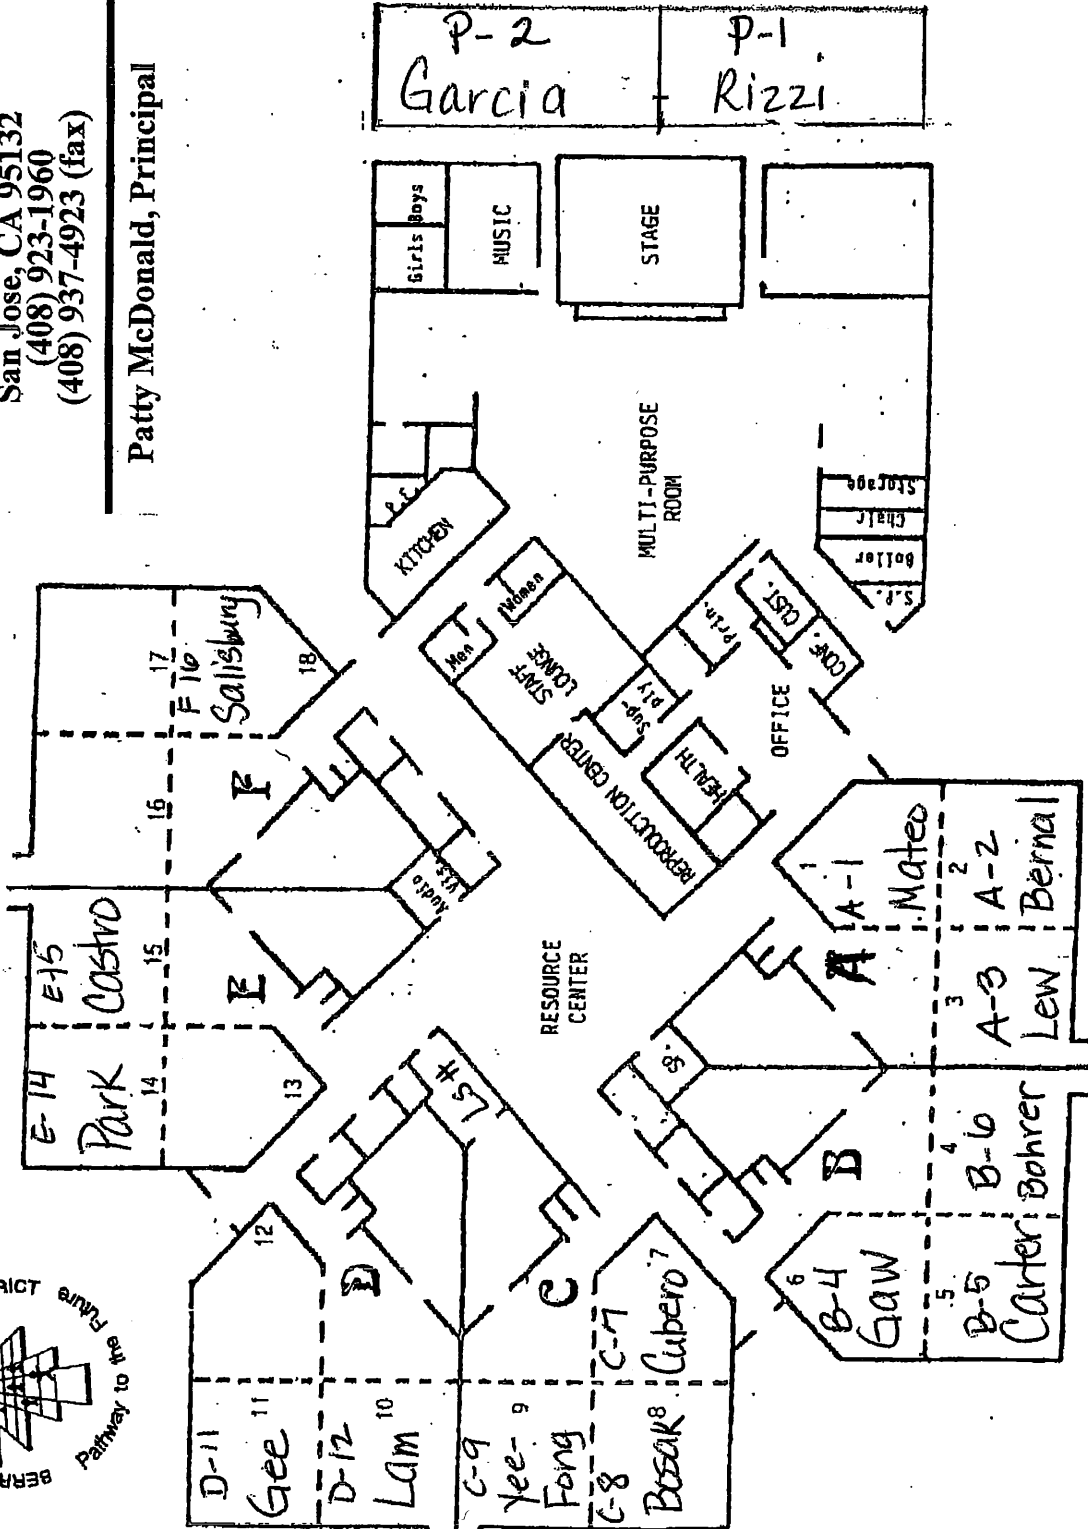



Summerdale Elementary School

1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960
 (408) 937-4923 (fax)

Patty McDonald, Principal

Tran

P-6

King

P-5


Labrador


P-4

P-3

Hopes

SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON: 10-10-12

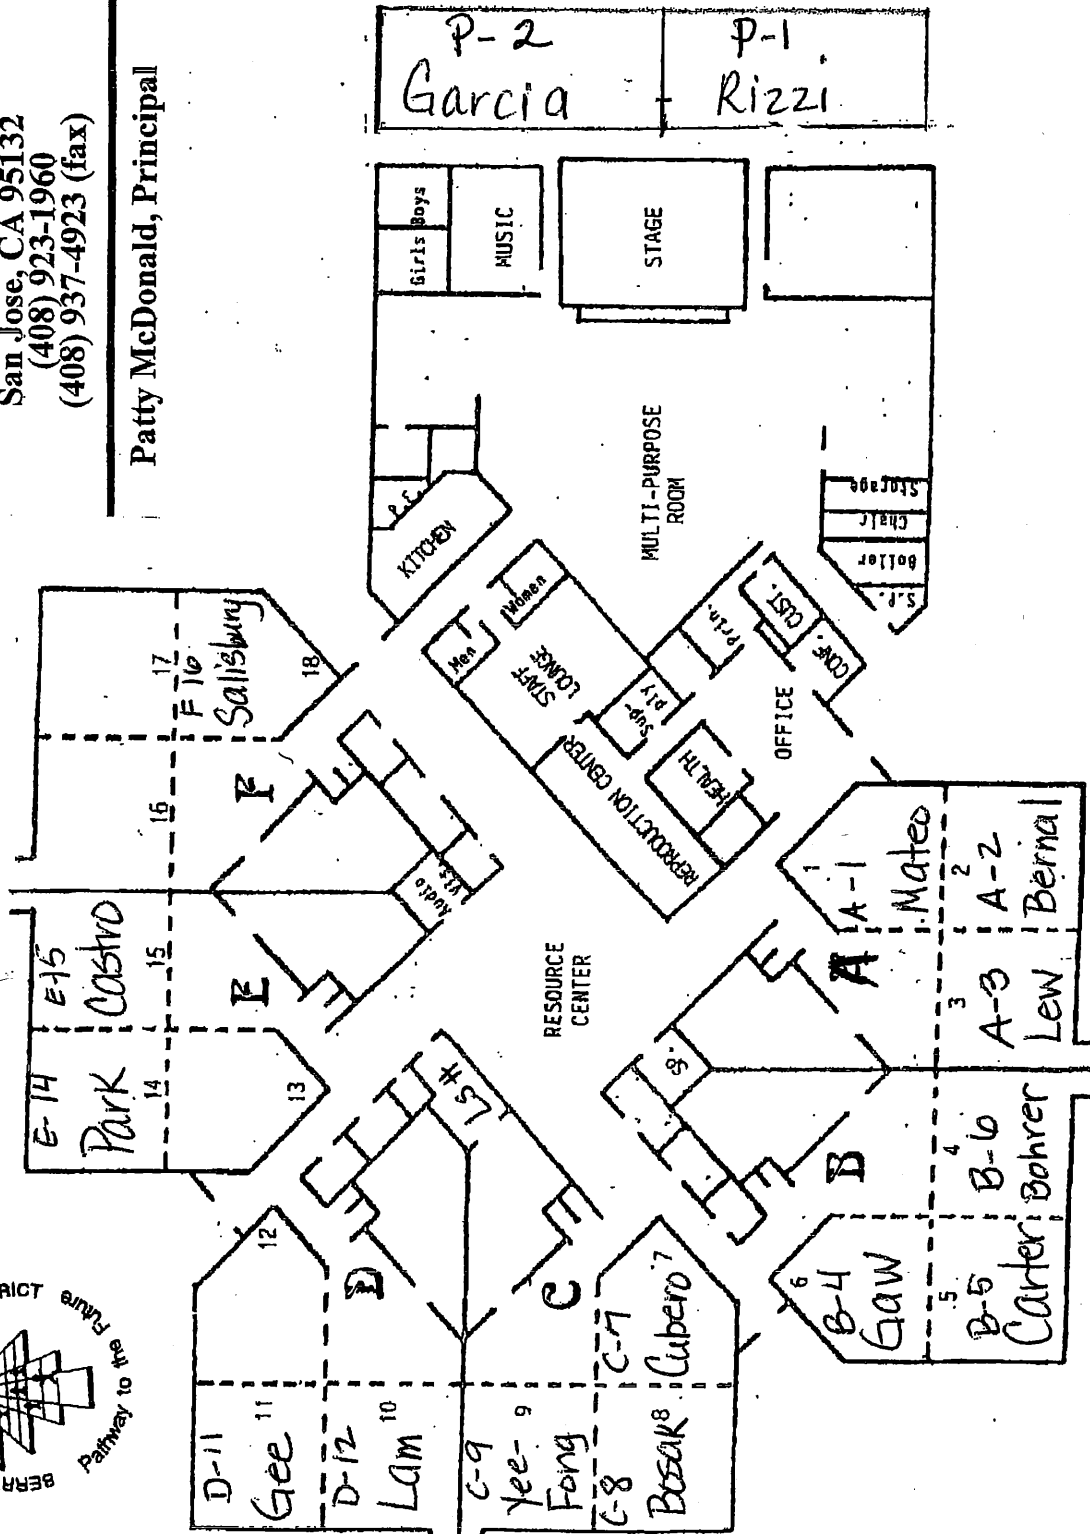



Summerdale Elementary School


1100 Summerdale Drive
San Jose, CA 95132
(408) 923-1960
(408) 937-4923 (fax)


Patty McDonald, Principal

Tran
P-6
King
P-5
Labrador
P-4

P-3
Hopes

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 04-09-12

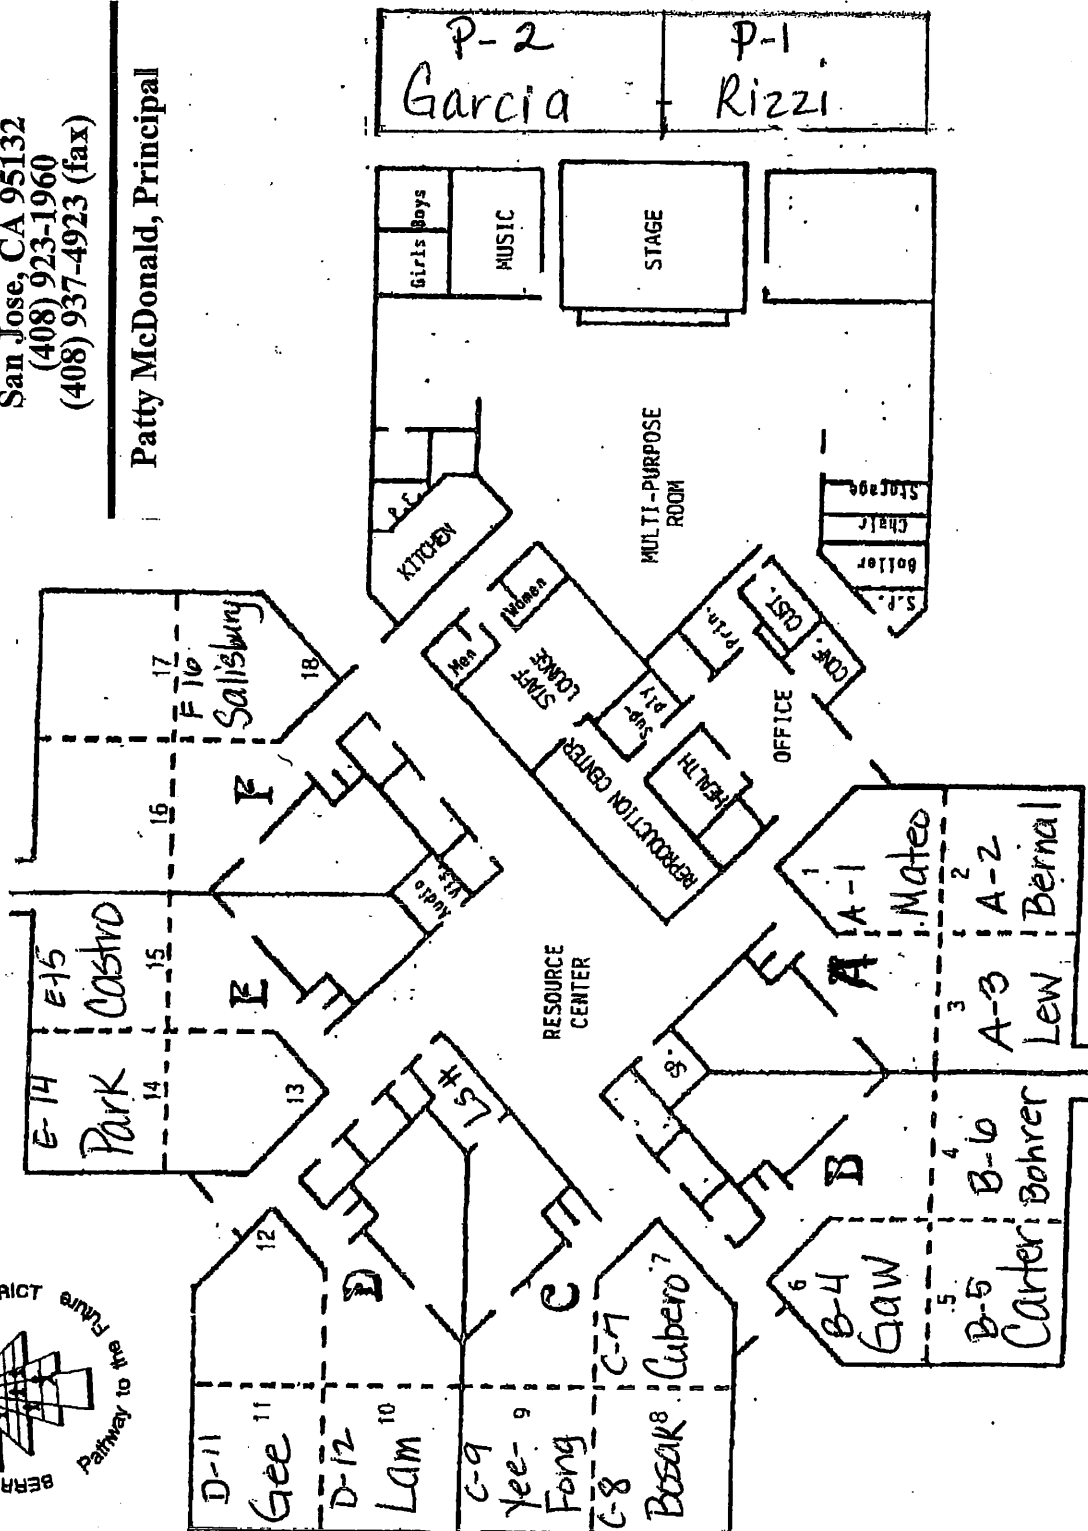



Summerdale Elementary School

1100 Summerdale Drive
 San Jose, CA 95132
 (408) 923-1960
 (408) 937-4923 (fax)

Patty McDonald, Principal

Tran

P-6

King


P-5

Labrador

P-4

P-3

Hopes

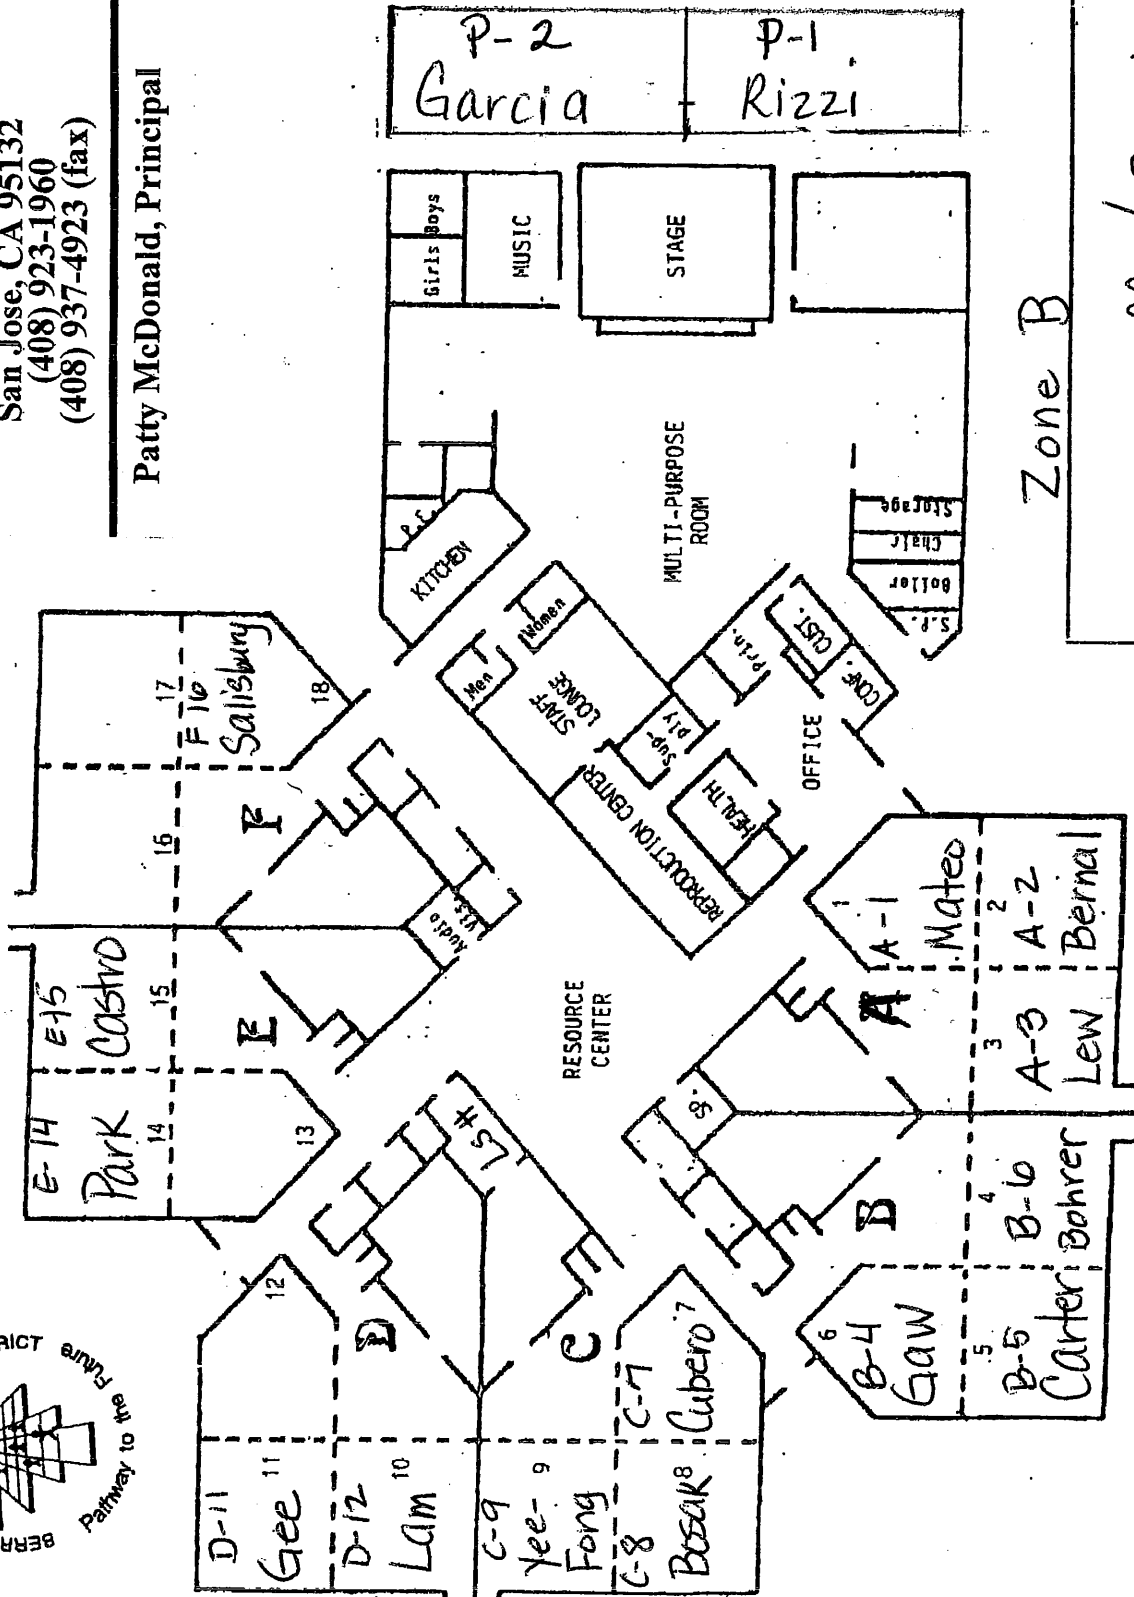

Zone A

Drop off / Pick Up Area

Summerdale School

1100 Summerdale Drive


San Jose, CA 95132

P. 1

408-261-1183

Rob LaPore

Nov 14 06 08:49a

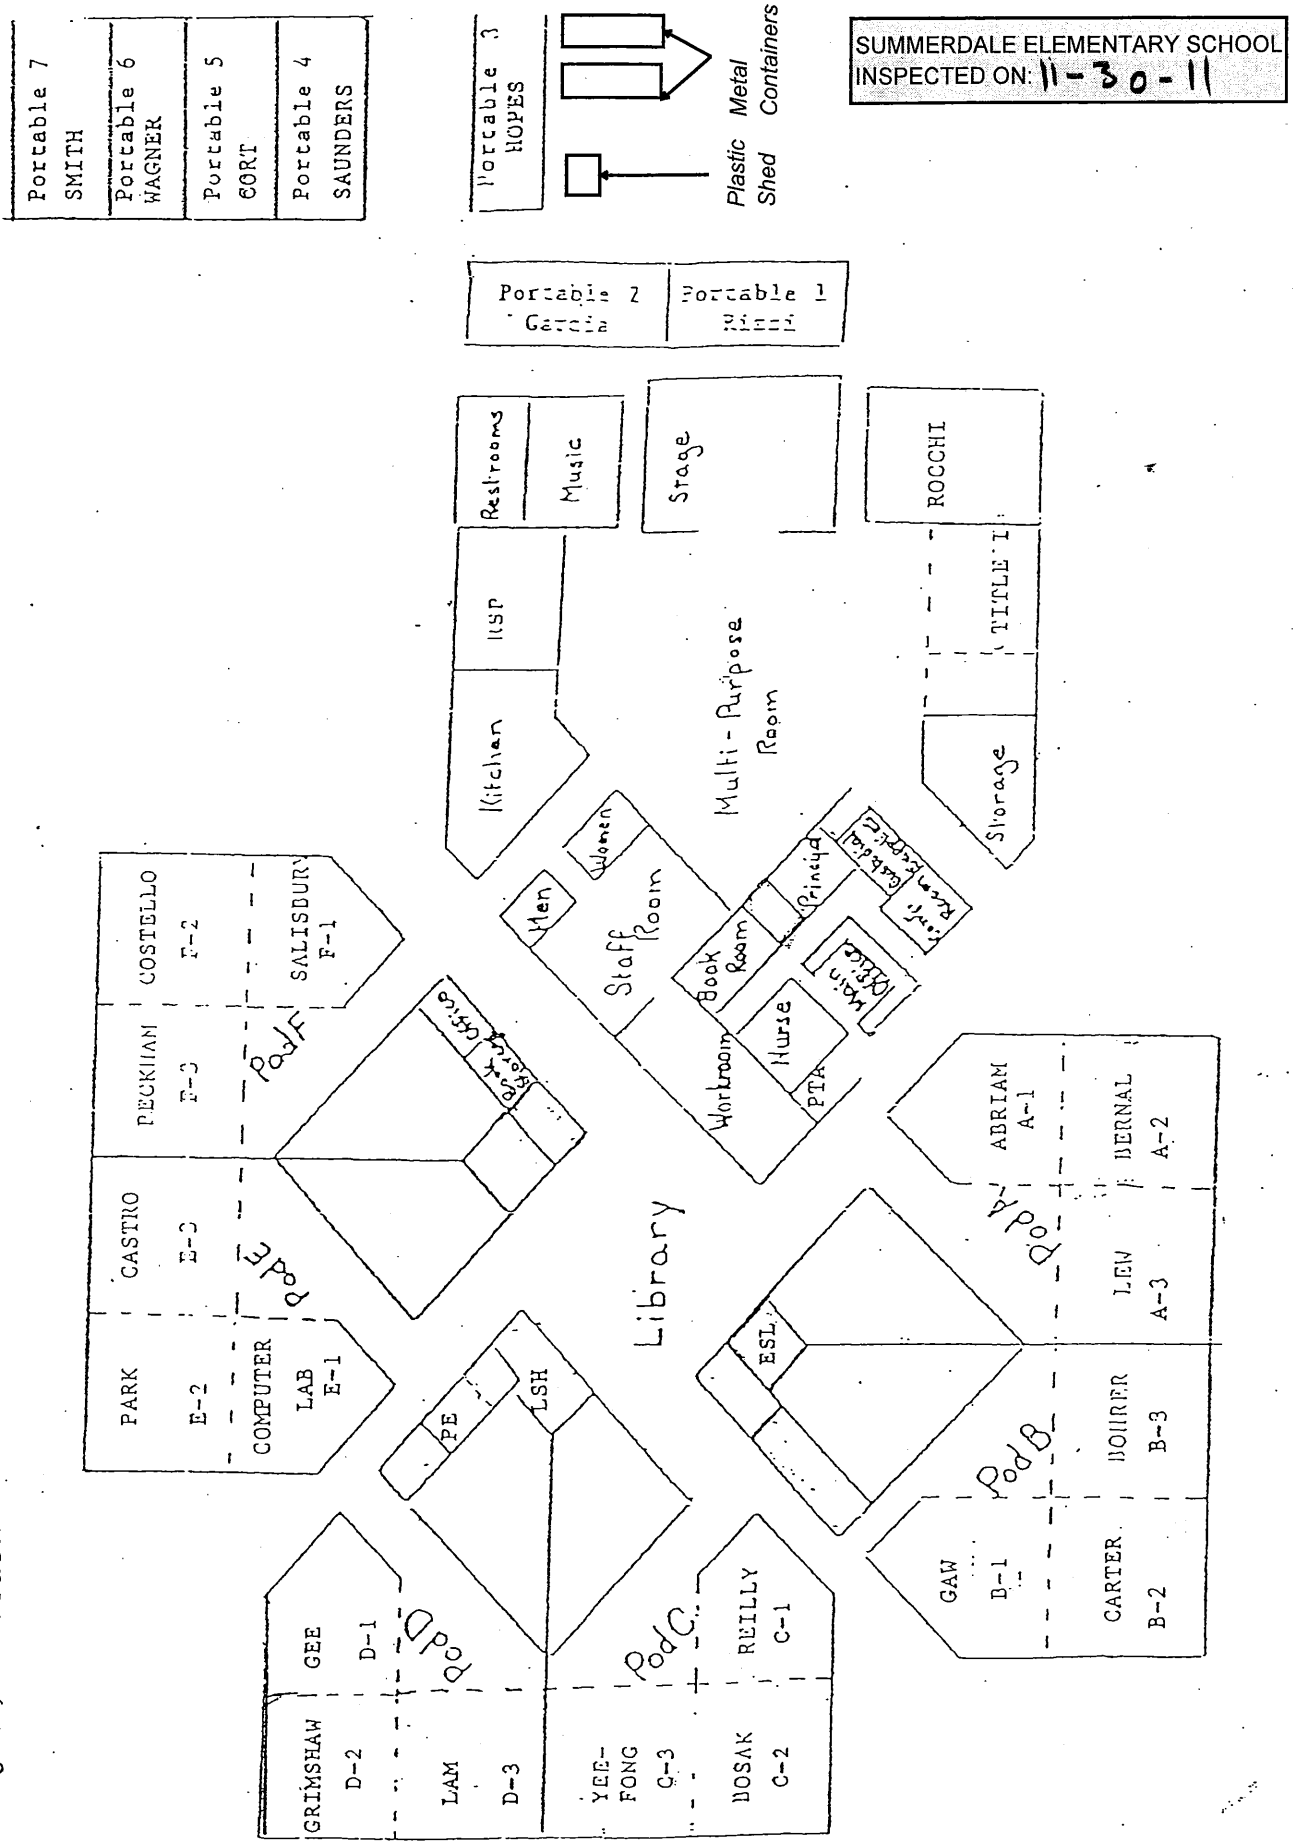

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 11-30-11

Summerdale School

1100 Summerdale Drive


San Jose, CA 95132

P. 1

408-261-1183

Rob LaPore

Nov 14 06 08:49a

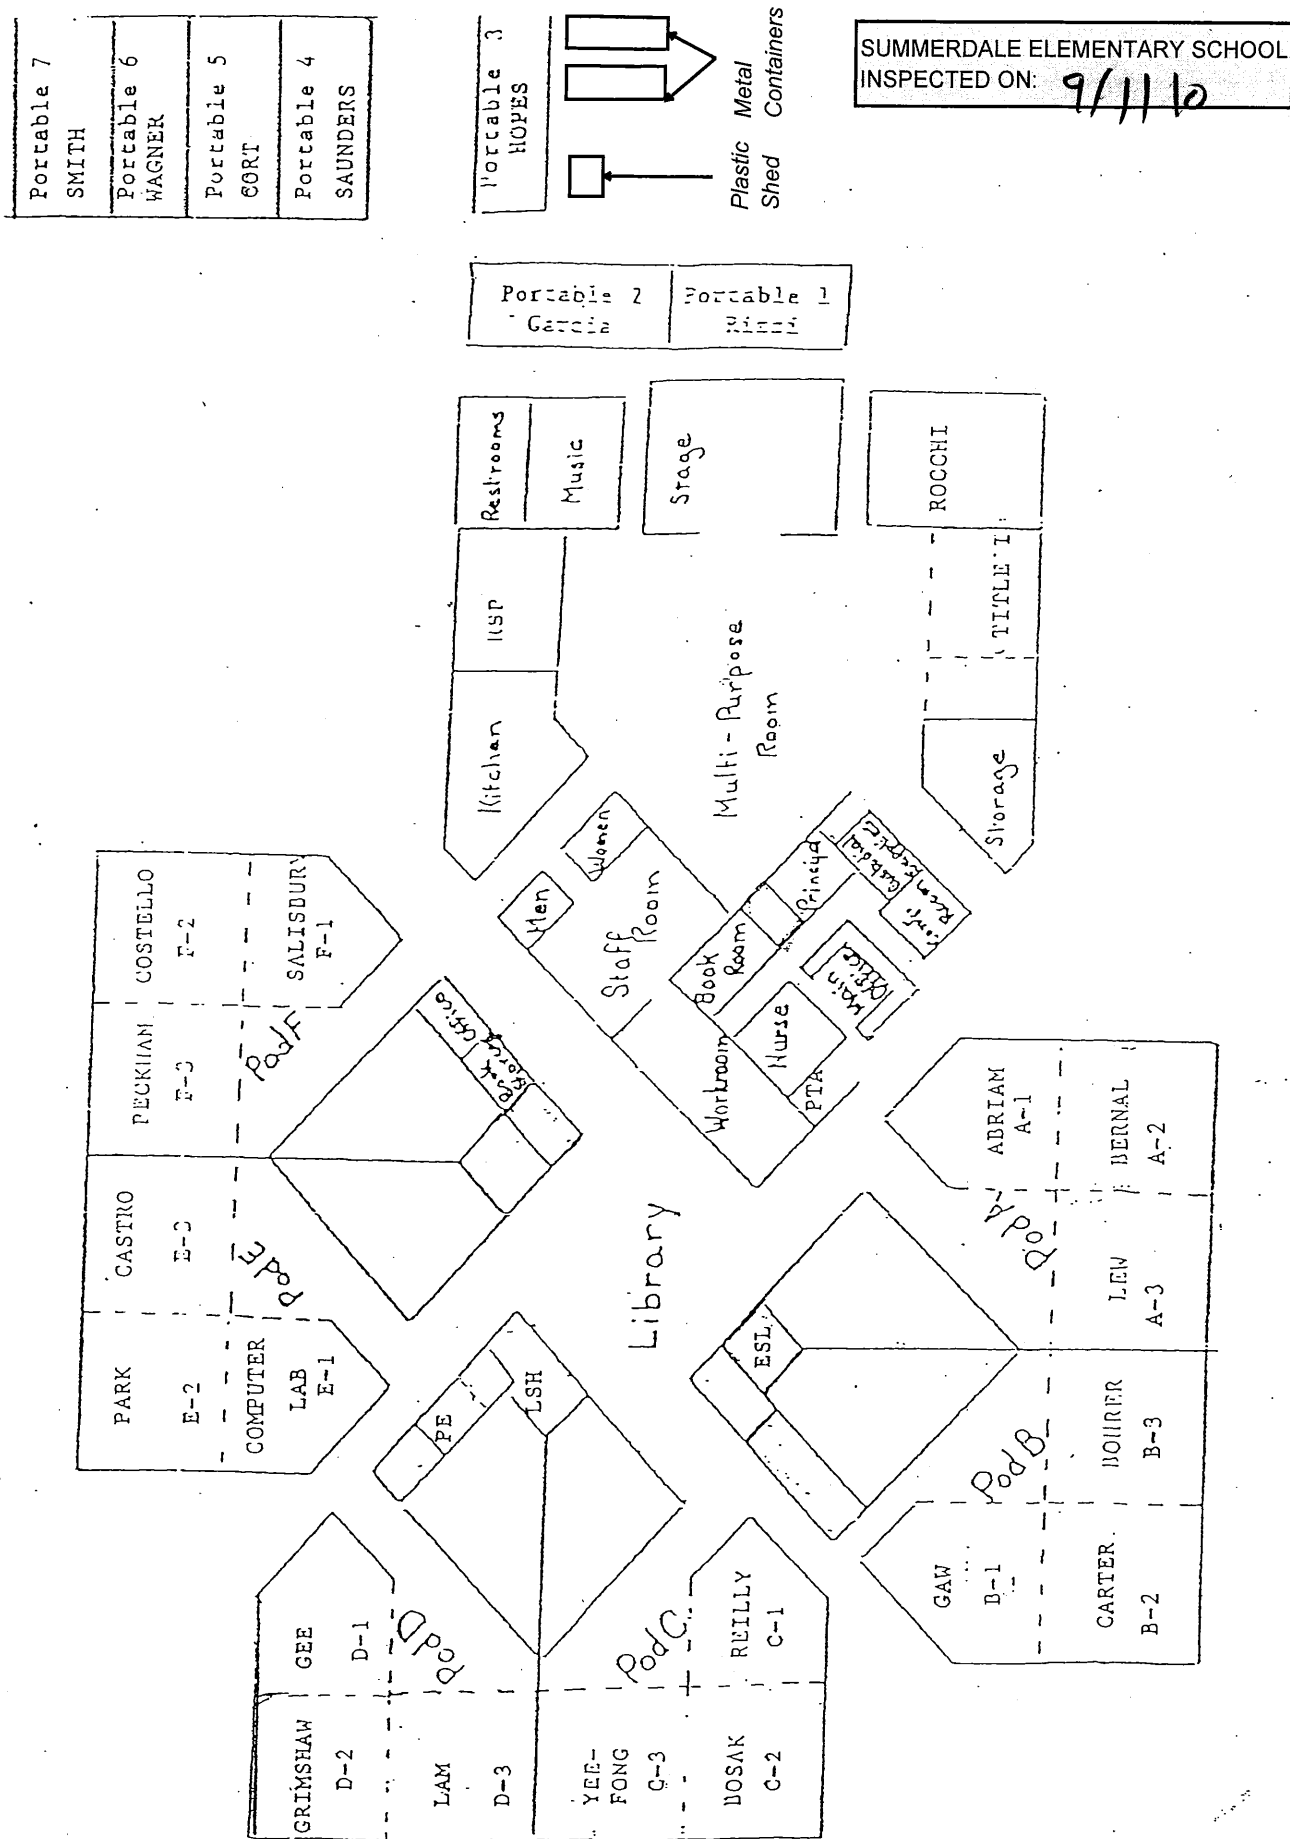

9/1/10

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 9/1/10


Summerdale School

1100 Summerdale Drive
San Jose, CA 95132


Portable 7
SMITH
Portable 6
WAGNER
Portable 5
GORT
Portable 4
SAUNDERS

Portable 3
HOPES

Portable 2
Garcia
Portable 1
Winters

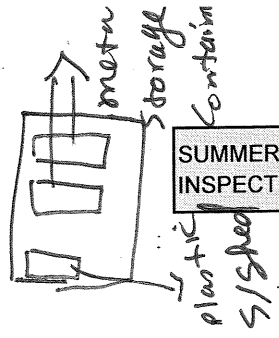

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 3/10/10

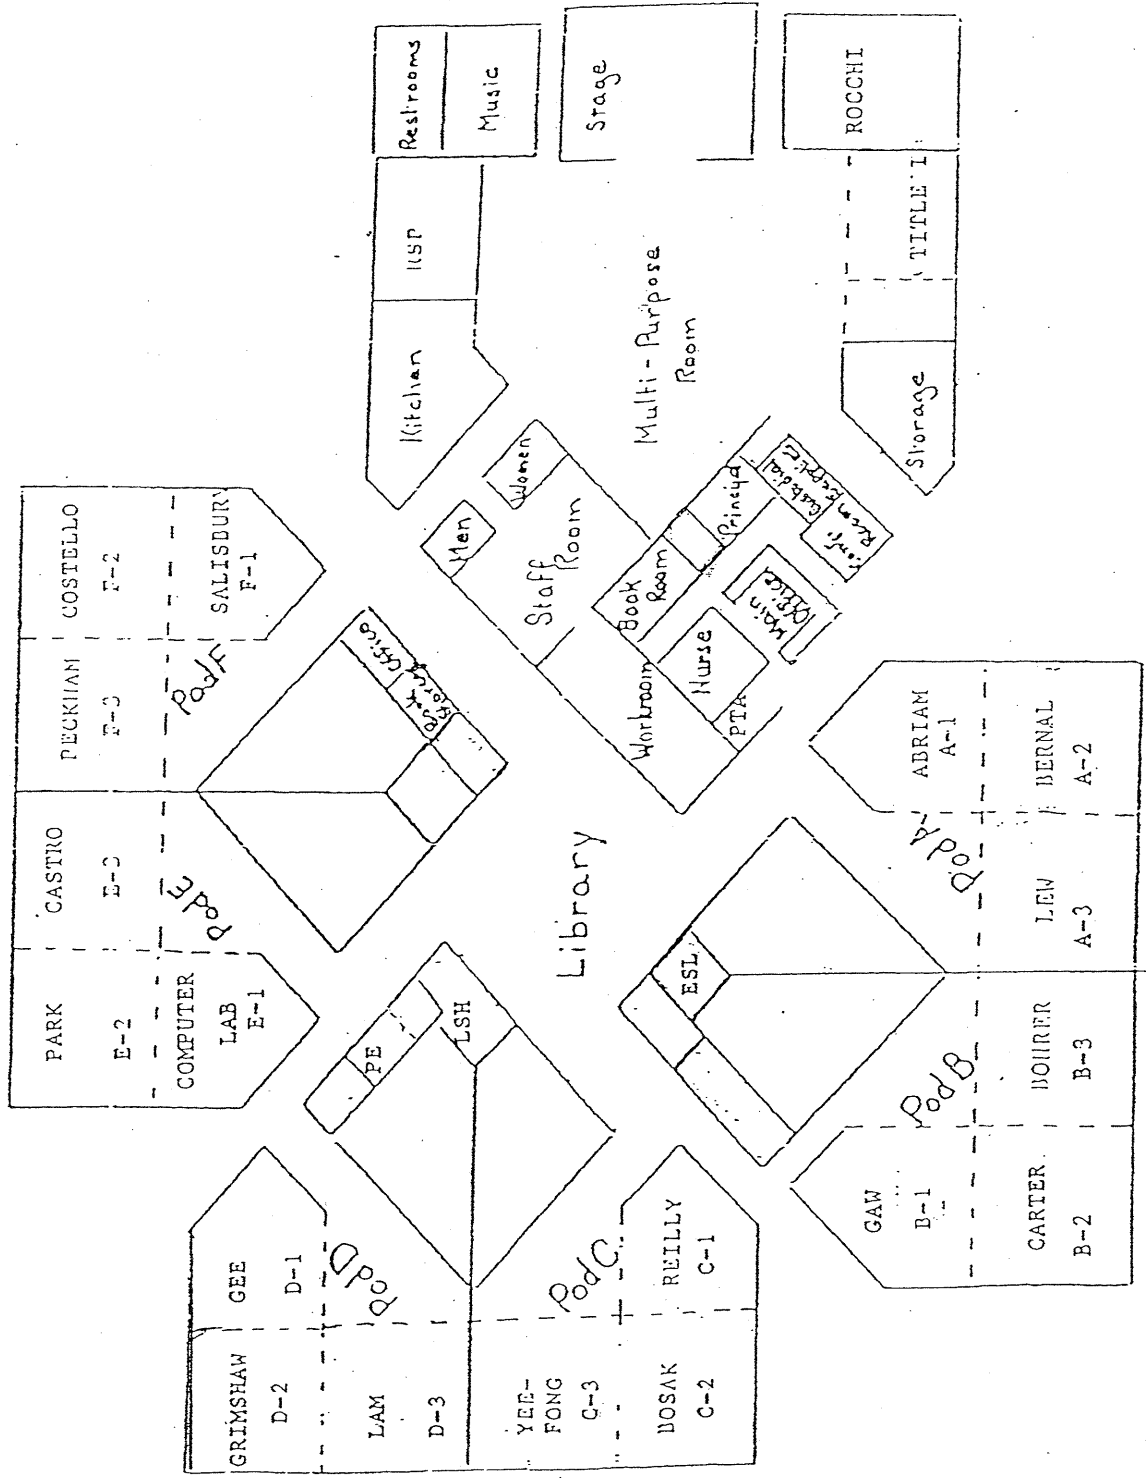

Summerdale School



1100 Summerdale Drive
San Jose, CA 95132

Portable 7
SMITH
Portable 6
WAGNER
Portable 5
CORT
Portable 4
SAUNDERS

Portable 3
HOPES

Portable 2
Garcia
Portable 1
Wynn

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 09-04-09

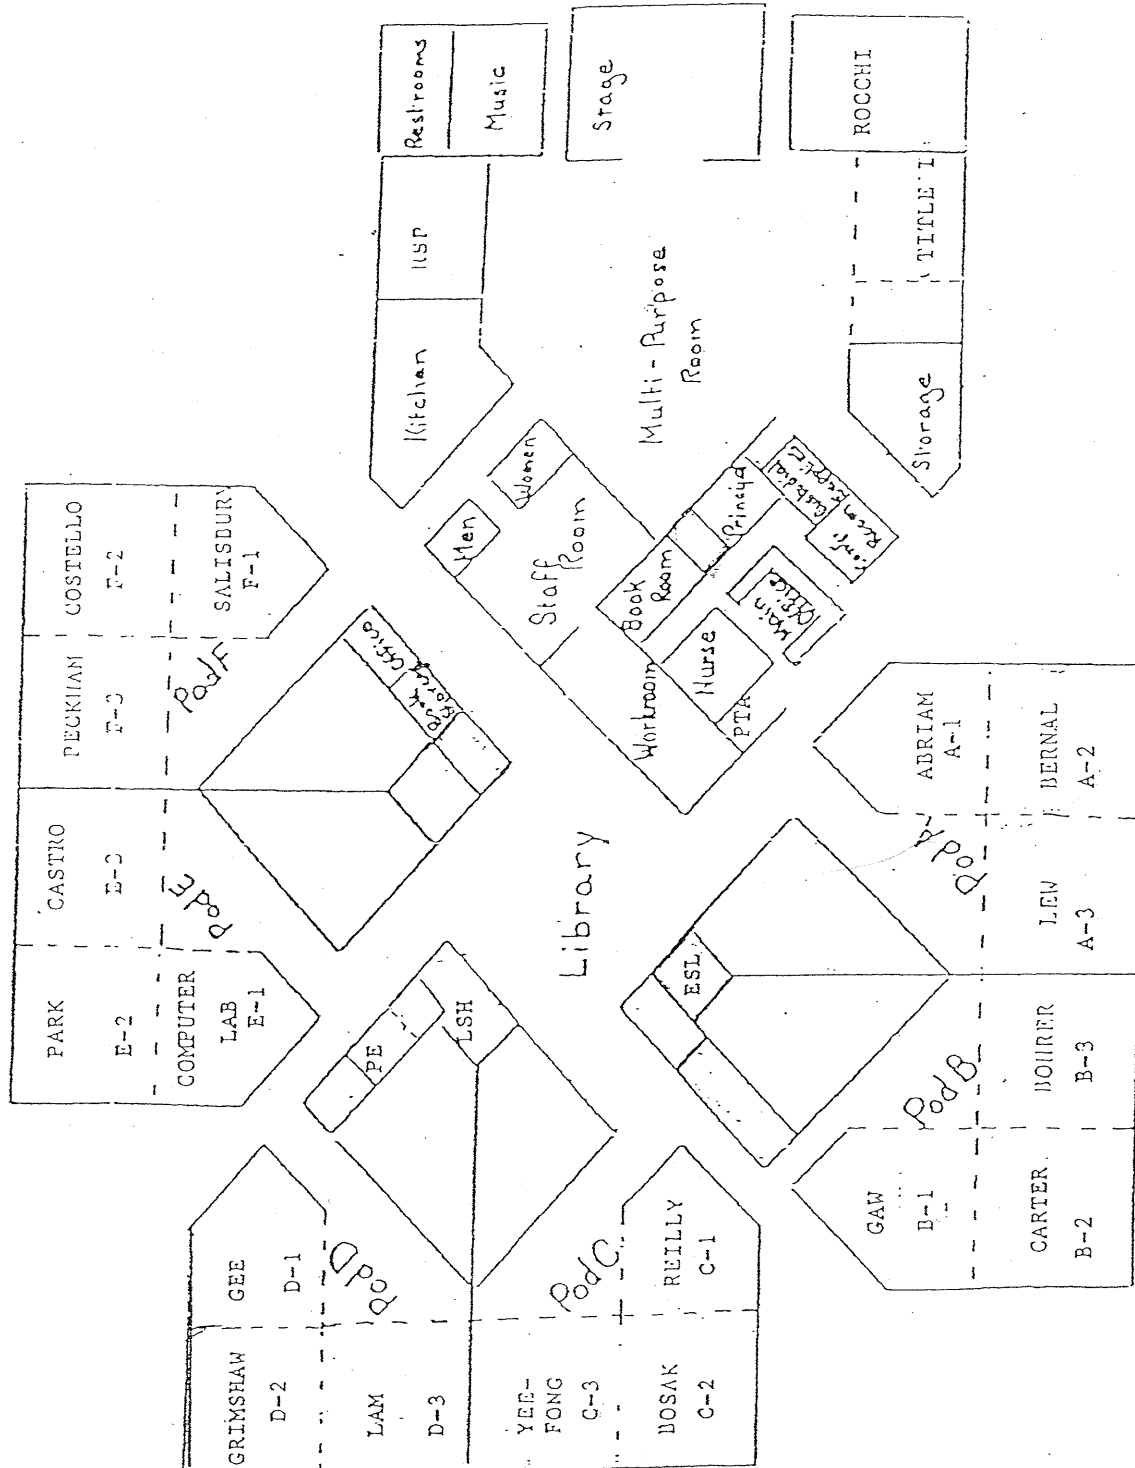

Summerdale School

1100 Summerdale Drive

San Jose, CA 95132

P.1

408-261-1183


Rob LaPore

Nov 14 06 08:49a

Portable 7
SMITH
Portable 6
WAGNER
Portable 5
CORT
Portable 4
SAUNDERS

Portable 3
HOPES

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 5-13-08

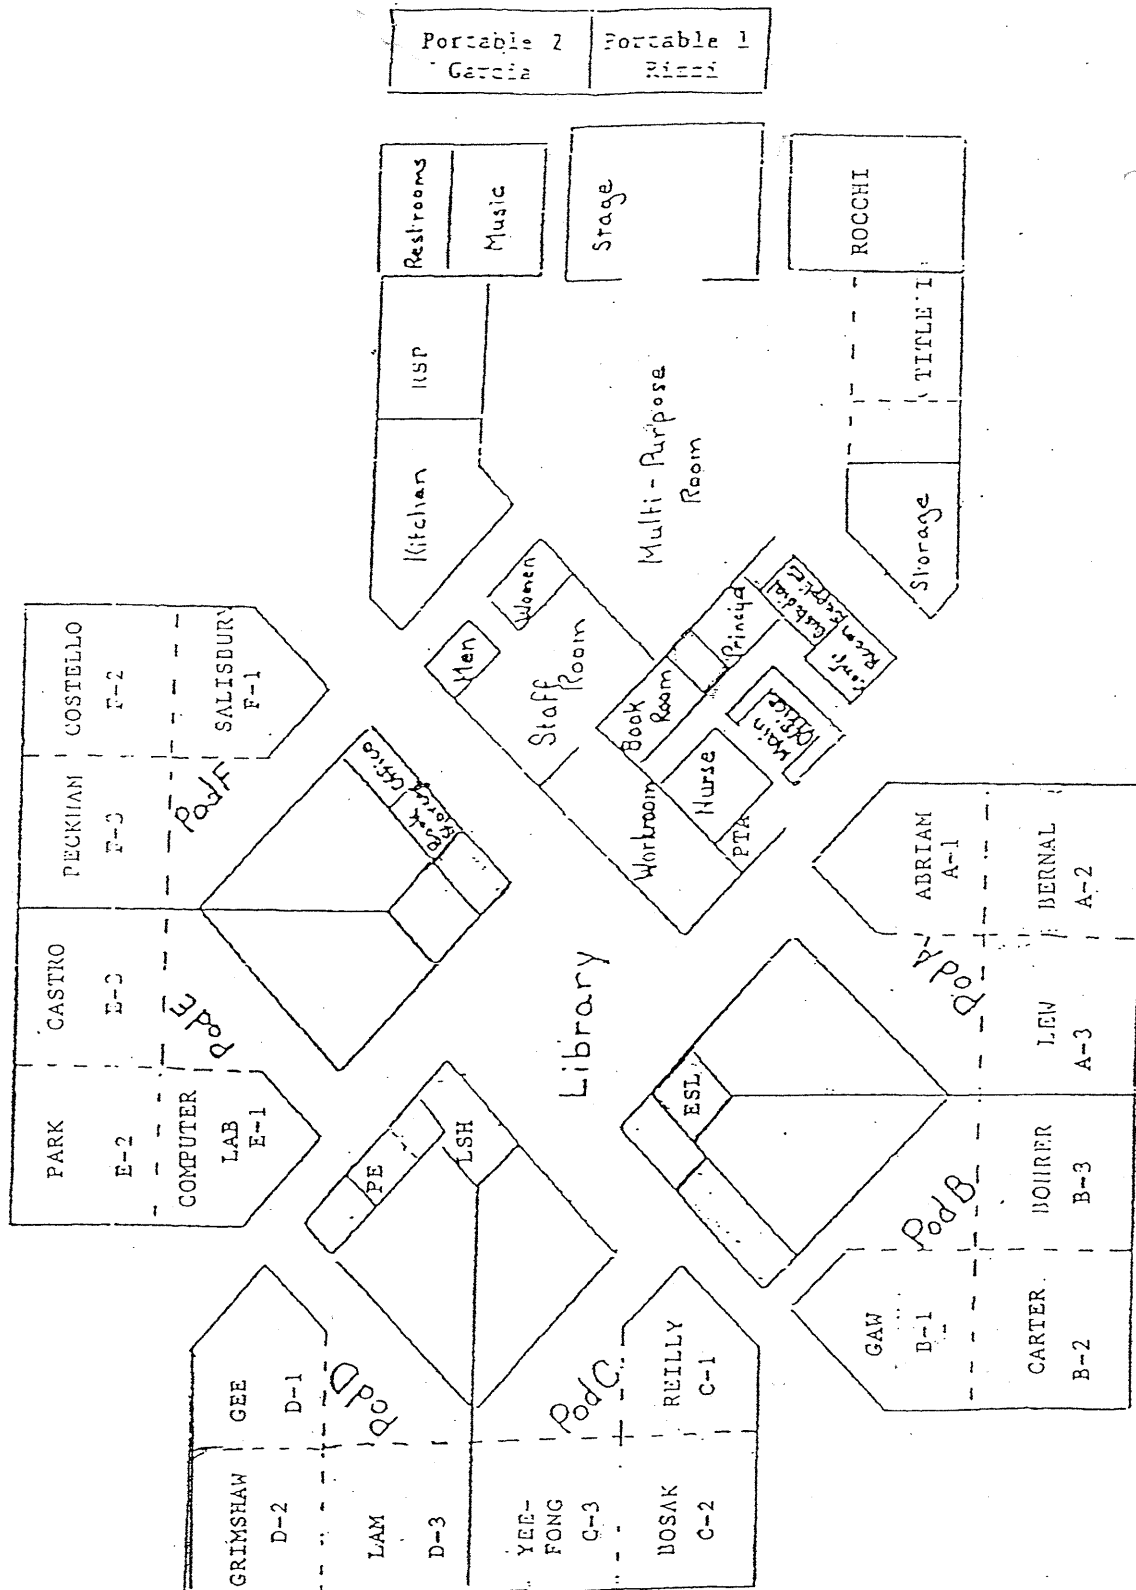

Summerdale School

1100 Summerdale Drive


San Jose, CA 95132

Portable 7
SMITH
Portable 6
WAGNER
Portable 5
CORT
Portable 4
SAUNDERS


Portable 3
HOPES

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 6/15/08

Portable 2
GARCIA
Portable 1
WILLIAMS

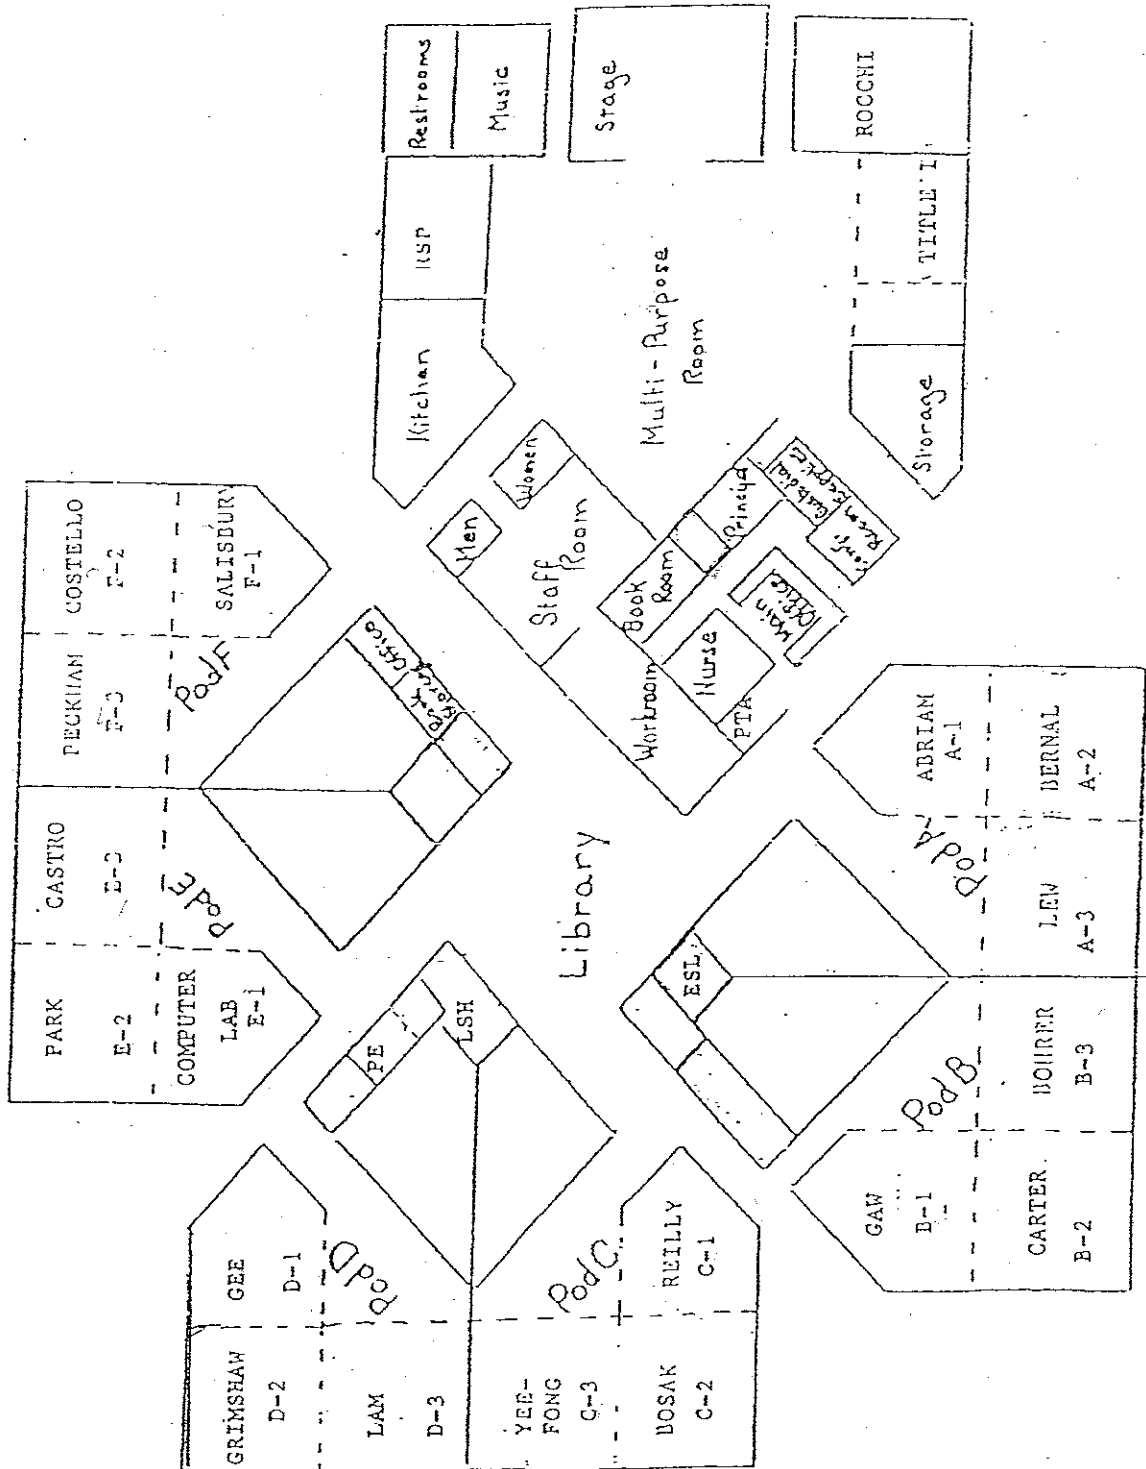

Summerdale School
 1100 Summerdale Drive
 San Jose, CA 95132

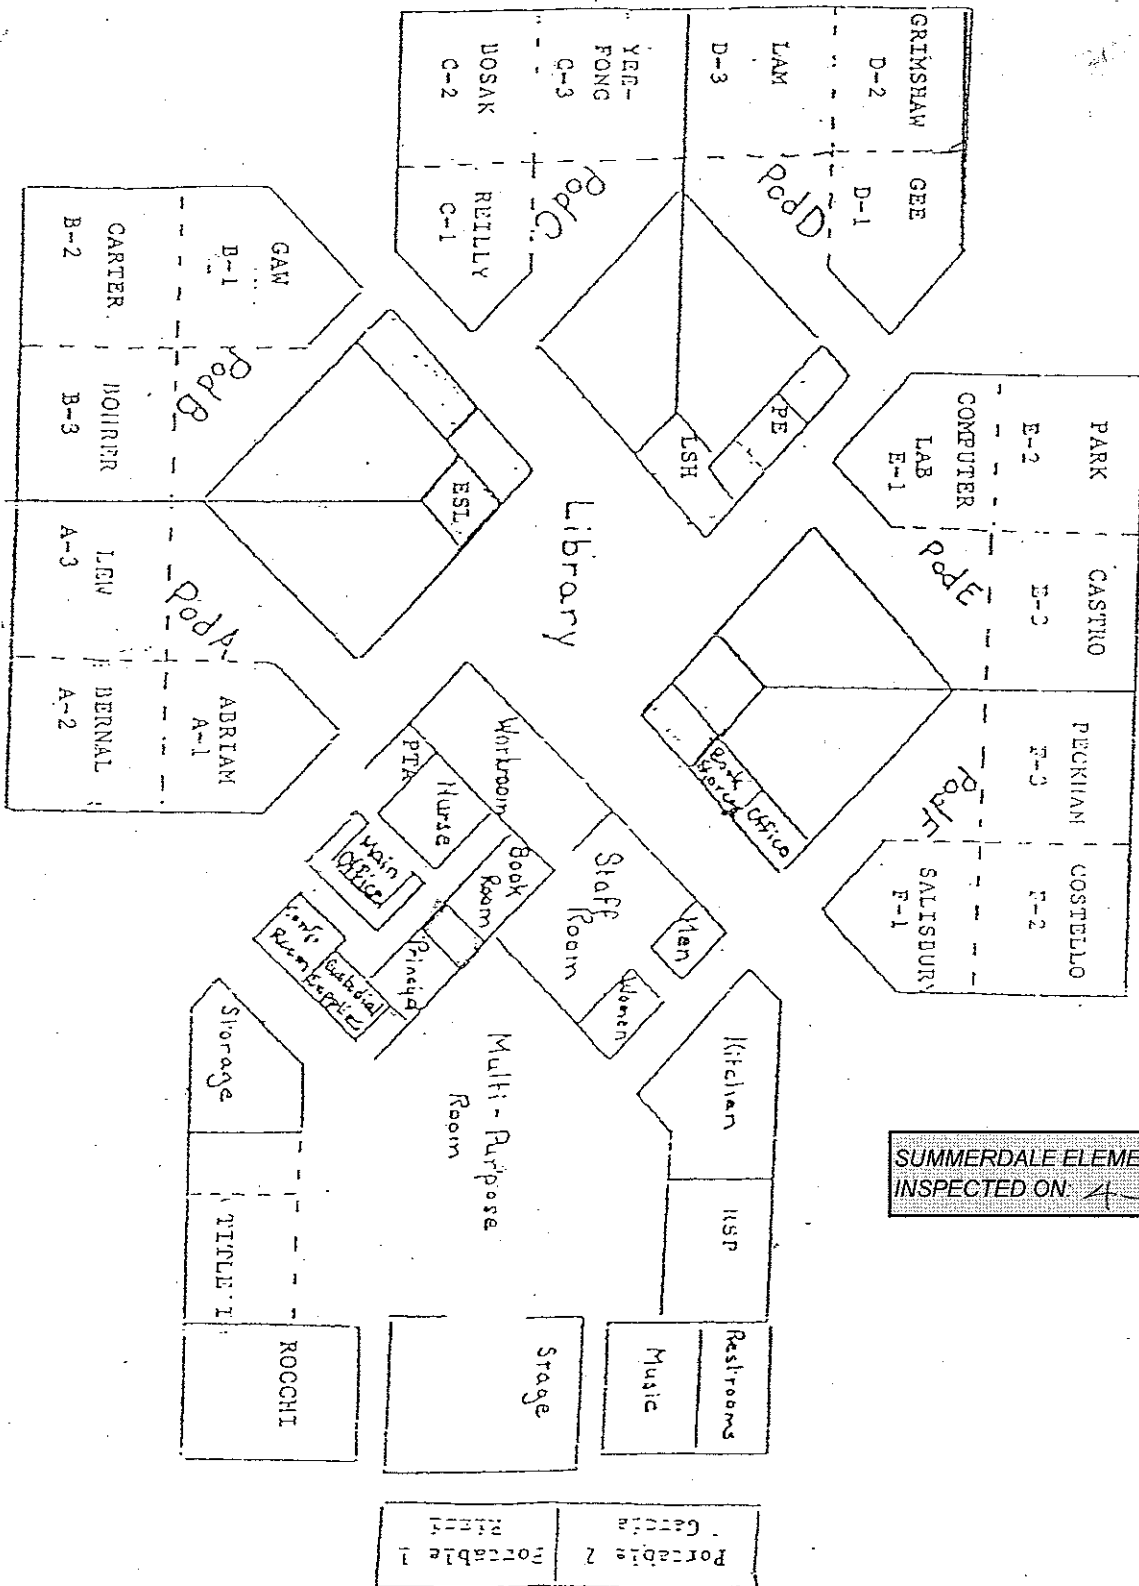


SUMMERDALE ELEMENTARY SCHOOL
 INSPECTED ON 4-16-08

Portable 7
SMITH
Portable 6
WAGNER
Portable 5
GORT
Portable 4
SAUNDERS


Portable 3
HOPES

Summerdale School 1100 Summerdale Drive San Jose, CA 95132

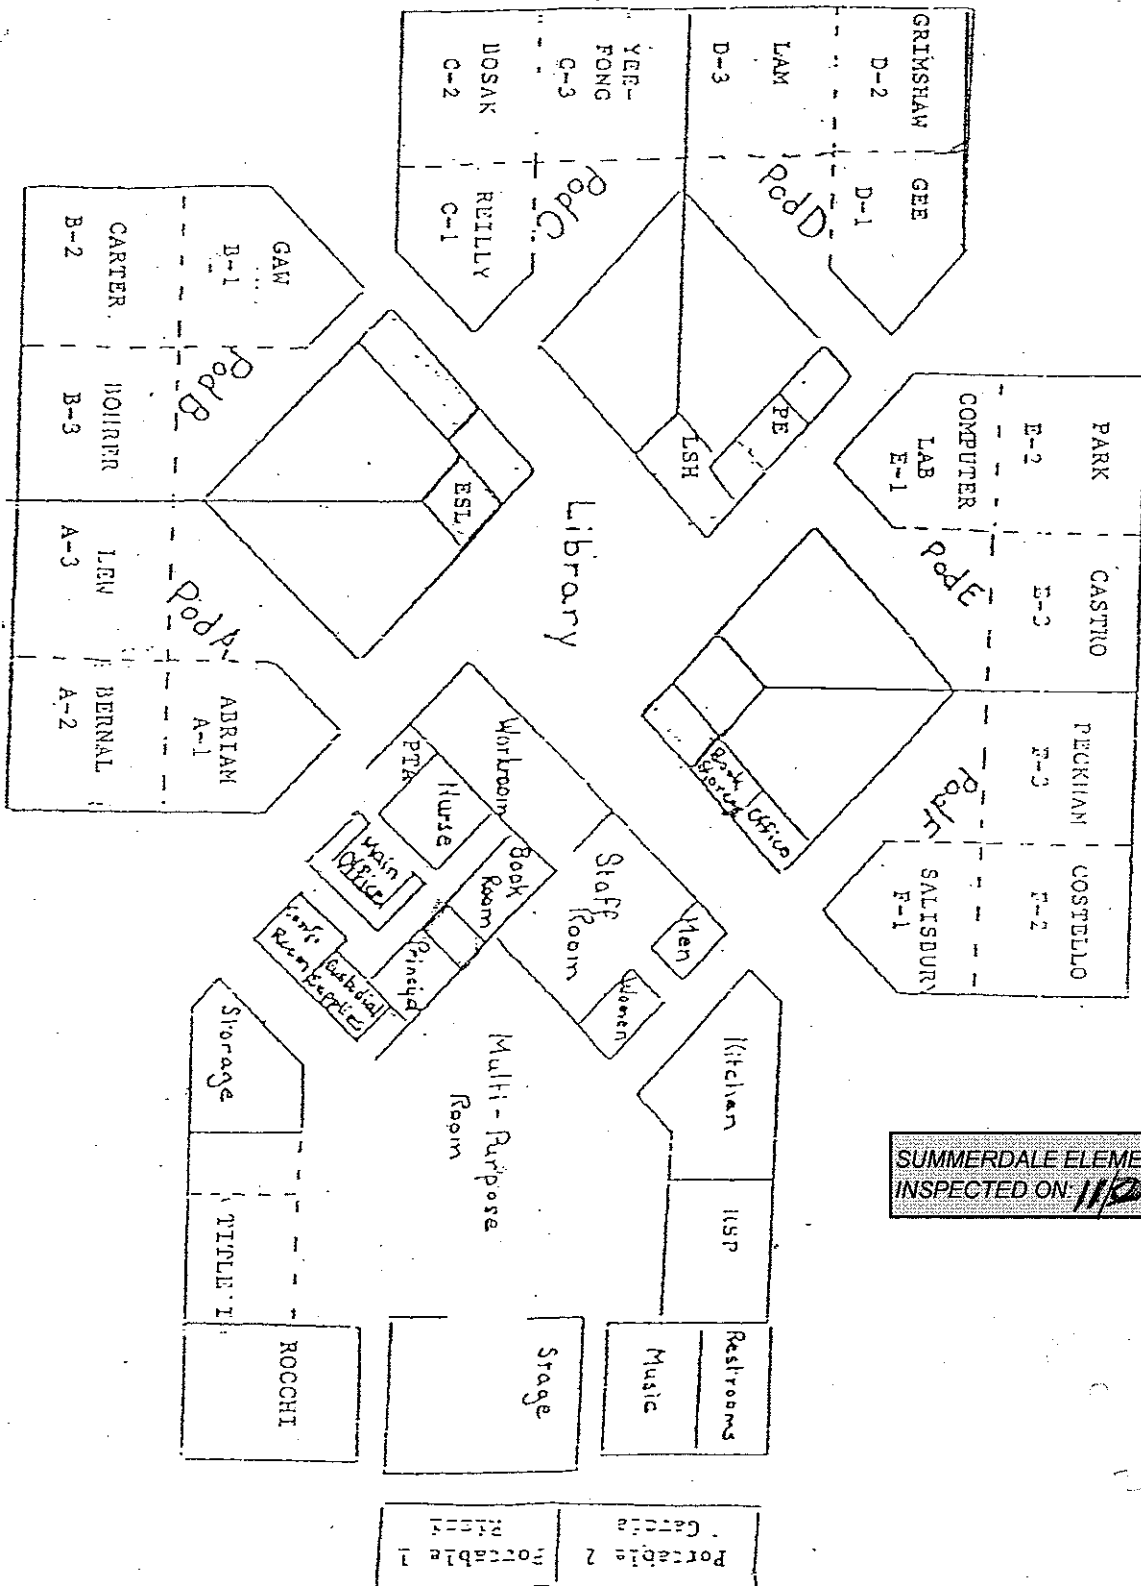

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON 11/25/07

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 03/05/07

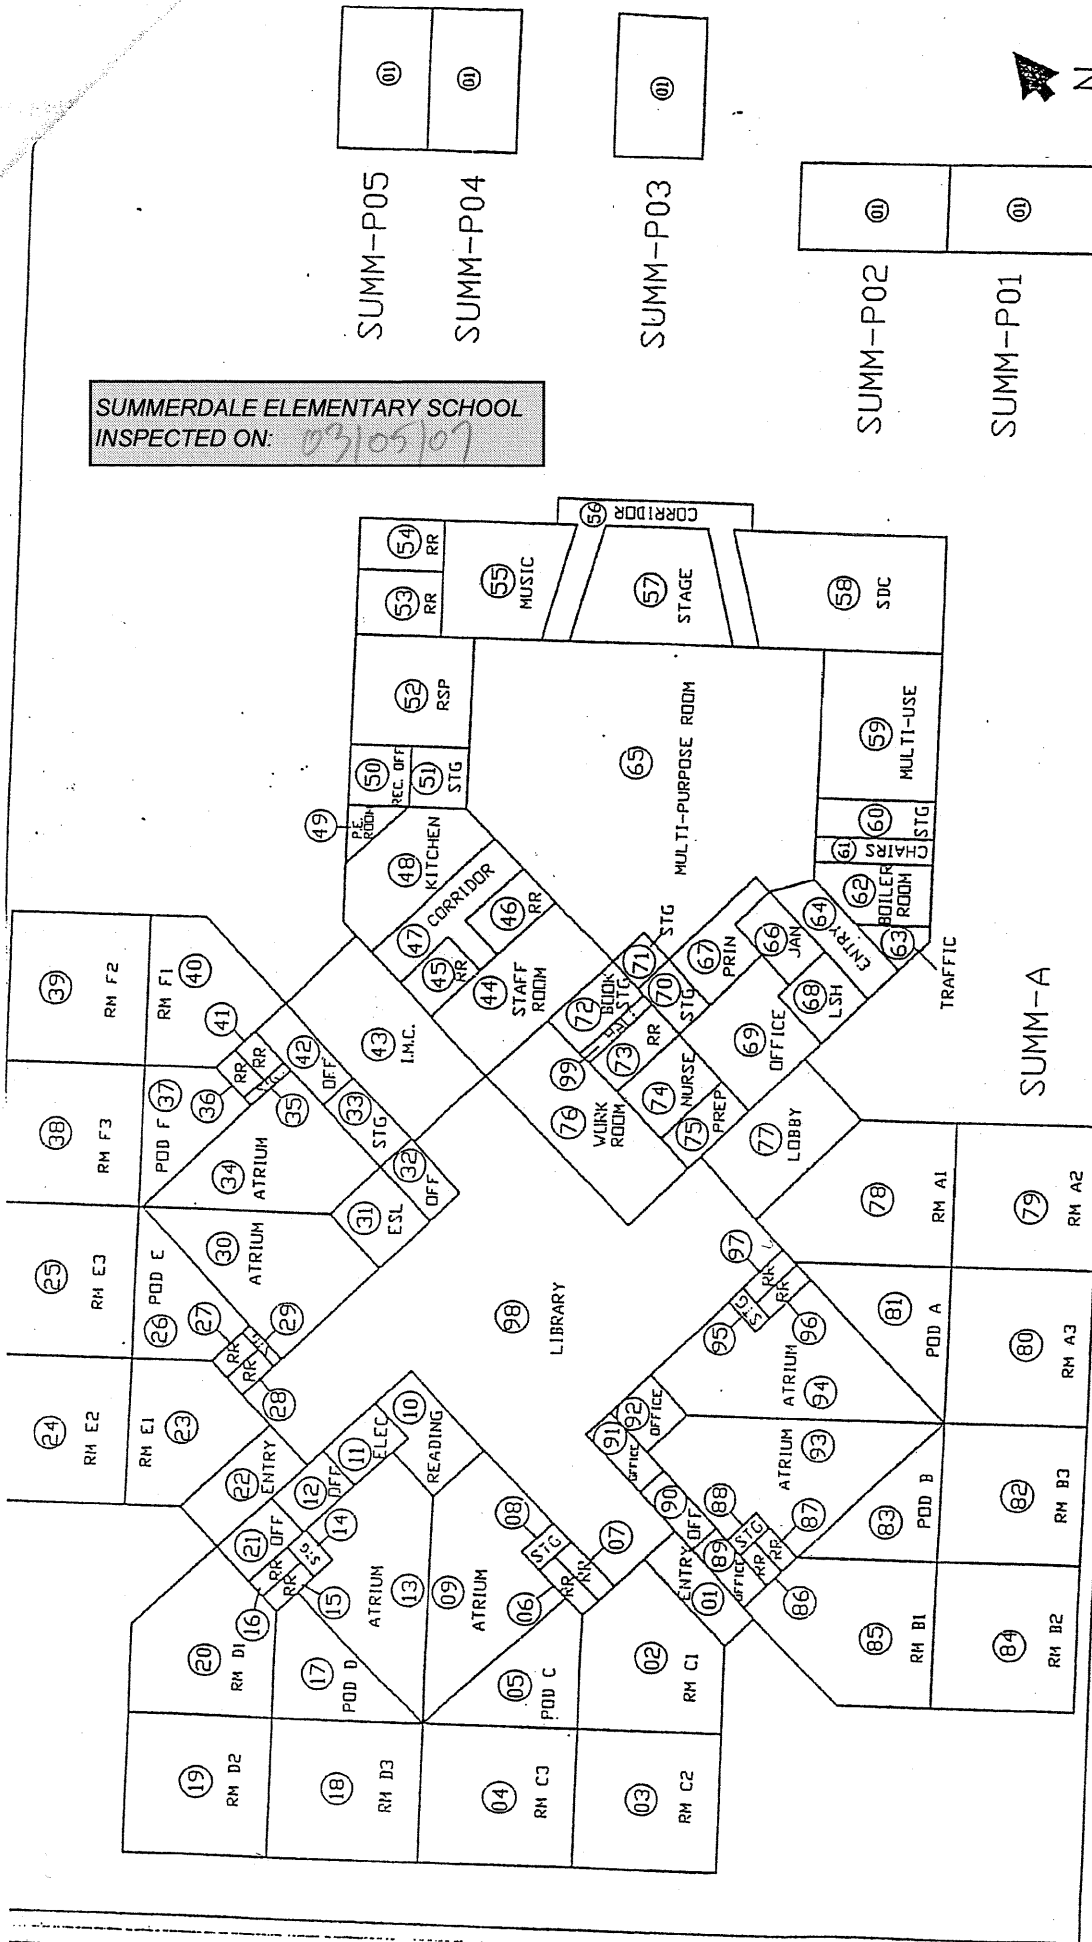

NOT TO SCALE




NAMING CONVENTION SITEPLAN

BERRYESSA UNIFIED
1376 PIEDMONT RD
SAN JOSE, CA 95122


SCHOOL NAME: SUMMERDALE ELEMENTARY
ADDRESS: 1100 SUMMERDALE DR.
SCHOOL DISTRICT: BERRYESSA UNIFIED

COUNTY: SANTA CLARA
ACREAGE: N/A
REV. DATE: 01/25/99

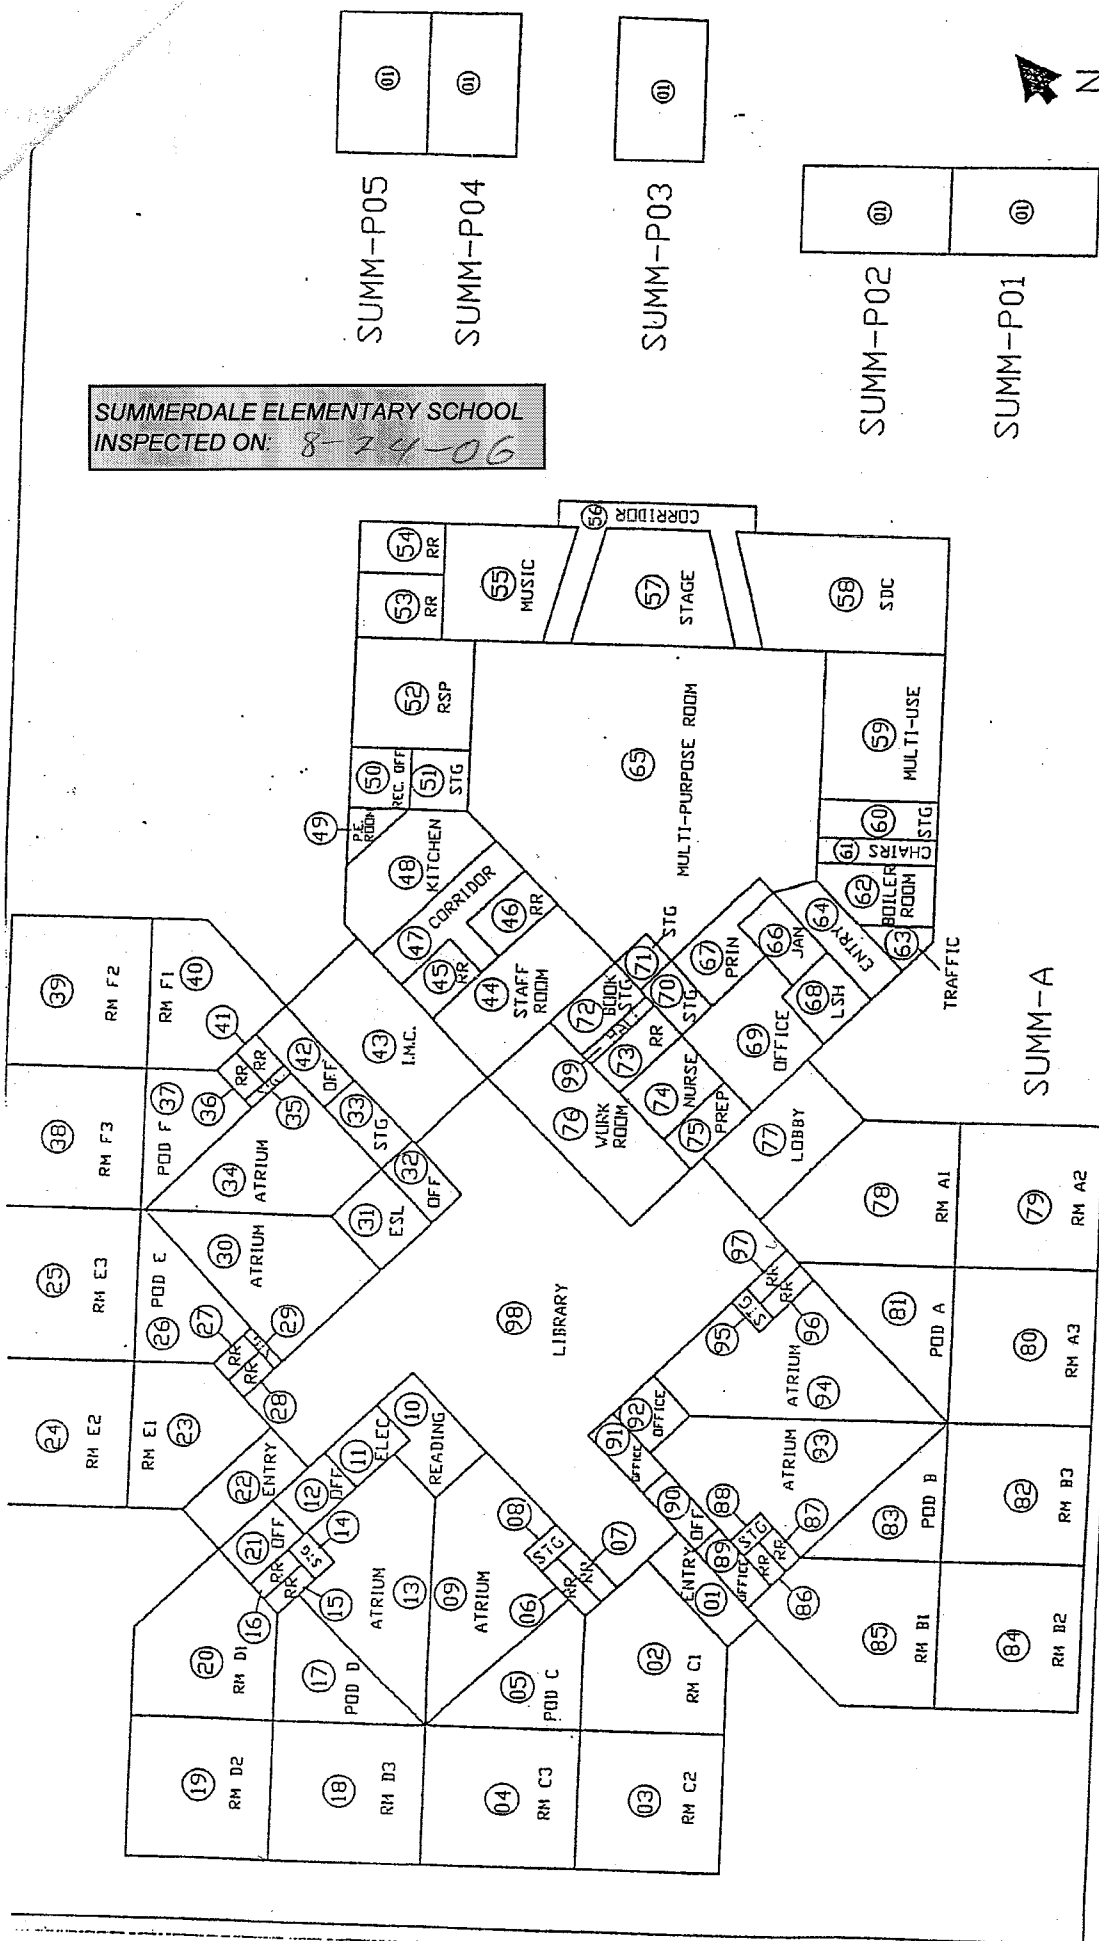

SCHOOL NAME: SUMMERDALE ELEMENTARY ADDRESS: 1100 SUMMERDALE DR. SCHOOL DISTRICT: BERRYESSA UNIFIED	COUNTY: SANTA CLARA ACREAGE: N/A REV. DATE: 01/25/99	NAMING CONVENTION SITEPLAN	BERRYESSA UNIFIED 1376 PIEDMONT RD SAN JOSE, CA 95132
--	--	----------------------------	---

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED ON: 04/19/06

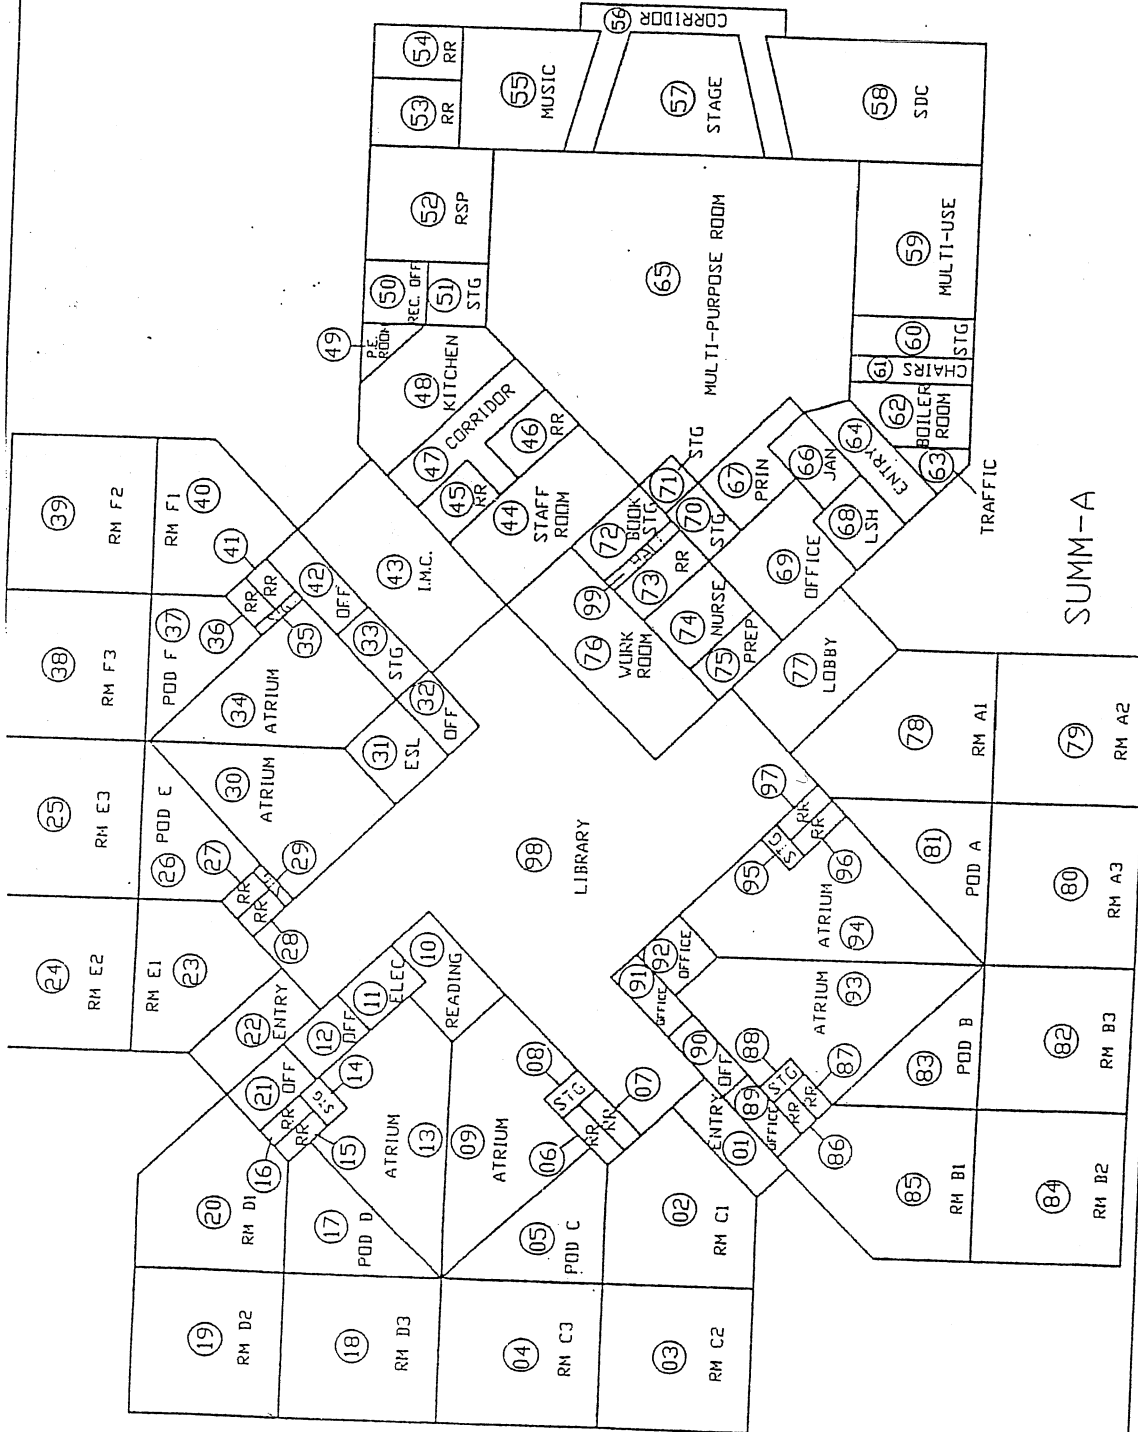

SUMM-P05
SUMM-P04

SUMM-P03

SUMM-P02
SUMM-P01



NOT TO SCALE


NAMING CONVENTION SITEPLAN

BERRYESSA UNIFIED
1376 PIEDMONT RD
SAN JOSE, CA 95132

SCHOOL NAME: SUMMERDALE ELEMENTARY
ADDRESS: 1100 SUMMERDALE DR.
SCHOOL DISTRICT: BERRYESSA UNIFIED

COUNTY: SANTA CLARA
ACREAGE: N/A
REV. DATE: 01/25/99

SUMMERDALE ELEMENTARY SCHOOL
INSPECTED SEPTEMBER 2005

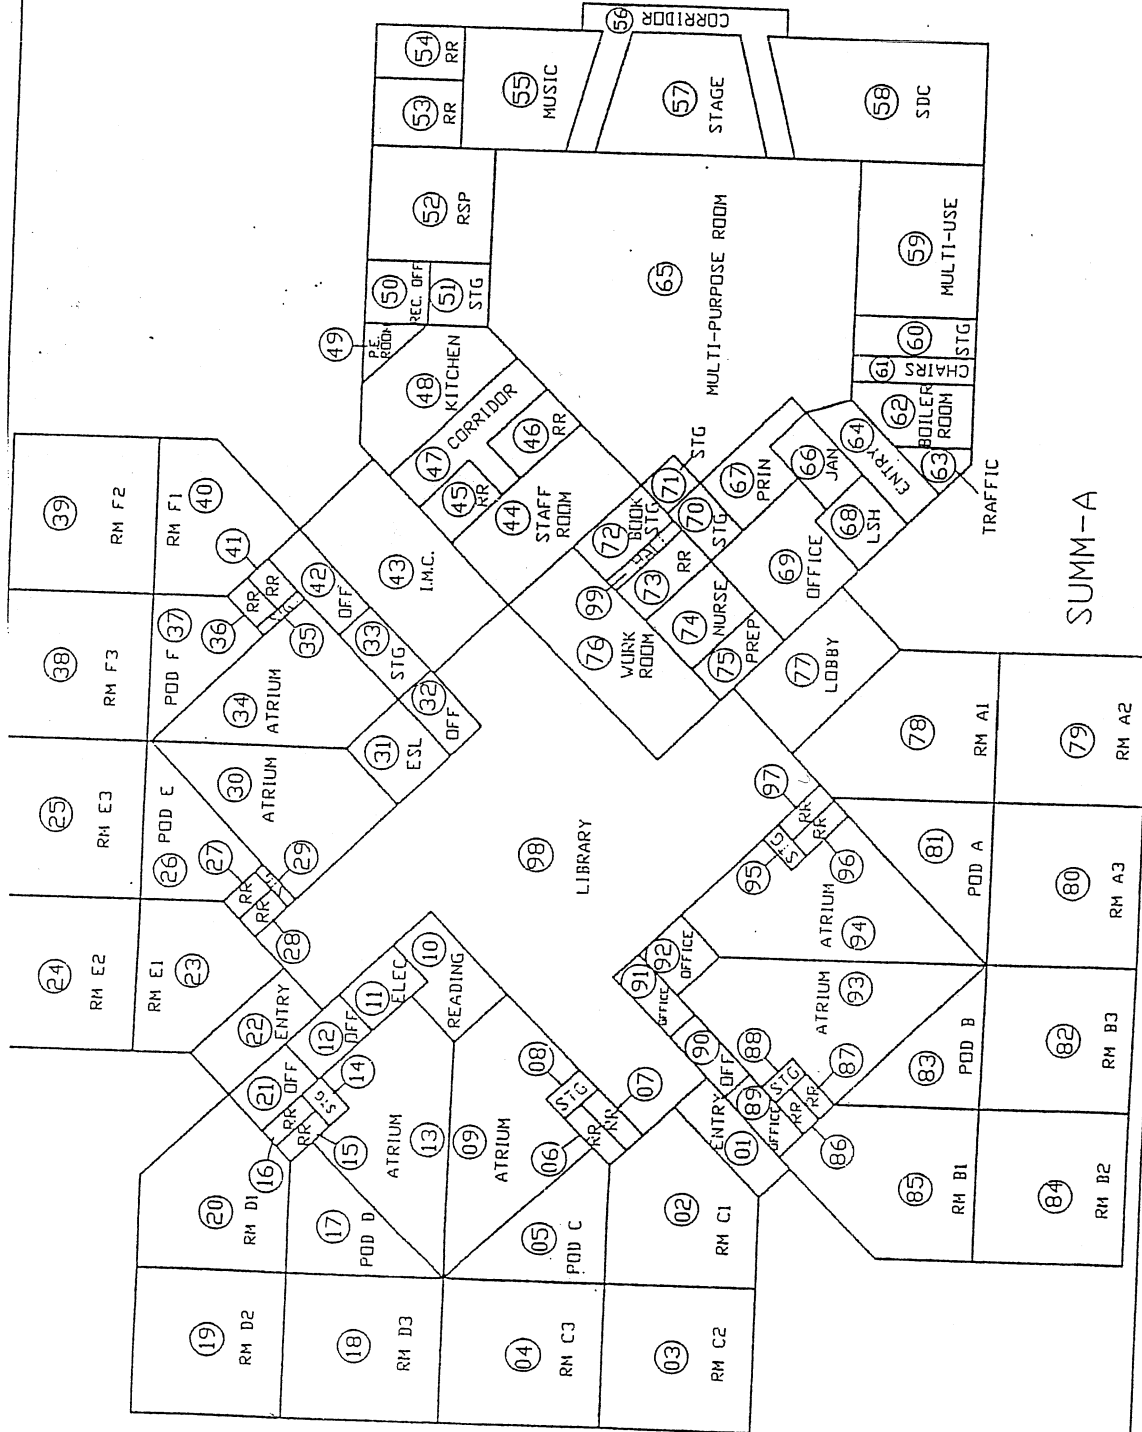

SUMM-P05
SUMM-P04

SUMM-P03

SUMM-P02
SUMM-P01



NOT TO SCALE

NAMING CONVENTION SITEPLAN

BERRYESSA UNIFIED
1376 PIEDMONT RD
SAN JOSE, CA 95132

SCHOOL NAME: SUMMERDALE ELEMENTARY
ADDRESS: 1100 SUMMERDALE DR.
SCHOOL DISTRICT: BERRYESSA UNIFIED

COUNTY: SANTA CLARA
ACREAGE: N/A
REV. DATE: 01/25/99
